# O'Hare Terminal 3 Improvements

COT3 Non-Mandatory Pre-Bid Conference Meeting & Meet The Primes Event







# This presentation and a copy of the sign-in sheet will be published to <a href="https://www.cot3.com">www.cot3.com</a>

If you are attending virtually, please type your name, company name, email address and phone # in the chat

NOTICE: NOTHING DISCUSSED TODAY IS INTENDED TO ALTER THE BID DOCUMENTS. ALL CLARIFICATIONS MUST BE SUBMITTED THROUGH THE REQUEST FOR INFORMATION (RFI) PROCESS FOR PROPER REVIEW AND RESPONSE.

IN CASE OF CONFLICTS BETWEEN TODAY'S DISCUSSIONS AND THE BID INFORMATION, BIDDERS SHOULD SUBMIT A PRE-BID RFI FOR CLARIFICATION AND GUIDANCE.

# Agenda

- Introductions
- II. Project Overview
- III. Trade Packages
- IV. Compliance
- V. Contract Administration
- VI. Safety
- VII. Quality
- VIII. Procurement
- IX. Conclusion & Next Steps
- X. Meet the Primes / Potential Prime Contractors

#### Main points:

- Return all documents needed with bid (reference the checklist)
- Be on the lookout for Addendums
- Complete the bid form in its entirety
- Bid the full scope of work, without exception
- Account for all Logisitics, DBE and Workforce requirements





### INTRODUCTIONS

- OWNER: Chicago Department of Aviation (CDA)
- PROGRAM MANAGER: Connect Chicago Alliance (CCA)
- CONSTRUCTION MANAGER AT RISK (CMAR): Clark-W.E. O'Neil JV (COT3)
  - Partner Firms
    - Cotter Consulting, Inc.
    - McKissack & McKissack Midwest, Inc.







### PROJECT OVERVIEW - SCOPE OF WORK

- Expansion of the Departures and Arrivals levels to create room for a new outbound baggage makeup area, additional hold-room space and a new American Airlines Club space
- Demolition of an existing bag claim area and construction of a new inbound bag claim area
- Reconfiguration of the TSA checkpoints
- Reconfiguration of vertical transportation (elevators and escalators)
- Renovation of the existing restrooms
- Demolition and reconfiguration of existing airport/airline support spaces
- Roof replacement of Terminal 3



# PROJECT OVERVIEW - T3 IMPROVEMENTS & SUPPLEMENTAL BAGROOM - SCHEDULE & LIQUIDATED DAMAGES

#### **NOTICE TO PROCEED:**

ANTICIPATED 4/26/24

#### **SUBSTANTIAL COMPLETION:**

2/10/27

REFER TO PUBLISHED SCHEDULE FOR MORE DETAIL

### SECTION 4 TIME OF COMPLETION/LIQUIDATED DAMAGES/WEATHER AND MORATORIUM DAYS TABLE

NO.	MILESTONE	MILESTONE DATE	AMOUNT OF LIQUIDATED DAMAGES		
1.	AA Club Shell ready for tenant fit out by others (Schedule activity CDA-1010, UL - AA Club TI Start)	4-Mar-25	\$5,000 per calendar day		
2.	Gate K1 including partial hold-room fit out (Schedule activity CS-AA-1990, Complete Gate Opening Checklist for K1 – Hold Rooms & AA Club)	22-Aug-25	\$5,000 per calendar day		
3.	Gate L2A including partial hold-room fit out (Schedule activity CS-AA-2010, Complete Gate Opening Checklist for L2A- Hold Rooms & AA club)	22-Aug-25	\$5,000 per calendar day		
4.	Concession shell ready for tenant fit out (Schedule activity IA-UL-2G.A1360, Final Acceptance and Turnover – Airline Ops & Commercial)	17-Sep-25	\$5,000 per calendar day		
5.	Substantial Completion (Schedule activity Mile-110, Substantial Completion)	10-Feb-27	\$3,000 per calendar day		

### PROJECT OVERVIEW – T3 IMPROVEMENTS & SUPPLEMENTAL BAGROOM - PRELIMINARY AIRSIDE LOGISTICS





#### O'Hare T3 Improvements

Airside Access - Trucking, Equipment Mobilization, & Deliveries

- 1. T3 Area of Work
- 2. Construction Vehicle Inspection Area #5 (CVIA 5) - Gate Access to Airside

#### Legend

- --- Airside
- Landside
- Active Taxiway



### PROJECT OVERVIEW -PRELIMINARY AIRSIDE LOGISTICS


Airside Access – Trucking, Equipment Mobilization, & Deliveries

#### Keynotes

- Primary Vehicular Access via Construction Vehicle Inspection Area #5 (CVIA 5) – Gate Access to Airside.
- During full duration of expansion work: Stabilized construction entrance w/ trackout control (synthetic/movable). Full-time tire wash by trades. Full-time sweeper by trades.
- During full duration of expansion work: Full time dedicated flaggers required by trades

#### Legend

- Construction Vehicular Traffic
- Construction Foot Traffic
- Guard Post

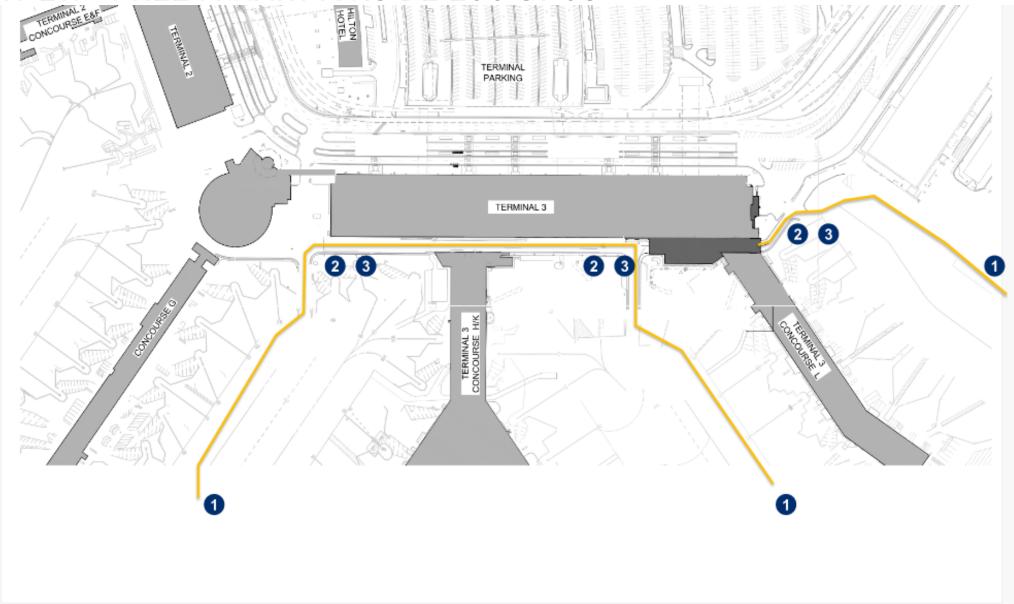

### PROJECT OVERVIEW -PRELIMINARY AIRSIDE LOGISTICS


Airside Access – Trade Access On Foot

#### Keynotes

- Airside trade access on foot through existing Guard Post #8 & #10
- 2. Guard Post #8
- 3. Guard Post #10

#### Legend

- Construction Vehicular Traffic
- Construction Foot Traffic
- Guard Post

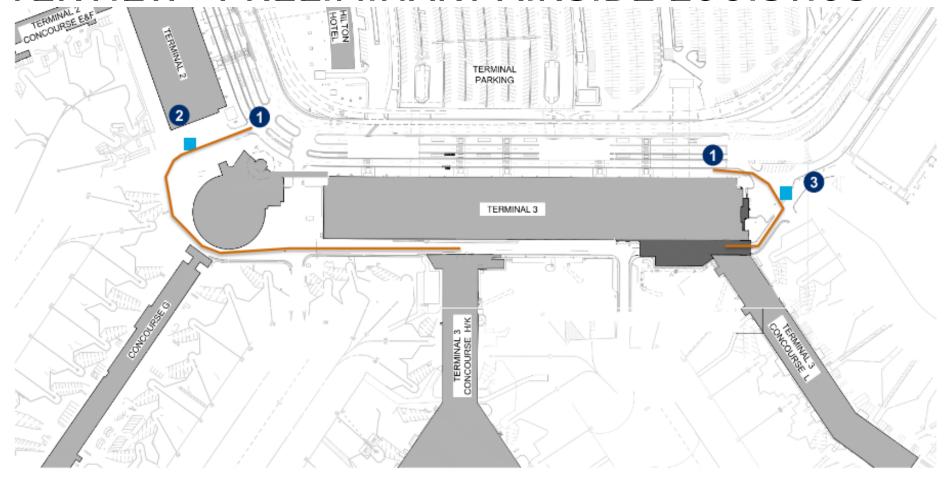


### PROJECT OVERVIEW -PRELIMINARY LANDSIDE LOGISTICS

Landside Access – Trucking, Equipment Mobilization, & Deliveries (NIGHT WORK)

#### Keynotes

- Primary Vehicular Access for Landside Construction
- Landside Construction Deliveries As Req'd to Service Work Areas. Schedule According to Area "Work Rules"
- Full-time sweeper required by trades during expansion area construction at VSR & haul routes
- Full time dedicated flaggers required by trades during expansion construction at VSR & haul routes.

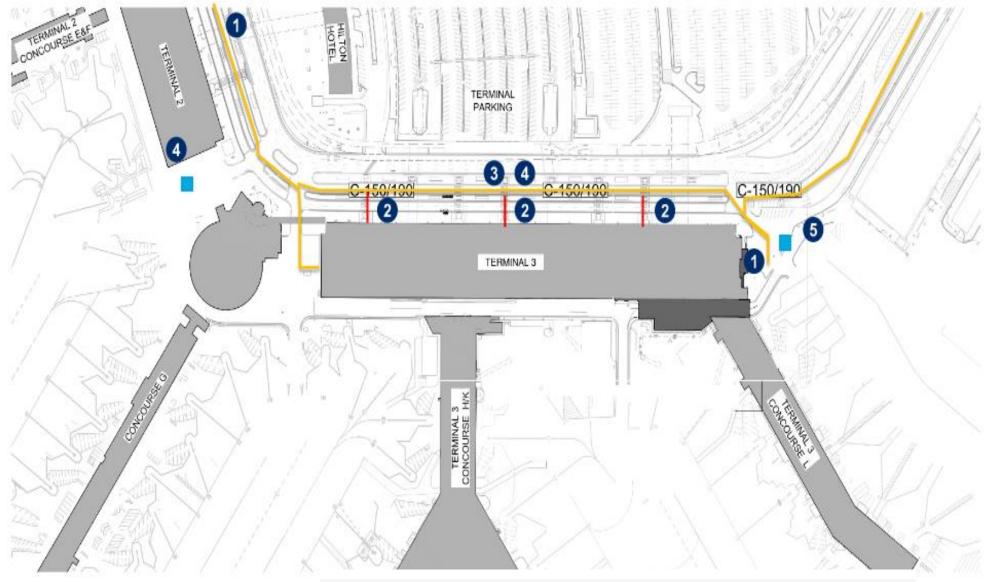

<sup>\*\*</sup>Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."

### PROJECT OVERVIEW -PRELIMINARY APRON WORK LOGISTICS

#### Apron - Work Rules

#### **General Notes**

- Subcontractor is responsible for maintaining tug traffic access to OH to all baggage areas including through the overhead doors at all times during operations.
- Gate K2 will remain operational. Work adjacent K2 must be scheduled & coordinated in advance with Owner and Clark-WE O'Neil JV
- During full duration of expansion work: Stabilized construction entrance w/ trackout control (synthetic/movable). Full-time tire wash by trades. Full-time sweeper by trades, by trades performing work on the VSR as required
- Full-time sweeper required by trades during expansion area construction at VSR & haul routes

#### Legend

- Jersey Barricade Construction Area
- ---- Jersey Barricade Temp Scheduled outing w/ Gate K2
- OH Protection
- Flagger
- Tire-Wash/Track-out Control
- OH Door
- Stair Tower Landing at Apron, Upper Level, Roof Level



INCL. IN YOUR BID AS NEEDED FOR YOUR WORK

<sup>\*\*</sup>Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."

### **NOTICE**:

BIDDERS MUST CONDUCT A SITE INSPECTION TO UNDERSTAND THE CONDITIONS, FACILITIES, AND SITE LOGISTICS RELEVANT TO THE WORK OUTLINED IN THE CONTRACT.

THE FAILURE TO VISIT THE SITE DOES NOT EXEMPT OR CHANGE THE BIDDER'S RESPONSIBILITY TO COMPLETE THE WORK IN ACCORDANCE WITH THE CONTRACT DOCUMENTS.

#### TRADE PACKAGES: BID PACKAGE 1, TRADE PACKAGES 2.26, 2.12, 2.18, 2.29

Resilient Flooring & Carpet

Resinous Flooring

Final Cleaning

2.12

2.18

Bid Package S	Schedule_v1	: Sheet1												
CLA	RK	W·E	E-O'NEIL											
TERMINAL 3 I	MPROVEME	NTS												
<b>BID PACKAGE</b>	/ TRADE P	ACKAGE	SCHEDULE											
Updated:	1/5/2024													
Note: Below da	ites / times a	re subject	to change at COT3's discretion. Updates will be poste	d on COT3's wel	osite and notices	distributed via Buildin	gConnected							
Bid Package Description	Bid Pkg	Trade Pacakg		Notice of Bid Opportunity	Invitation to Bid Date	Pre-Bid Conference Date / Time	Question Cut-Off Date / Time	Bid Opening Date / Time						
, i		e   ८.၂၃	IEIIazzu	Date IUIZUIZUZS	0112012027	01/30/27 10.00 AN	02/00/2 <del>1</del> 0.00pm	טבובטובטבד ב.טטטווו						
		2.15	Painting & Intumescent Fireproofing	10/26/2023	01/23/2024	01/30/24 10:00 AM	Date / Time Time 02/06/24 5:00pm 02/23/2024 2:00pm	02/23/2024 2:00pm						
		2.16	Metal Wall Panels	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm						
		1.10	Fire Protection	10/26/2023	01/03/2024	01/10/24 8:00 AM	01/17/24 5:00pm	03/01/2024 2:00pm						
		2.14	Doors, Frames and Hardware	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm						
								2.17	Interior Glass	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.20	TSA Systems Integrator	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm						
		2.22	Pedestrian Security Equipment - Breach control	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm						
		2.24	Overhead doors	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm						
		2.25	Signage	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm						
		2.26	Division 10 - Specialties & Accessories	10/26/2023	02/07/2024	02/14/24 10:00am	02/21/24 5:00pm	03/08/2024 2:00pm						

10/26/2023

10/26/2023

10/26/2023

02/07/2024

02/07/2024

02/07/2024

02/14/24 10:00am

02/14/24 10:00am

02/14/24 10:00am

02/21/24 5:00pm

02/21/24 5:00pm

02/21/24 5:00pm

03/08/2024 2:00pm

03/08/2024 2:00pm

03/08/2024 2:00pm

### **COMPLIANCE- REQUIREMENT SUMMARY**

#### **DBE** Requirements

- Participation at any level
- Trade specific range:
   24% 30%+
   depending on trade

## City Resident & Project Area Resident Requirements

- 50% City Residents
- 7.5% Project Area Residents
- Norwood Park
- Edison Park
- Jefferson Park
- Dunning
- Forest Glen
- Portage Park

### Affirmative Action Requirements

- Minority participation: 19.6%
- Female participation: 6.9%

#### Buy America Build America (BABA) Project

 See specifications for complete requirements

**Workforce Commitments** 

### **COMPLIANCE- DBE PARTICIPATION**

- DBE Certification must be from the **Illinois Unified Certification Program** ("IL UCP") for the participation to apply towards the project requirements
- The DBE Contract Specific Goals set during the contract bid are applicable to any adjustments made to the contract after award.
- The contribution towards meeting the Contract Specific Goals only include the dollars paid to the DBE firm for the work performed within its certified Area of Specialty.
- All Subcontractors are required to use the B2Gnow system to track compliance and payments, including:
  - Entering all certified and non-certified Sub tier Subcontractors, including contract values.
  - Confirming payment(s) received and reporting sub tier Subcontractor payments made.
  - Ensure all sub tier Subcontractor commitments are current and all payments are confirmed.



### COMPLIANCE- DBE PARTICIPATION



#### CITY OF CHICAGO

#### Department of Procurement Services Aileen Velazquez, Chief Procurement Officer

121 North LaSalle Street, Room 806 Chicago, Illinois 60602-1284 Fax: 312-744-3281

DBE SPECIAL CONDITIONS FOR FAA/FTA/FHWA (IDOT) FUNDED CONTRACTS CONSTRUCTION, SERVICES, TASK ORDER SERVICES, AND SUPPLY

ARTICLE 1. SPECIAL CONDITIONS REGARDING DISADVANTAGED BUSINESS ENTERPRISE COMMITMENT Contractor must comply with the following terms and conditions where Work or Services are funded in whole or in part by any federal funds including but not limited to FHWA, FTA and FAA.

In the event of a conflict between these Special Conditions and 49 CFR Part 26, the provisions of 49 CFR Part 26 shall control.

It is the policy of the City that Disadvantaged Business Enterprises (DBEs) as defined in 49 CFR Part 26, have the maximum opportunity to participate fully in the performance of contracts subject to 49 CFR Part 26. Contractor must not discriminate against any person or business on the basis of race, color, national origin or sex in the performance of this Contract. Contractor must carry out applicable requirements of 49 CFR Part 26 in the award and administration of United States Department of Transportation (DOT)-assisted contracts and take affirmative action to ensure that businesses owned by socially and economically disadvantaged individuals have full opportunity to participate.

The CMAR has set an overall DBE Program Goal of 30%.

Failure to carry out the commitments and policies set forth in this Article constitutes a material breach of the Contract and may result in the termination of the Contract or such remedy as the CMAR deems appropriate.

#### 1.1.1. Contract-Specific DBE Participation Goal

The CMAR sets contract-specific goals for participation in furtherance of reaching its overall DBE Program Goal.

For purposes of this contract, the CMAR has set the following contract goal:

#### Contract DBE Participation Goal: 24%

Note: if this contract is task-order based, goals will be set for the individual task orders; in the context of each task order, these provisions will apply to those task order goals as if they were an overall contract goal.

A bid or proposal may be rejected as non-responsive if the bidder/proposer fails to submit one or more of the following with its bid demonstrating its good faith efforts to meet the Contract DBE Participation Goal by reaching out to DBEs to perform work on the contract

- A DBE compliance plan demonstrating how the bidder/proposer plans to meet the Contract DBE Participation Goal (Schedule D. D-1 or D-3 and Schedule(s) C. C-1 or C-3); and/or
- Documentation of Good Faith Efforts to obtain DBE participation in this contract.

Note: Schedules D and C are used for contracts for construction work. Schedules D-1 and D-3 are used for contracts for services, and Schedules D-3 and C-3 are used for task order based contracts.

The bidder/proposer must make good faith efforts to obtain DBE participation in this contract. The commitment will be reflected in Schedule D, D-1 or D-3. The bidder/proposer must document that it has obtained enough DBE participation to meet the Contract DBE Participation Goal set forth above or, if unsuccessful in doing so, has made adequate Good Faith Efforts to meet the goal (see Section 1.7 "Good Faith Efforts"). If awarded the Contract, Contractor must expend not less than the committed percentage of the total Contract Price (including any amendments and modifications) for contract participation by DBEs.

For purposes of evaluating bidder/proposer's responsiveness, the Contract DBE Participation Goal will be a percentage of the total contract value. The Contract DBE Participation Goal applies to the total value of the contract, inclusive of all amendments and modifications. The Chief Procurement Officer also has the authority to review each proposed contract modification and amendment that by itself or aggregated with previous modification amendment requests, increases the contract value by 10 percent of the initial award or \$50,000, whichever is greater, for opportunities to increase participation of DBEs already involved in the contract.

CMAR Federally Funded Instructions and Execution Documents



#### **CITY OF CHICAGO ASSIST AGENCY LIST**

	ATTACHMENT B (On Bidder/Proposer's Letterhead)	
RETURN RECEIPT REQUESTED		(Date)
	Re: Specification	
(Assist Agency Name and Address)	Description:	
Dear :		
(Bidder/Proposer) intends Bids are due on	to submit a bid/proposal in response to the above	e referenced specification with the CMAI
The following areas have been identified in	for subcontracting opportunities on both a direct	and indirect basis:
	ractors have not been successful in order to m of any DBE firms that would be capable of perfi	
Name of Company Re	presentativeatat	Address/phone
within (10) ten working days of receipt of	this letter	
receipt of this letter to:  Program Manager Connect Chicago Alliance 10510 West Zemble Road Chicago, IL 60666		
(Timely Information Open Imme	•	
If you wish to discuss this matter, please of	ontact the undersigned at	-
Sincerely,		
CMAR Federally Funded	Instructions and Execution Documents	
Terminal 3 Improvements	Bid Parkana No. 1.1	S5-24

of small, minority and/c							
	Chatham Busine	ss Association 5	Small Business Dev. *			evelopment Council Inc. *	
51st Street Business Asso	800 E. 78th Street			105 W. Adams			
220 E. 51st Street	Chicago, IL 60816	3		Chicago, IL 60	003-0233		
Chicago, IL 60615	773-994-5006						
773-285-3401	773-855-8908		est Development Corpora	tion		rican Construction Industry	
773-285-3407	admin@cbaw	2601 W. 63rd Stre			Association (H		
the51ststreetbusinessass	www.cbawork	Chicago, IL 6062	9		650 W. Lake St		
www.51stStreetChicago.c	Maintains list	773-362-3373			Chicago, IL 606	361	
	Provides train	c.james@grea					
Maintains list of certified: Provides training for busin		www.greatersc					
Provides training for busir	Chicago Urb	training for bus	South Shore Chamber, In	nc. *		Sustainable Options for Urb	an Living, Inc. (SOUL)
	4510 S. Michi	training for bus	1750 E. 71st Street			11603 S. Throop	
Angel of God Resource Co	Chicago, IL 6		Chicago, IL 60649-2000			Street Chicago, IL 60643	
14527 S. Halsted	773-285-5800		773-955- 9508			773-250-1770 Ext 702	
Riverdale, IL 60827	jjohnson@chi		773-955-9554			773 250-1770 Ext 702	
708-392-9323	Maintains list	HIRE360	Tonya Trice, Executive Dir	rector		Cyndi@soul-	
708-880-0121	Provides train	2301 S Lake S Chicago, IL 60	info@southshorechamber			program.com www.soul-	
info.eogrc@gmaiil.com		312 575-2500	www.southshorechamberi			program.com	
www.angelofgodresource		info@HIRE360	Maintains list of certified fi			Maintains list of certified firms:	
Maintains list of certified		www.HIRE360	Provides training for busin	esses: Yes		Provides training for businesse	es: Yes
Provides training for busir	Contractor A	list of certified					
		training for bus	The Monroe Foundation			Turn 2 Growth	
Austin African American	1507 E. 53rd S	training for bus	1547 South Wolf Road			15475 S. Park	
5820 W. Chicago Ave.	Chicago, IL. 6		Hillside, Illinois 60162 773-315-9720			South Holland, IL 60473 708-913-4700	
Chicago, IL 60651	312-436-0301	Illinois Hispar					
773-626-4497	info@contrac	222 Merchand	omonroe@themonroefoun www.themonroefoundation			info@turn2growth.org www.turn2growth.org	
info@sasbns.org	www.contract	Chicago, IL 60	Maintains list of certified fi			Maintains list of certified firms:	. V
www.aaabna.org	list of certified training for bu	312-425-9500	Provides training for busin			Provides training for businesse	
Maintains list of certified	training for bt	info@ihccbusir	Provides training for busin	esses. Tes		Provides training for businesse	es. res
Provides training for busir	Council of B	www.ihccbusin					
	Engineering	Maintains list c	US Minority Contractors	Association Inc	*	Women's Business Develop	ment Center *
Black Contractors Owners	1 South Waci	Provides traini	1250 S. Grove Ave. Suite			8 S. Michigan Ave., Suite 400	ment demer
7811 S. Stony Island Ave.	Chicago, IL 6		Barrington, IL 60010	200		Chicago, IL 60603	
Chicago, IL 60649	312-960-1236		847-352-5010			312-853-3477×220	
773-346-5658	msutton@infr		847-382-1787			312-853-0145	
773-346-5659	Maintains list	JLM Business	larry.bullock@usminorityo	ontractors.org		edimenco@wbdo.org	
admin@bcoechicago.org	Provides train	Center* 2622	www.USMinorityContracto			www.wbdc.org	
www.bcoechicago.org		Chicago, IL 60 773-826-3064	Maintains list of certified fi	rms: Yes		Maintains list of certified firms:	Yes
Maintains list of certified		773-359-4021	Provides training for busin	esses: Yes		Provides training for businesse	es: Yes
Provides training for busir	Elite Service	lady930@prod	_				
Trovides training for busin	420 Lake Cor	www.jlmcenter	Women Construction Ov	vners & Executiv	res (WCOE) *		
BOP Project 5000 NFP	Deerfield, IL (	Maintains list c	Chicago Caucus				
644 E. 79th Street	847-453-8890	Provides traini	308 Circle Avenue				
	jscifers@scig		Forest Park, IL 60130 708-366-1250				
Chicago, IL 60619 773-891-5939	www.elitesdv		/08-366-1250 mkm@mkmservices.com				
773-891-3939	Maintains list	Native Americ	www.wcoeusa.org				
	Provides train	100 N. Riversii	Maintains list of certified fi	rms: Yes			
bopbizcenter@gmail.com		Chicago, IL 60	Provides training for busin				
list of certified firms: Yes		630-926-1700	1				
Provides training for busir	Federation o	info@nacc-il.o					
	4210 W. Irvin	www.nacc-il.or					
	Chicago, IL 6	Maintains list c					
	312-360-1122	Provides trainii					
	info@fwcchic						
	www.fwechie; Maintains list						
	Provides train	Rainbow/PUS					
	riovides trair	930 E. 50th Stn					
		Chicago, IL 60					
		773-255-9087					
		773-256-2768					
*Prime Contract		imitchell@rain					
		www.rainbowp					
Rev. July 2020 – I		Maintains list c					
		Frovides trainii					
	*Prime						

\*Prime Contractors should contact agency with subcontracting opportunities to connect certified firms



OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

### **COMPLIANCE- WORKFORCE COMMITMENTS**

Federal Requirements

Minority Worker Requirement – 19.6%

Female Worker Requirement – 6.9%

Chicago Requirements

City of Chicago Residency Requirement – 50%

Project Area Worker Requirement – 7.5%

The Contract requires compliance with Chicago Residency Ordinance, Section 2 92 330 of the Chicago Municipal Code.

Failure to meet these requirements will result in assessment of penalties in the form of liquidated damages

1/20 of 1% (0.05%), 0.0005, of the approved contract value shall be assessed to the prime Subcontractor for each percentage of shortfall toward the stipulated residency requirement.

### **CONTRACT ADMINISTRATION- SOFTWARE**

### Administrative

- B2Gnow
- DocuSign
- LCP Tracker
- Oracle Textura
- Wrap X

### Project Management

- Revisto
- E-Builder
- Primavera P6
- Procore

### CONTRACT ADMINISTRATION- SCHEDULE OF VALUES REQUIREMENTS

Subcontract shall include line items on their Schedule of Values for the following work activities (at the following percentages relative to total Subcontract value):

- Close-out Documentation and Submittals including but not limited to As-builts, Warranty Documents, LEED and Training (2%)
- Punch List (2%)
- Demobilization (2%)
- Cleanup (2%)
- Safety (2%)

Subcontractor shall include a line item on their Schedule of Values for the city's residency requirements as outlined in Exhibit B and in the Chicago Municipal Code section 2-92-330. The line item shall consist of the maximum possible of the liquidated damages associated with the project area and city resident requirements. Subcontractor shall be allowed to invoice this line item periodically, and only to the extent that these residency requirements have been met and confirmed through certified payroll. At the end of the Project an accounting will be tabulated to determine any liquidated damages owed by Subcontractor related to unmet residency requirements, and these damages will be funded from this line item in the Subcontractor Schedule of Values.

### **CONTRACT ADMINISTRATION- SCHEDULE**

Schedule Resource Loading will be required by each Subcontractor:

- Manpower (Crew Size and Hours)
- Equipment (Type, Quantity and Equipment Hours)

### **CONTRACT ADMINISTRATION- PAYMENT APPLICATIONS**

### MANDATORY WITH EACH PAYMENT REQUEST:

- G702 AND G703
- STATEMENT OF SUBCONTRACTOR TO COT3
- CONDITIONAL WAIVER AND RELEASES ON PROGRESS PAYMENTS
- WAIVER OF LIEN TO DATE
- CHANGE ORDER REQUEST LOG
- IF APPLICABLE, CITY OF CHICAGO C&D DEBRIS RECYCLING COMPLIANCE FORMS
- IF APPLICABLE, DIESEL EMISSIONS COMPLIANCE FORM
- IF APPLICABLE, STORED MATERIAL DOCUMENTATION
- OTHER SAM DOCUMENTATION, AS APPLICABLE

### CONTRACT ADMINISTRATION- INSURANCE

Owner Controlled Insurance Program (OCIP)

Insurance Administrator – Alliant

Each Subcontractor, along with all lower-tier subcontractors, including professional services and suppliers, must undergo the enrollment process. Alliant will assess and notify if any firm is ineligible for participation in the program.

The Subcontractor must input all lower-tier subcontractors into WrapX. The actual labor, categorized by classification, needs to be documented through monthly payroll entries in the WrapX portal.

Review and approval of insurance will be handled directly between the Subcontractor and Alliant.

Additional insurance requirements outside of OCIP. See Sample Subcontract – Exhibit E

### **CONTRACT ADMINISTRATION- OCIP**

### **Enrolled Parties**

- All Eligible Prime Subs
- All Eligible
   Subcontractor Tiers
   performing labor or
   services at the Project
   Site
- Other Parties Enrolled at Owners Discretion

#### **Excluded Parties**

- Demolition
- Hazardous Materials Contractors/Transporters
- Vendors, Suppliers, Fabricators, Material Haulers, Truckers, Cranes
- Subcontractors of any tier not eligible for and are excluded from the OCIP

### **CONTRACT ADMINISTRATION- OCIP ENROLLMENT**

#### **Contract signed with Subcontractor**

The Awarding Contractor Notifies Alliant through a Notice of Award (NOA) Letter

#### **Enrollment in project**

- Alliant works directly with the subcontractor for enrollment
- Enrollment must be completed online and be accepted before commencing work onsite
- If a subcontractor is onsite prior to enrollment, Carrier is not obligated to cover any accidents- there is no coverage.
- Backdating coverage is challenging if a contractor is discovered onsite without enrollment Enrollment – requires the following information:
  - Onsite Enrollment Form
  - Insurance Cost Worksheet with WC/GL/XS Rate & Declaration Pages
  - Offsite proof of insurance COI & Policy Endorsements (All Tiers)

#### **Ongoing Subcontractor Responsibilities:**

- Submit monthly payroll to Alliant through online entry
- Provide renewal offsite COI & Endorsements (All Tiers)

# CONTRACT ADMINISTRATION- PROFESSIONAL LIABILITY INSURANCE



CDA'S PPL INSURANCE PROGRAM IS A
REQUIREMENT FOR ALL SUBCONTRACTORS
THAT HAVE A SCOPE OF WORK THAT INCLUDES
DESIGN AND ENGINEERING



THE COST OF PARTICIPATING INTO THE PROGRAM IS 3/4% AND WILL BE DEDUCTED FROM THE CONTRACT AMOUNT



NO CHANGE ORDERS WILL BE ISSUED IF THIS FEE IS NOT RETURNED IT APPEARS THIS COST HAS NOT BEEN RETURNED TO ANY CONTRACTOR TO DATE (YET)

### **SAFETY**

- Chicago Department of Aviation Construction Safety Manual November 2022
- Clark-W.E. O'Neil JV Safety Manual
- Subcontractor is required to: (i) develop a sitespecific safety plan, and (ii) reference subcontract for additional safety requirements and dedicated on-site Safety representation



### CONSTRUCTION SAFETY MANUAL NOVEMBER 2022



### QUALITY ASSURANCE / QUALITY CONTROL

Technical Specification 01 4000 – Quality Requirements

Prior to commencing work:

- The Subcontractor must submit a Quality Control Plan for approval by COT3
- The Subcontractor is responsible to conduct a Pre-activity meeting

Each Subcontractor is required to provide a dedicated Quality Control representative onsite at all times

### PROCUREMENT - QUESTIONS, PRE-BID RFI'S & ADDENDUMS

Bid Package Schedule\_v1 : Sheet1

CLA CONSTRU	CTION		·O'NEIL						
BID PACKAGE			SCHEDULE						
Jpdated:	1/5/2024								
•			to change at COT3's discretion. Updates will be poste	ed on COT3's wel	osite and notices	distribute	a Buildin	gConnected	
Bid Package Description	Bid Pkg	Trade Pacakg e	Trade Package Description	Notice of Bid Opportunity Date	Invitation to Bid Date		ference ime	Question Cut-Off Date / Time	Bid Opening Date Time
		2.13	тепаzzo	10/20/2023	01/20/2024	01/00/2-110.		02/00/24 5.00pm	02/20/2024 2.00pm
		2.15	Painting & Intumescent Fireproofing	10/26/2023	01/23/2024	01/30/24 10:		02/06/24 5:00pm	02/23/2024 2:00pm
		2.16	Metal Wall Panels	10/26/2023	01/23/2024	01/30/24 10:		02/06/24 5:00pm	02/23/2024 2:00pm
		1.10	Fire Protection	10/26/2023	01/03/2024	01/10/24 8:0		01/17/24 5:00pm	03/01/2024 2:00pm
		2.14	Doors, Frames and Hardware	10/26/2023	01/31/2024	02/07/24 10:	00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.17	Interior Glass	10/26/2023	01/31/2024	02/07/24 10:	00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.20	TSA Systems Integrator	10/26/2023	01/31/2024	02/07/24 10:	MA 00	02/14/24 5:00pm	03/01/2024 2:00pm
		2.22	Pedestrian Security Equipment - Breach control	10/26/2023	01/31/2024	02/07/24 10:	MA 00	02/14/24 5:00pm	03/01/2024 2:00pm
		2.24	Overhead doors	10/26/2023	01/31/2024	02/07/24 10:	MA 00	02/14/24 5:00pm	03/01/2024 2:00pm
		2.25	Signage	10/26/2023	01/31/2024	02/07/24 10:	00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.26	Division 10 - Specialties & Accessories	10/26/2023	02/07/2024	02/14/24 10:	00am	02/21/24 5:00pm	03/08/2024 2:00pm
		2.12	Resilient Flooring & Carpet	10/26/2023	02/07/2024	02/14/24 10:	00am	02/21/24 5:00pm	03/08/2024 2:00pm
		2.18	Resinous Flooring	10/26/2023	02/07/2024	02/14/24 10:	00am	02/21/24 5:00pm	03/08/2024 2:00pm
		2.29	Final Cleaning	10/26/2023	02/07/2024	02/14/24 10:	00am	02/21/24 5:00pm	03/08/2024 2:00pm

### PROCUREMENT – REQUEST FOR INFORMATION



SUBMIT ALL PROJECT RFI'S VIA EMAIL OR THROUGH BUILDING CONNECTED





Email:

ProjectCOT3.inquiries@clarkconstruction.com



Subject: RFI T3 Improvements "Trade Package" – "Company Name"

#### NOTES:

- MAKE SURE TO SUBMIT ALL QUESTIONS VIA RFI BY THE QUESTION CUT-OFF DATE & TIME INDICATED. LATE QUESTIONS WILL NOT BE RESPONDED TO!
- ALL RESPONSES WILL BE PROVIDED VIA BID ADDENDUM.

### PRE-BID ADDENDUM TIMELINE

ADDENDUMS, IF ANY, ARE PLANNED TO BE ISSUED FOR ISSUANCE NO LATER THAN ONE WEEK BEFORE THE BID OPENING

#### LIST OF ANTICIPATED ADDENDUMS:

- UPDATED PROJECT SCHEDULE
- UPDATED EXHIBIT B'S
- ADDENDUM #01 DESIGN UPDATES/CLARIFICATIONS
- ADDENDUM #02 DESIGN UPDATES/CLARIFICATIONS
- ADDENDUM #XXX PRE-BID RFI RESPONSES

### PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

### **PROCUREMENT - CHECKLIST**

#### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ☐ Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5 ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ■ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

### PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Base Bid Line Items - Pricing

**Alternates** 

**Inclusions** 

\*Scope included per Exhibit B

Scope-Specific Information and Unit Costs



### PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Scope-Specific Information and Unit Costs (continued from above)

General Acknowledgements

02141 : O'Hare Terminal 3 Improvements  00 West Balmoral Avenue, Terminal 3, Chicago, It. 60566, United States of America			
*Asbestos Abatement of 4* LTWR Fittings (\$ per Each)	per each	s	
*Lead Based Paint Abatement of door frames (\$ per Each)	per each	\$	
*Lead Based Paint Abatement of wide flange beams (\$ per SF)	per square foot	\$	
*Lead Based Paint Abatement of pipe hangars (\$ per Each)	per each	S	
*Lead Based Paint Abatement of valve wheels (\$ per Each)	per each	\$	
*Lead Based Paint Abatement of electrical boxes (\$ per Each)	per each	\$	
*Lead Based Paint Abatement of pipe - assume 4* OD (\$ per Linear Foot)	per linear foot	\$	
*Lead Based Paint Abatement of bollards or pipe guards (\$ per Each)	per each	\$	
*Lead Based Paint Abatement of handrail/guard rail (\$ per Linear Foot)	per linear foot	\$	
General Acknowledgments	Mark "yes" to all		
*Have you prepared your proposal in accordance with the Plans and Specifications?			O N
"Have you reviewed all Division 0 and 1 of the Specifications?			O N
"Have you reviewed the requirements for shift work and included premium cost as applicable?			O N
*Does your scope require design services or engineering?	C	) Yes	O N
"If Yes to Design Services and Engineering, have you included 3/4% of your Bid total in you Bid for Project Professional Liability Insurance that may not be refunded at the end of the Job?	С	) Yes	() No
"Subcontractor acknowledges their responsibility for all liquidated damages as a result of their performance and Work, as defined in the Owner Master Agreement, No. 234140.	C	) Yes	() No
Subcontractor acknowledges that they shall be responsible for any Builders Risk and General Liability deductibles associated with a claim resulting from your Work, as outlined in Exhibit D or E of the Subcontract Agreement.	C	) Yes	O N
<sup>1</sup> The Bidder agrees to submit its bid without limitations or exceptions, except as permitted by the Contract Documents.	C	) Yes	O N
*The Bidder further agrees that if awarded the Contract, the Bidder shall perform the Contract with no limitations or exceptions.	C	) Yes	() N
*The Contract Base Bid shall include the entire scope of Work and requirements of Part One, Part Two, Part Three and the Contract Drawings of the Contract Documents.	C	) Yes	() N
* The Contract will be awarded to the responsive and responsible Bidder offering the lowest Contract Base Bid, as determined by the Chief Procurement Officer.	C	) Yes	( No
*The contractor acknowledges that they may be asked to proceed with a Letter of Intent.	C	) Yes	O N
Bids will be compared based on the Bid Amount(s) and any combination of Alternates of each Trade Package, correctly computed, and a contract, if awarded, will be to the lowest response and responsible bidder, as determined by the CMAR.	С	) Yes	O N


### PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

General Acknowledgements (continued from above)

Checklist of Required Documents to attached to your electronic bid submission through building connected

DBE Schedules (as applies)

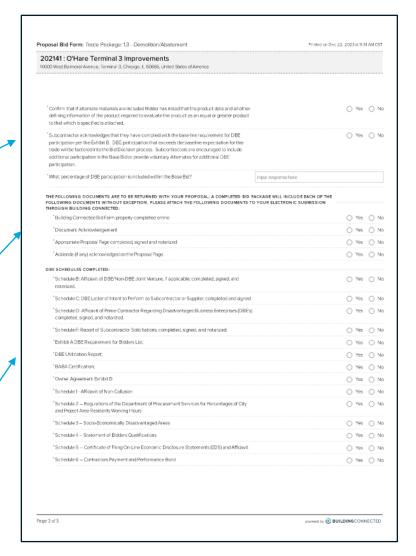

## PROCUREMENT – BID FORM (SUBMIT ONLINE)


BUILDING CONNECTED BID FORM SECTIONS

Checklist of Required Documents to attached to your electronic bid submission through building connected

**FAA Certifications** 

Other Requirements

Subcontract Exhibits

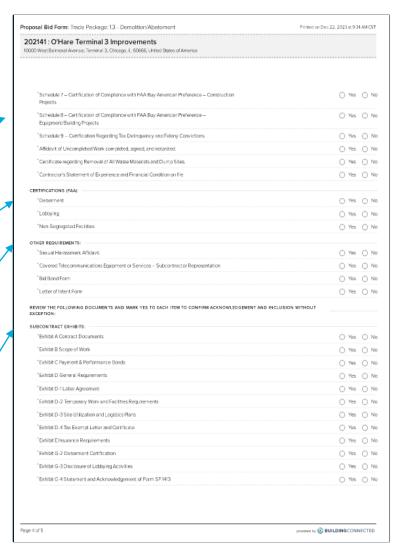

## PROCUREMENT – BID FORM (SUBMIT ONLINE)


BUILDING CONNECTED BID FORM SECTIONS

Subcontract Exhibits (continued)

Subcontract Attachments

Certifications

**Attachments** 

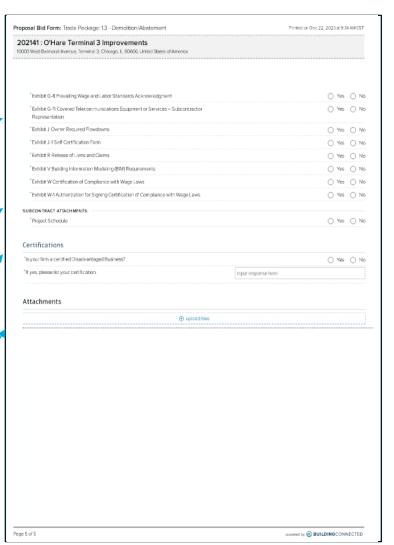

## PROCUREMENT – CHECKLIST (list of items to be returned with bid)

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ☐ Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



## PROCUREMENT - DOCUMENT ACKNOWLEDGEMENT

Complete and return with your bid.

This checklist is intended to assist Bidders but does not necessarily reference all documents required in this partice Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalid a bid.  Review the following Documents and initial each item to confirm acknowledgement and inclusion without exception.  Subcontract Exhibits:  1Exhibit A Contract Documents 2Exhibit B Scope of Work 3Exhibit B Scope of Work 3Exhibit D Scope of Work 4Exhibit D Factor Section of Section 1Exhibit D Scope of Work 5Exhibit D Factor Section Section 1Exhibit D Scope of Work 6Exhibit D Factor Section Sectio		(Federally Funded)
Subcontract Exhibits:  1Exhibit A Contract Documents 2Exhibit B Scope of Work 3Exhibit D General Requirements 4Exhibit D General Requirements 5Exhibit D-1 Labor Agreement 6.	Specifi	
1. Exhibit A Contract Documents 2. Exhibit B Scope of Work 3. Exhibit C Payment & Performance Bonds 4. Exhibit D General Requirements 5. Exhibit D General Requirements 6. Not Used 7. Exhibit D-3 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-2 Debarment Certification 10. Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-4 Statement and Acknowledgement of Form SF in the Statement of St	Review	the following Documents and initial each item to confirm acknowledgement and inclusion without exception
2. Exhibit B Scope of Work 3. Exhibit C Payment & Performance Bonds 4. Exhibit D General Requirements 5. Exhibit D-1 Labor Agreement 6. Not Used 7. Exhibit D-3 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-12 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J Ower Required Flowdowns 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	Subcon	ract Exhibits:
3. Exhibit C Payment & Performance Bonds 4. Exhibit D General Requirements 5. Exhibit D-I Labor Agreement 6. Not Used 7. Exhibit D-1 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J-1 Self Certification Form 16. Exhibit J-1 Self Certification Form 17. Exhibit R Release of Liens and Claims 18. Exhibit W Building Information Modeling (BIM) Requirements 19. Exhibit W Building Information Modeling (BIM) Requirements 19. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title  Date	1.	Exhibit A Contract Documents
4. Exhibit D General Requirements 5. Exhibit D-1 Labor Agreement 6. Not Used 7. Exhibit D-3 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-2 Debarment Certification 10. Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J-1 Self Certification Form 17. Exhibit R Release of Liens and Claims 18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	2.	Exhibit B Scope of Work
5. Exhibit D-1 Labor Agreement 6. Not Used 7. Exhibit D-3 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-2 Debarment Certification 10. Exhibit G-3 Disclosure of Lobbying Activities 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J-1 Self Certification Form 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	3.	Exhibit C Payment & Performance Bonds
6. Not Used 7. Exhibit D-3 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-3 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J-1 Self Certification Form 17. Exhibit J-1 Self Certification Form 18. Exhibit Vauilding Information Modeling (BIM) Requirements 19. Exhibit Wuilding Information Modeling (BIM) Requirements 19. Exhibit W-1 Authorization of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Date  Date	4.	Exhibit D General Requirements
7. Exhibit D-3 Site Utilization and Logistics Plans 8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-2 Debarment Certification 10. Exhibit G-3 Disclosure of Lobbying Activities 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J-1 Self Certification Form 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Bridling Information Modeling (BIM) Requirements 19. Exhibit W-crtification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title  Date		
8. Exhibit D-4 Tax Exempt Letter and Certificate 9. Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-3 Disclosure of Lobbying Activities 13. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 14. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 15. Exhibit J-1 Covered Telecommunications Equipment or Services – Subcontractor Representation 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Betailing Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	6.	
9. Exhibit E Insurance Requirements 10. Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J Owner Required Flowdowns 16. Exhibit 11 Self Certification Form 17. Exhibit R Release of Liens and Claims 18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W Building Information Modeling (BIM) Requirements 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws Subcontract Attachments: 1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	7.	Exhibit D-3 Site Utilization and Logistics Plans
10. Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J Owner Required Flowdowns 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Exhibit W Certification of Compliance with Wage Laws 19. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments: 1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	8.	Exhibit D-4 Tax Exempt Letter and Certificate
11. Exhibit G-3 Disclosure of Lobbying Activities 12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413 13. Exhibit G-4 Streaming Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J-1 Self Certification Form 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit W Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	9.	Exhibit E Insurance Requirements
12. Exhibit G-4 Statement and Acknowledgement of Form SF 1413  13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment  14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation  15. Exhibit J Owner Required Flowdowns  16. Exhibit J-1 Self Certification Form  17. Exhibit R Release of Liens and Claims  18. Exhibit V Building Information Modeling (BIM) Requirements  19. Exhibit W Certification of Compliance with Wage Laws  20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule  2. Letter of Intent  Authorized Signature  Title Date	10.	Exhibit G-2 Debarment Certification
13. Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J Owner Required Flowdowns 16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	11.	Exhibit G-3 Disclosure of Lobbying Activities
14. Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation 15. Exhibit J Owner Required Flowdowns 16. Exhibit J 1- Self Certification Form 17. Exhibit R Release of Liens and Claims 18. Exhibit W Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title  Date	12.	Exhibit G-4 Statement and Acknowledgement of Form SF 1413
15. Exhibit J Owner Required Flowdowns 16. Exhibit 1-1 Self Certification Form 17. Exhibit R Release of Liens and Claims 18. Exhibit W Building Information Modeling (BIM) Requirements 19. Exhibit W-certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	13.	Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment
16. Exhibit J-1 Self Certification Form 17. Exhibit Release of Liens and Claims 18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W-1 Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	14.	Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation
17. Exhibit R Release of Liens and Claims 18. Exhibit W Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	15.	Exhibit J Owner Required Flowdowns
18. Exhibit V Building Information Modeling (BIM) Requirements 19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	16.	Exhibit J-1 Self Certification Form
19. Exhibit W Certification of Compliance with Wage Laws 20. Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	17.	Exhibit R Release of Liens and Claims
20Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1.	18.	Exhibit V Building Information Modeling (BIM) Requirements
20 Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws  Subcontract Attachments:  1. Project Schedule 2 Letter of Intent  Authorized Signature  Title Date	19.	Exhibit W Certification of Compliance with Wage Laws
1. Project Schedule 2. Letter of Intent  Authorized Signature  Title Date	20	
2 Letter of Intent  Authorized Signature  Title Date	Subcon	ract Attachments:
2Letter of Intent  Authorized Signature  TitleDate		
Authorized Signature  Title Date		
TitleDate	2	Letter of Intent
TitleDate		
	Autho	rized Signature
I hereby acknowledge all of the above documents and certify that all associated costs are included in our proposal.		Date
		Date
		acknowledge all of the above documents and certify that all associated costs are included in our proposal.
		acknowledge all of the above documents and certify that all associated costs are included in our proposal.
		acknowledge all of the above documents and certify that all associated costs are included in our proposal.
		acknowledge all of the above documents and certify that all associated costs are included in our proposal.

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



## PROCUREMENT – PROPOSAL PAGES S5-1 - S5-5 (as applies)

### SECTION 5 PROPOSAL TO BE EXECUTED BY A CORPORATION

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 44 Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criger's and Cohomistal Requirements (If RPFRPG), 6) Proposal Pages, 7) Certifications and 8) Addenda Nov. (none unley)

and affirms that the corporation shall be bound by all the terms and condition.

Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only
the corporation has taken express written exception thereto in the sections of this specification designated the

Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an EDS Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted any certification in the EDS false, inaccurate or incomplete.

Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership withheld and the information provided therein to the best of its knowledge is current and the undersigned II any agreement with any other bidder (proposer) or prospective bidder (proposer) or with any other corporation relating to the price named in this proposal or any other proposal, nor any agreement or arrang any act or omission in restraining of free competition among bidders (proposers) and has not disclosed to ecoporation the terms of this bidd (proposal) or the proposal) or the proposal or proposal pro

Proposals must be submitted with original signatures in the space provided. Proposals not properly signed

NAME OF CORROBATION

#### PROPOSAL TO BE EXECUTED BY A SOLE PROPRIETOR

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Palas or Drawings (if applicable). 5) Leptialed Specifications or Scope of Services, Evaluation/Selection Critegia and Submittal.

#### PROPOSAL TO BE EXECUTED BY A PARTNERSHIP

The undersigned hereby acknowledges having received Bid Package No. 14 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Biddee (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Submittal Requirements (If RFPRFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless indicated here) and affirms that the partnership shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the nattractible has aktice excess wittine exception thereto in the sections of this specification designated for that rumose.

Under penalty of perjury, the undersigned. (1) warrants that he/she was authorized to submit an EDS on behalf of the Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are true, accurate and complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of this proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted that would render any certification in the EDS false, naccurate or incomplete.

Further, the undersigned being duly sworm deposes and says on eath that no disclosures of ownershelp interests have been withheld and the information provided therein to the best of its knowledge is current and the undersigned has the relief into the undersigned and the undersigned has the relief into the proposer of the proposer of

sal Pages, 7) Certifications and 8) Addenda Nos. (none unless indithe sole proprietor shall be bound by all the terms and conditions of
the a complete set thereof is attached to this proposal, except only
ritten exception thereto in the sections of this specification designa

sed: (1) warrants that he/she was authorized to submit an EDS on b that all certifications and statements contained in the EDS are true, shmitted on-line; and (3) further warrants that, as of the date of sub nages in Circumstances since the date that the EDS was submitted t curate or incomplete.

om deposes and says on oath that no disclosures of ownership interient to the best of its knowledge is current and the undersigned proposer) or propective bidder (proposer) or with any other person in this proposal or any other proposal, nor any agreement or arrange ee competition among bidders (proposers) and has not disclosed to basl) or the price named herein.

nal signatures in the space provided. Proposals not properly signed

### PROPOSAL TO BE EXECUTED BY A JOINT VENTURE

The undersigned hereby acknowledges having received Bid Package No. 14 containing a full set of Contract Documents, including, but not insulined a, I hartestrones to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation-Selection Criteria and Submittal Requirements (if RFPRRQ), 6) Proposal Pages, 7) Certifications and 8) Addensa Nos. (none unless indicated here) and affirms that the Joint Venture and the board by all the terms and conditions contained in the

and affirms that the Joint Venture shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the Joint Venture has taken express written exception thereto in the sections of this specification designated for that purpose.

Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an EDS on behalf of the Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are true, accurate and complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of this proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted that would render any certification in the EDS false, inaccurate or incomplete.

Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership interests have been without the information provided therein to the best of its knowledge is current and the undersigned has not entered into any agreement with any other bidder (recrosser) or prospective bidder (percosser) or with any other person. Furn or

## SUBMIT ONE (1) OF THE APPLICABLE PROPOSAL EXECUTION FORMS WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED, SIGNED AND NOTARIZED

*Note: In the event that this out (proposal) is signed by other than the resident, attach nereo a central section of Corporate By-Laws or other authorization, such as a resolution by the Board of Direct permits the person to sign the offer for the Corporation.	revised Statutes 1705 Chapter 70 Sec. 4 Caseq.	s 1903 Chapter 90 Sec. 4 et seq.	JOINT VENTURE ADDRESS: (Print or Type)
ATTEST: (Corporate Secretary Signature) (Affix Corporate Seal)  State of  County of  This instrument was acknowledged before me on this day of, 20 by	Registration Number:  SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE PARTNERSHIP  (If all General Partners do not sign, indicate authority of partner signatories by attaching copy of partnership agreement or other authorizing document):  Partner Signature:  (Signature)  Address:  [Print or Type]	(Print or Type)    cdged before me on thisday of, 20 by as President (or other authorized officer) and (Corporation Name).	If you are operating under an assumed name, provide County registration number herein under as provided in the Illinois Revised Statutes 1965 Chapter 96 Sec. 4 et soq. Registration Number: SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE JOINT VENTURE (If all members of the Joint Venture do not sign, indicate authority of signatories by attaching copy of Joint Venture agreement or other authorizing document):  SIGNATURE OF Authorized Party:
as President (or other authorized officer) and  Secretary of (Corporation Name).	Address: (Signature) (Print or Type)		TITLE OF SIGNATORY:  (Print or Type)
Secretary or (Corporation Name). (Seal)  Notary Public Signature  Commission Expires:	Partner Signature:  (Signature)  Address:  (Print or Type)  State of	prop	BUSINESS ADDRESS:  (Print or Type)  ATTEST:  (Joint Venture Secretary Signature) (Affix Joint Venture Seal)
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Biol Package No.: 1,4 S	This instrument was acknowledged before me on this day of	Instructions and Execution Documents Bid Package No.: 1.4	OR Joint Venturer Signature:  (Signature)  Address:  (Print or Type)
	CMAR Federally Funded Instruction and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4 S5-2		CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1,4 SS-4

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



# PROCUREMENT – ADDENDA (if any) ACKNOWLEDGED ON PROPOSAL EXECUTION FORM

FILL IN THE BLANK ON YOUR APPLICABLE PROPOSAL EXECUTION FORM (S5-1 – S5-5)



		r			
SECTION 5		900000000000000000000000000000000000000			
PROPOSAL TO BE EXECUTED BY A CORPORATION		PROPOSA	AL TO BE EXECUTED BY A SOLE PROPRIETOR	50	
The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Con-		The undersigned hereby acknowledge	es having received Bid Package No. 1.4 containing a full set of Contra- actions to Bidders (Proposers). 2) General Conditions. 3) Special Condit	et Documents,	
neluding, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions	ions 4) Contract	Plans or Descrives (if andicable) St.	Detailed Specifications or Scope of Services, Evaluation/Selection Criter	ris and Submittal	
Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation Selection Crie Requirements (If RFP/RFO), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless			al Pages, 7) Certifications and 8) Addenda Nos. (none unless indir- the sole proprietor shall be bound by all the terms and conditions or	*****	
and affirms that the corporation shall be bound by all the terms and conditions	PROPOSAL TO BE EXECUTED BY A PART The undersigned hereby acknowledges having received Bid Package No. 1.4 co		ther a complete set thereof is attached to this proposal, except only	PROPOSAL TO	O BE EXECUTED BY A JOINT VENTURE
contract Documents, regardless of whether a complete set thereof is attached to this proposal, except on the corporation has taken express written exception thereto in the sections of this specification designated by	including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Co	ditions, 3) Special Conditions, 4) Contract	ritten exception thereto in the sections of this specification designat		
	Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Add	valuation Selection Criteria and Submittal	sed: (1) warrants that he/she was authorized to submit an EDS on b	including, but not limited to, 1) Instructions	ing received Bid Package No. 1.4 containing a full set of Contract Doct to Bidden (Proposers), 2) General Conditions, 3) Special Conditions, 4) C
Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an EDS Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are tr	and affirms that the partnership shall be bound by all t	e terms and conditions contained in the	hat all certifications and statements contained in the EDS are true, ibenited on-line; and (3) further warrants that, as of the date of sub-	Plans or Drawings (if applicable) 5) Detailo	I Specifications or Scope of Services, Evaluation Selection Criteria and Su Pages, 7) Certifications and 8) Addenda Nos. (2000c unless indicated
complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of su	Contract Documents, regardless of whether a complete set thereof is attached to t the nartnership has taken express written exception thereto in the sections of this se		nges in Circumstances since the date that the EDS was submitted t	, and afferm that the	Joint Venture shall be bound by all the terms and conditions contained
proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted to any certification in the EDS false, inaccurate or incomplete.			curate or incomplete.	Contract Documents, regardless of whether	a complete set thereof is attached to this proposal, except only to the extenception thereto in the sections of this specification designated for that pu
Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership	Under penalty of perjury, the undersigned: (1) warrants that he'she was author Disclosing Party on-line: (2) warrants that all certifications and statements cor	ized to submit an EDS on behalf of the	orn deposes and says on eath that no disclosures of ownership inte	and the second second second second	
withheld and the information provided therein to the best of its knowledge is current and the undersigned in	complete as of the date the EDS was submitted on-line; and (3) further warrant	that, as of the date of submission of this	therein to the best of its knowledge is current and the undersigned roposer) or prospective bidder (proposer) or with any other person.	Under penalty of perjury, the undersigned	t (1) warrants that holde was authorized to submit an EDS on behalf all certifications and statements contained in the EDS are true, accur-
my agreement with any other bidder (proposer) or prospective bidder (proposer) or with any other corporation relating to the price named in this proposal or any other proposal, nor any agreement or arrangement.	proposal or bid, there have been no changes in Circumstances since the date that any certification in the EDS false, inaccurate or incomplete.	the EDS was submitted that would render	in this proposal or any other proposal, nor any agreement or arrang se competition among bidders (proposers) and has not disclosed to	complete as of the date the EDS was subm	sitted on-line; and (3) further warrants that, as of the date of submission
any act or omission in restraining of free competition among bidders (proposers) and has not disclosed to an			re competition among bidders (proposers) and has not disclosed to sal) or the price named herein.		s in Circumstances since the date that the EDS was submitted that would
corporation the terms of this bid (proposal) or the price named herein.	Further, the undersigned being duly sworn deposes and says on eath that no dis withheld and the information provided therein to the best of its knowledge is curre	losures of ownership interests have been	nal signatures in the space provided. Proposals not properly signer		
Proposals must be submitted with original signatures in the space provided. Proposals not properly signed to	withheld and the information provided therein to the best of its knowledge is curre any agreement with any other bidder (proposer) or prospective bidder (prop	n and the undersigned has not entered into oser) or with any other person, firm or	nut regressives in the space provided. Proposats not properly signer		deposes and says on oath that no disclosures of ownership interests has
NAME OF CORPORATION:	corporation relating to the price named in this proposal or any other proposal, nor	my agreement or arrangement under which		withheld and the information provided there are accorded with any other hidder (m	in to the best of its knowledge is current and the undersigned has not enter conoser) or prospective bidder (proposer) or with any other person.
(Print or Type)	any act or omission in restraining of free competition among bidders (proposers) a cornoration the terms of this bid (proposal) or the price named herein.	nd has not disclosed to any person, firm or	(Signature)	corporation relating to the price named in th	is proposal or any other proposal, nor any agreement or arrangement under
SIGNATURE OF PRESIDENT*:				any act or omission in restraining of free co corporation the terms of this bid (proposal)	impetition among bidders (proposers) and has not disclosed to any person, in the price named horses
(Or Authorized Officer) (Signature)	Proposals must be submitted with original signatures in the space provided. Propo BUSINESS NAME:	als not properly signed will be rejected.			
TITLE OF SIGNATORY:	(Print or Type)		(Print or Type)	Proposals must be submitted with original s	ignatures in the space provided. Proposals not properly signed will be rejo
(Print or Type)	BUSINESS ADDRESS:			JOINT VENTURE NAME:	
BUSINESS ADDRESS:	(Print or Type)		(Print or Type)	20131 VESTURE CORE	(Print or Type)
(Print or Type)  *Note: In the event that this bid (proposal) is signed by other than the President, attach hereto a certif	If you are operating under an assumed name, provide County registration numb Revised Statutes 1965 Chapter 96 Sec. 4 et seq.	r herein under as provided in the Illinois	assumed name, provide County registration number herein under as a 1965 Chapter 96 Sec. 4 et sea.	JOINT VENTURE ADDRESS:	
that section of Corporate By-Laws or other authorization, such as a resolution by the Board of Disec-			100 CO 10	JOENI VENTURE ADDRESS.	(Print or Type)
permits the person to sign the offer for the Corporation. ATTEST:	Registration Number: SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE PARTNERSE		(Print or Type)	If you are operating under an assure	sed name, provide County registration number herein under as provided
(Corporate Secretary Signature)	(If all General Partners do not sion, indicate authority of partner signatories by a		(1)	in the Illinois Revised Statutes 196	5 Chapter 96 Sec. 4 et seq.
(Affix Corporate Scall)	other authorizing document):			Registration Number: SIGNATURES AND ADDRESSE	S OF ALL MEMBERS OF THE JOINT VENTURE
	Partner Signature: (Signature)			(If all members of the Joint Ventur	e do not sign, indicate authority of signatories by attaching copy of Joint.
County of	Address:		ndged before me on thisday of, 20 by as President (or other authorized officer) and	Venture agreement or other authori	zing document):
This instrument was acknowledged before me on thisday of, 20by	(Print or Type) Partner Signature:		(Corporation Name).	SIGNATURE OF	
as President (or other authorized officer) and	(Signature)			Authorized Party:	(Signature)
	Address: (Print or Type)			TITLE OF SIGNATORY:	(organization)
Secretary of(Corporation Name).	Partner Signature:				(Print or Type)
	(Signature)		prop	BUSINESS ADDRESS:	
Sotary Public Signature Commission Expires:	(Print or Type)			ATTEST:	(Print or Type)
Commission Capture	State of County of				(Joint Venture Secretary Signature)
				OR	(Affix Joint Venture Scal)
CMAR Federally Funded Instructions and Execution Documents	This instrument was acknowledged before me on this as President (or other authorized officer)	day of, 20 by	1	Joint Venturer	
Ferninal 3 Improvements Bid Package No.: 1.4 S	Secretary of (Corporation Name).	na as	Instructions and Execution Documents	Signature:	Eddardon B.
	(Seal)		Bid Package No. 1.4	Address: (S	ignature)
1	Notary Public Signature			0	rint or Type)
	Commission Expires:				
				CMS Extents Factor	Induction and Francisco Decements
	CMAR Federally Funded Instructions and Execution Documents				

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36.



## PROCUREMENT – SCHEDULE B: AFFIDAVIT OF DBE/NON-DBE **JOINT VENTURE**

Complete and return with your bid.

Include as an attachment on Building Connected

### SCHEDULE B: Affidavit of DBE/Non-DBE Joint Venture (FTA, FHWA and FAA Funded Contracts)

Note: If all joint venturers are DBEs, a written joint venture agreement between the DBE venturers may be submitted in lieu of this form. In all proposed joint ventures, each DBE venturer must submit a copy of its current Letter of Certification

REFER TO YOUR JOINT VENTURE AGREEMENT EXCEPT TO EXPAND ON ANSWERS PROVIDED ON THIS FORM. IF

I.	Name of joint venture:
	Address of joint venture:
	Phone number of joint venture:
II.	Identify each non-DBE venturer(s):
	Name of Firm:
	Address:
	Phone:
	Contact person for matters concerning DBE compliance:
III.	Identify each non-DBE venturer(s):
	Name of Firm:
	Address:
	Phone:
	Contact person for matters concerning DBE compliance:
IV.	Describe the role(s) of the DBE venturer(s) in the joint venture:
	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
V.	Attach a copy of the joint venture agreement. In order to demonstrate the DBE venturer's share in the ownership, control, management responsibilities, risks and profits of the joint venture, the proposed joint venture agreement must include specific
	details related to: (1) the contributions of capital and equipment; (2) work items to be performed by the DBE's own forces; (3)
	work items to be performed under the supervision of the DBE venturer; and (4) the commitment of management, supervisory
	and operative personnel employed by the DBE to be dedicated to the performance of the project.
VI.	
	A. What are the percentage(s) of DBE ownership of the joint venture?
	DBE ownership percentage(s) Non-DBE ownership percentage(s)
	Non-DBE ownership percentage(s)
	B. Specify DBE percentages for each of the following (provide narrative descriptions and other details as applicable):
	1. Profit and loss sharing:
	Capital contributions:
	(a) Dollar amounts of initial contribution:  (b) Dollar amounts of anticipated on-going contributions:
	(b) Dona amounts of and open on-going conditions.
CMA	AR Federally Funded Instructions and Execution Documents
Term	inal 3 Improvements Rid Package No : 1 1 S5-25

# PROCUREMENT – SCHEDULE C: DBE LETTER OF INTENT TO PERFORM AS A SUBCONTRACTOR OR SUPPLIER

Complete and return with your bid.

	sc	HEDULE C	
	DBE	Letter of Intent to	
		Subcontractor or Supplier	
Project Name:		Bid Package No.:	
From:			
	(Name of DBE Firm)		
To:			and the City of Chicago.
	(Name of Prime Contractor)		
The DBE status of the unders Certification Letter	signed is confirmed by t	he attached City of Chicago or Illi	inois Uniform Certification Progra
		g services in connection with the oposed scope of work and/or pa	
The above described perform	ance is offered for the fo	ollowing price and described terms	of payment:
Pay Item No./De	<u>escription</u>	Quantity/Unit Price	<u>Total</u>
		Grand	1 Total: \$
Partial Pay Items For any of the above items that	at are partial pay items s	Grand specifically describe the work and	I Total: \$subcontract dollar amount(s):
	at are partial pay items s	specifically describe the work and	subcontract dollar amount(s):
SUB-SUBCONTRACTING LE A zero (0) must be shown in e schedule.  % of the dollar value.	EVELS sach blank if the DBE wi	specifically describe the work and	subcontract dollar amount(s):  I Total: \$ work listed or attached to this n-DBE contractors.
SUB-SUBCONTRACTING LE A zero (0) must be shown in e schedule. % of the dollar valu % of the dollar valu NOTICE: If any of the DBE s explanation, description an the undersigned will enter into	EVELS sach blank if the DBE will le of the DBE subcontra le of the DBE subcontra scope of work will be s d pay item number of t o a formal written agree	Grand I not be subcontracting any of the	work listed or attached to this n-DBE contractors. Te contractors. The vendor and attach a brief ted. The contractor, conditions as a Prime Contractor, conditions
SUB-SUBCONTRACTING LE A zero (0) must be shown in e schedule.  % of the dollar valu  NOTICE: If any of the DBE s explanation, description and The undersigned will enter int upon your execution of a cont the CMAR.	EVELS each blank if the DBE will be of the DBE subcontra ue of the DBE subcontra scope of work will be s d pay item number of t o a formal written agree ract with the CMAR, wit	Grand If not be subcontracting any of the ct that will be subcontracted to not that will be subcontracted to DB ubcontracted, list the name of the work that will be subcontracted ment for the above work with you.	work listed or attached to this n-DBE contractors. The vendor and attach a brief ted. as a Prime Contractor, conditioner receipt of a signed contract from
SUB-SUBCONTRACTING LE A zero (0) must be shown in e schedule.  % of the dollar valu  NOTICE: If any of the DBE s explanation, description and The undersigned will enter int upon your execution of a cont the CMAR.	EVELS seach blank if the DBE will be of the DBE subcontral be of the DBE will be of the DBE subcontral be	Grand I not be subcontracting any of the ct that will be subcontracted to not that will be subcontracted to DB ubcontracted, list the name of the work that will be subcontractent for the above work with you inin three (3) business days of you	work listed or attached to this n-DBE contractors.  Te contractors.  The vendor and attach a brief ted.  The contractor of a signed contract from the contract of the contract
SUB-SUBCONTRACTING LE A zero (0) must be shown in e schedule.  % of the dollar valu % of the dollar valu % of the dollar valu nOTICE: If any of the DBE s explanation, description an the undersigned will enter int upon your execution of a cont the CMAR. NOTICE: THIS SCHEDULE A (Signature of President/Owner/C	EVELS seach blank if the DBE will be of the DBE subcontral be of the DBE will be of the DBE subcontral be	Grand I not be subcontracting any of the ct that will be subcontracted to not that will be subcontracted to DB ubcontracted, list the name of the work that will be subcontractent for the above work with you inin three (3) business days of you	work listed or attached to this n-DBE contractors.  Te contractors.  The vendor and attach a brief ted.  The contractor of a signed contract from the contract of the contract
SUB-SUBCONTRACTING LE A zero (0) must be shown in e schedule. % of the dollar valu % of the dollar valu NOTICE: If any of the DBE s explanation, description and The undersigned will enter int upon your execution of a cont the CMAR. NOTICE: THIS SCHEDULE A	EVELS seach blank if the DBE will be of the DBE subcontral be of the DBE will be of the DBE subcontral be	Grand I not be subcontracting any of the ct that will be subcontracted to not that will be subcontracted to DB ubcontracted, list the name of the work that will be subcontractent for the above work with you inin three (3) business days of you	work listed or attached to this n-DBE contractors.  Te contractors.  The vendor and attach a brief ted.  The contractor of a signed contract from the contract of the contract

# PROCUREMENT – SCHEDULE D: AFFIDAVIT OF PRIME CONTRACTOR REGARDING DISADVANTAGED BUSINESS ENTERPRISE (DBEs)

Complete and return with your bid.

DPS Version 04/25/2017		
	SCHEDULE D  Affidavit of Prime Contractor ng Disadvantaged Business Enterprises (DBEs) (FTA/FHWA and FAA Funded Projects)	
Project Name:		
Department Project No.:		
Bid Package No.:		
State of		
County (City) of	) :ss )	
In connection with the above	captioned contract, I HEREBY DECLARE AN and duly authorized representative of	ND AFFIRM that I am th
(Title of Affiant)	and duly authorized representative or	
(	(Name of Prime Contractor)	
Names of DBE Firms	Type of Work to be Performed	Credit Toward
rames of DDL Titles	(in accordance with Schedule Cs)	DBE Goal
Traines of BBE 1 mms	(in accordance with Schedule Cs)	DBE Goal
141116 01 252 1 21 113	(in accordance with Schedule Cs)	
- Marie of BEE 1 mile	(in accordance with Schedule Cs)	DBE Goal
- Marks of SEE Table	(in accordance with Schedule Cs)	DBE Goal
- Market of SEC 1 and	(in accordance with Schedule Cs)	DBE Goal  S S
- Marie St SSE Tallis	(in accordance with Schedule Cs)	DBE Goal  S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S
	(in accordance with Schedule Cs)	DBE Goal  S S S S S S S S S S S S S S S S S S

## PROCUREMENT – SCHEDULE F: REPORT OF SUBCONTRACTOR SOLICITATIONS

Complete and return with your bid.

	E F: Report of Subcontractor Solicitations
(	FHWA, FTA and FAA Funded Contracts)
	Project Name: Specification #:
_	Specification #:
[,(Name of reporter)	on behalf of(Prime contractor)
have either personally solicited, or p	ermitted a duly authorized representative of this firm to solicit, work for ctors which comprise all DBE and non-DBE subcontractors who bid or que
Name of Subcontractor	
Address of Subcontractor	
	□Yes □ No
Type of Work Solicited	
Years in Business (if available)	
Name of Subcontractor	
Address of Subcontractor	
Contact Person	
	□Yes □ No
Type of Work Solicited	
Years in Business (if available)	
Years in Business (if available) Annual Gross Receipts (if available)	
Name of Subcontractor	
Name of SubcontractorAddress of Subcontractor	
Name of Subcontractor	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified?	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available)	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified?	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Annual Gross Receipts (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Contact Person	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Contact Person	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Name of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified?	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	

## PROCUREMENT – EXHIBIT A DBE REQUIREMENT FOR BIDDER/PROPOSER LIST

Complete and return with your bid.

Include as an attachment on Building Connected.

	ersion 04/25/2017	EXHIBIT A
	DBE I	REQUIREMENT FOR BIDDER/PROPOSER LIST
bidd requ on th	ing or proposing on pro ested to provide a list of his contract. Failure to c	The CMAR is required to maintain a bidders list, consisting of all finine contracts and bidding or quoting subcontracts. The bidder/proposer fall DBE <u>AND non-DBE subcontractors</u> who bid or quote price information to operate may result in the bidder/proposer being deemed non-responsive proposer is requested to provide the following information:
Prim	e Contractor (Including	all partners to a Joint Venture, if applicable)
	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	
Subo	contractors (all DBE AN	ID non-DBE subcontractors)
1.	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	
2.	Name:	
	Address:	
	Address:	
	City, State, Zip:	

Instructions and Execution Documents

\$5-41

CMAR Federally Funded

## PROCUREMENT – DBE UTILIZATION REPORT

Complete and return with your bid.

DPS Version 04/25				
		DBE Utilization	Report	
NOTICE:	AWARDED A CONTRA BE REQUIRED TO SUB	T TO BE COMPLETED AT CT WITH AN APPROVED DB MIT THIS REPORT IN ACCORD NDITION REGARDING DISAL MENT.	E/MBE/WBE PLAN, THE ANCE WITH THE REPORT	PRIME CONTRACTOR WILL ING REQUIREMENTS STATED
Contract Adm	inistrator:		Bid Package No.	
			Date of Award:	
STATE OF:	(	)	Utilization Report N	o
COUNTY (C	ITY) OF: (	)		
In connection	with the above-captione	d contract:		
I HEREBY D	ECLARE AND AFFIRM	I that I am the		
and duly auth	orized representative of		(Title - Print or Type)	
and that the f	(Address of C following Disadvantaged	ompany) , Minority and Women Busi	(Name of Comp any - Print or Typ	(Phone) en contracted with, and have
and that the f furnished, or a	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref	ompany)	(Name of Comp any - Print or Typenson of Comp and	(Phone) en contracted with, and have ontract agreement.
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref	ompany) , Minority and Women Busi ing materials for, and renderi	(Name of Comp any - Print or Ty)  changes Enterprises have been g services stated in the co	(Phone) en contracted with, and have ontract agreement.
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date. BE/WBE Firm Name	ompany) , Minority and Women Busing materials for, and renderial lects the value of each DBE/ Indicate Type of Firm	(Name of Comp any - Print or Ty)  compass Enterprises have been general services stated in the compass of the c	(Phone) n contracted with, and have outract agreement. it and the amounts of money  Amount Paid To-Date
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date. BE/WBE Firm Name	ompany) , Minority and Women Busing materials for, and renderial lects the value of each DBE/  Indicate Type of Firm (DBE/MBE/WBE)	(Name of Comp any - Print or Ty)  compass Enterprises have been general services stated in the compass of the c	(Phone) n contracted with, and have outract agreement. it and the amounts of money  Amount Paid To-Date
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date. BE/WBE Firm Name	ompany) , Minority and Women Busing materials for, and renderial lects the value of each DBE/  Indicate Type of Firm (DBE/MBE/WBE)	(Name of Comp any - Print or Ty)  compass Enterprises have been general services stated in the compass of the c	(Phone) n contracted with, and have outract agreement. it and the amounts of money  Amount Paid To-Date
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date. BE/WBE Firm Name	ompany) , Minority and Women Busing materials for, and renderial lects the value of each DBE/  Indicate Type of Firm (DBE/MBE/WBE)	(Name of Comp any - Print or Ty)  compass Enterprises have been general services stated in the compass of the c	(Phone) n contracted with, and have outract agreement. it and the amounts of money  Amount Paid To-Date
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date. BE/WBE Firm Name	ompany) Minority and Women Busing materials for, and renderi lects the value of each DBE/  Indicate Type of Firm (DBE/MBE/WBE)	(Name of Comp any - Print or Ty)	(Phone) n contracted with, and have ontract agreement. It and the amounts of money  Amount Paid To-Date  \$
and that the f furnished, or a The following paid to each to	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date.  BE/WBE Firm Name	ompany) Minority and Women Busing materials for, and renderi lects the value of each DBE/  Indicate Type of Firm (DBE/MBE/WBE)	(Name of Comp any - Print or Ty)	(Phone) n contracted with, and have ontract agreement. It and the amounts of money  Amount Paid To-Date  \$
and that the f furnished, or i  The following paid to each to  DBE/ME	(Address of C following Disadvantaged are furnishing and prepar g Schedule accurately ref o date.  BE/WBE Firm Name	ompany)  Minority and Women Busing materials for, and renderi lects the value of each DBE/  Indicate Type of Firm (DBE/MBE/WBE)	(Name of Comp any - Print or Ty)  (Lease SEnterprises have been generally services stated in the composition of the composition	(Phone) m contracted with, and have outract agreement. it and the amounts of money  Amount Paid To-Date  \$

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions



## PROCUREMENT – SCHEDULE 1 AFFIDAVIT OF NON-COLLUSION

Complete and return with your bid.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175
Construction Management At-Risk Services for O'Hare 21 at O'Hare international Airport Chicago Department of Aviation (Specification No.1258275)
SCHEDULE 1
AFFIDAVIT OF NON-COLLUSION
STATE OF ILLINOIS }
SS COUNTY OF COOK }
, being first duly sworn, deposes and says that:
(1) He/She is
of
(Owner, Partner, Authorized Officer, or Representative or Agent)
(Name of Organization/Firm)
the Bidder that has submitted the attached Bid;
<ul> <li>(2) That Bidder is fully informed respecting the preparation and contents of the attached Bid and of all pertinent circumstances respecting such Bid;</li> <li>(3) Such Bid is genuine and is not a collusive or sham bid;</li> <li>(4) Neither Bidder nor any of its officers, partners, owners, agents, representatives, employees, or parties in interest, including this affiant, has in any way colluded, connived, conspired, or agreed, directly or indirectly, with any other Bidder, firm, or person to submit a collusive or sham bid in connection with the Contract for which the attached bid has been submitted or to refrain from bidding in connection with such Contract, or has in any manner, directly or indirectly, sought by agreement or collusion or communication or conference with any other Bidder, firm, or person to fix the price or prices in the attached bid or in that of any other Bidder, or to fix any overhead, profit, or cost element of the bid price of any other Bidder, or to secure through any collusion, conspiracy, connivance or unlawful agreement any advantage against the City of Chicago or any person interested in the proposed Contract; and</li> <li>(5) The price or prices quoted in the attached Bid are fair and proper and are not tainted by any collusion, conspiracy, connivance, or unlawful agreement on the part of the Bidder or any of its agents, representatives, owners, employees, or parties in interest, including this affiant.</li> <li>(6) The Bidder is not barred from bidding as a result of having violated Illinois Criminal Code, 720 ILCS 5/33E-3 (Bid-rigging), 720 ILCS 5/33E-4 (Bid rotating) or the Prevailing Wage Act, 30 ILCS 570/0.01 through 570/7.</li> </ul>
(Signed)
(Title)
Exhibit D to the Agreement D-28   Page Required Subcontract Provisions

PROCUREMENT – SCHEDULE 2 regulations of the department of procurement services for percentages of City and Project Area Residents working hours

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

### REGULATIONS OF THE DEPARTMENT OF PROCUREMENT SERVICES FOR PERCENTAGES OF CITY AND PROJECT AREA RESIDENTS WORKING HOURS

### GENERAL PROVISIONS

### 1. Statement of Authority

These regulations are issued pursuant to the following Section of the Municipal Code

Section 2-92-330 of Municipal Code of Chicago establishes a minimum number of hours to be performed by City Residents as well as a minimum number of hours to be performed by Project Area residents. Subsection (a) requires the Chief Procurement Officer to "develop standards and procedures for reducing or waiving these minimum percentages level of Chicagoans work hours for eligible residents when a bidder or contractor can demonstrate the impracticality or excessive cost of complying with these percentage levels for particular contracts or classes of employees." Subsection (f) authorizes the Chief Procurement Officer to "adopt, promulgate and enforce reasonable rules and regulations pertaining to the administration and enforcement" of

Subsection (a) provides that, for any construction project advertised, or if not advertised, awarded, by the City that has an estimated contract value of \$100,000 or more, and where not otherwise prohibited by federal, state or local law, the total hours worked by persons on the site of the construction project by employees of the contractor and subcontractors shall be performed (i) at least 50 percent by City Residents; and (ii) at least 7.5 percent by Project Area residents. Work hours performed by Project Area residents shall be considered to be work hours performed by City Residents for purposes of calculating the minimum work hour percentage required to be performed by City Residents.

### 2. Application and Statement of Purpose

These regulations describe how the ordinance will be administered and enforced, including the right of the Chief Procurement Officer to waive the residency

### DEFINITIONS

Unless otherwise specified, whenever used in these regulations, the following terms have the following meanings:

"City Residents" means persons domiciled within the City of Chicago.

Exhibit D to the Agreement Required Subcontract Provisions D-30 | Page

# PROCUREMENT – SCHEDULE 4 STATEMENT OF BIDDER'S QUALIFICATIONS

Complete and return with your bid.

		Construction Management		Hare 21 at O'Hare International Airpo of Aviation (Specification No.125827
	CHEDULE 4 FATEMENT OF BIDDE	R'S QUALIFICATIONS		
	the request of the City, the pability of the Bidder to pe	e Bidder shall also submit a erform the Contract.	additional infor	mation regarding the
В	idder:			
S	ubmitted By:	5		
T	itle:	<u>-</u>		
P	ermanent Main Office Ad	dress:		
L	ocal Address:			
	ocal Telephone No. and F.	ax Number:	k of this nature	?
Ho	ow many years operating a	s Trade Contractor for work	lue and scope o	f work:
Ho	ow many years operating a st of recently completed co	s Trade Contractor for work	lue and scope o	
Lis	ow many years operating a st of recently completed co	s Trade Contractor for work	lue and scope o	f work:
Lis 1. 2. 3.	st of recently completed co	s Trade Contractor for work	lue and scope o	f work:
List 1. 2. 3. 4.	st of recently completed co	s Trade Contractor for work	lue and scope o	f work:
Lis 1. 2. 3.	st of recently completed co	s Trade Contractor for work	lue and scope o	f work:
Lis 1. 2. 3. 4. 5.	st of recently completed co	s Trade Contractor for work	lue and scope o	f work:
Lis 1. 2. 3. 4. 5. 6.	st of recently completed co	s Trade Contractor for work	lue and scope o	f work:
Lis 1. 2. 3. 4. 5. 6. 7.	st of recently completed co	s Trade Contractor for work ontracts of similar dollar va  Dollar Amount	Year of Contract	Nature of Project
Lis 1. 2. 3. 4. 5. 6. 7. 8.	st of recently completed co	s Trade Contractor for work	Year of Contract	Nature of Project  Furnish any information
List 1. 2. 3. 4. 5. 6. 7. 8. The reco	st of recently completed co	Dollar Amount  Dorizes any person, firm, or cago in verification of this s	Year of Contract	Nature of Project  Furnish any information

# PROCUREMENT – SCHEDULE 5 CERTIFICATE OF FILING ON-LINE ECONOMIC DISCLOSURE (EDS) STATEMENTS AND AFFIDAVIT

The bidder shall complete an online EDS prior to the bid due date. A bidder who does not file an electronic EDS prior to the bid due date may be found non-responsible and its bid rejected. If you are unable to complete the online EDS and print a Certificate of Filing prior to the bid/proposal due date, the City will accept a paper EDS provided written justification is submitted with the bid/proposal explaining the Bidder's good faith efforts to complete it before the bid/proposal due date and the reasons why on line EDS could not be completed



Hard copy to be submitted with your bid but do NOT need to submit electronically pior to bid. Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

### SCHEDULE 5

### INSTRUCTIONS FOR COMPLETING ECONOMIC DISCLOSURE STATEMENT AND AFFIDAVIT (EDS) ON-LINE

The Bidder shall complete an online EDS prior to the bid due date. A Bidder who does not file an electronic EDS prior to the bid due date may be found non-responsive and its bid rejected. If you are unable to complete the online EDS and print a Certificate of Filing prior to the bid/proposal due date, the City will accept a paper EDS provided written justification is submitted with the bid/proposal explaining the Bidder's good faith efforts to complete it before the bid/proposal due date and the reasons why on line EDS could not be completed.

### 1.1. ONLINE EDS FILING REQUIRED PRIOR TO BID OPENING

The Bidder must complete an online EDS prior to the bid opening date.

A Bidder that does not file an electronic EDS prior to the bid opening will be found nonresponsive and its bid will be rejected, unless a paper EDS and justification is submitted with the bid as described above. Paper EDS forms may be obtained on the City's wesite at: http://www.cityofchicago.org/city/en/depts/dps/provdrs/comp/svcs/economic\_disclosurestate mentseds.html

### 1.2. ONLINE EDS WEB LINK

The web link for the Online EDS is https://webapps.citvofchicago.org/EDSWeb

### 1.3. ONLINE EDS NUMBER

Upon completion of the online EDS submission process, the Proposer will be provided an EDS number. Bidders should provide this number here:

EDS Number:

### 1.4. ONLINE EDS CERTIFICATION OF FILING

Upon completion of the online submission process, the Proposer will be able to print a hard copy Certificate of Filing. The Proposer should submit the signed Certificate of Filing with its bid. Please insert your Certification of Filing following this page.

A Proposer that does not include a signed Certificate of Filing with its bid must provide it upon the request of the Chief Procurement Officer.

### 1.5. PREPARATION CHECKLIST FOR REGISTRATION

To expedite and ease your registration process, we recommend that you collect the following information prior to registering for an Online EDS user account:

Exhibit D to the Agreement Required Subcontract Provisions D-38 | Page

# PROCUREMENT – SCHEDULE 6 CONTRACTOR'S PERFORMANCE & PAYMENT BOND RIDER ATTACHED

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 6 CONTRACTOR'S PERFORMANCE AND PAYMENT BOND RIDER ATTACHED

### CONTRACTOR'S PERFORMANCE & PAYMENT BOND

Know All Men by these Presents, That we,

COMPANY NAME STREET ADDRESS CITY, STATE ZIP CODE

Principal, hereinafter referred to as Contractor, and , Surety of the County of and State of , are held and firmly bound unto the CITY OF CHICAGO in the penal sum of:

--- Dollar Amount in Words and 00/100 Dollars (\$ ) ---

lawful money of the United States, for the payment of which sum of money, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

Sealed with our seals and dated this

day o

, 20 .

The Condition of the Above Obligation is such, that whereas the above bounden Contractor has entered into a certain contract with the City of Chicago, bearing

Contract (PO) No. XXXXX and Specification No. XXXXXX all in conformity with said contract, for,

Furnishing the City of Chicago, Name of User Department, all labor, tools, material, and equipment required and necessary for the project known as:

### PROJECT DESCRIPTION

\* The attached rider is incorporated herein by reference.

Now, if the said Contractor shall in all respects well and truly keep and perform the said contract on its part, in accordance with the terms and provisions of all of the Contract Documents comprising said contract, and in the time and manner therein prescribed, and further shall save, indemnify, and keep harmless the City of Chicago against all loss, damages, claims, liabilities, judgments, costs and expenses which may in anywise result stere from, or which may insult from strict liability, or said contract, or which may in anywise result therefrom, or which may result from strict liability, or which may in anywise result from any injuries to, or death of, any person, or damage to any real or personal property, arising directly or indirectly from or in connection with, work performed or to be performed under said contract by said Contractor, its Agents, Employees or Workmen, assignees, subcontractors, or anyone else, in any respect whatever, or which may result on account of any infringement of any patent by reason of the materials, machinery, devices or apparatus used in the performance of said contract, and moreover, shall pay to said City any sum or sums of money determined by the Purchasing Agent, and/or by a court of competent jurisdiction, to be due said City by reason of any failure or neglect in the performance of the requirements of said contract, wherefore the said Purchasing Agent shall have elected to suspend or cancel the same, and shall pay all claims and demands whatsoever, which may accrue to each and every materialman and subcontractor, and to each and every person who shall be employed by the said Contractor or by its assignees and subcontractors, in or about the performance of said contract, and with wages paid at prevailing wage rates if so required by said contract, and shall insure its liability to pay the compensation, and shall pay all claims and demands for compensation which may accrue to each and every person who shall be employed by them

Exhibit D to the Agreement
Required Subcontract Provisions

D-461Page

## PROCUREMENT – SCHEDULE 7 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE CONSTRUCTION PROJECTS

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

## SCHEDULE 7 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE CONSTRUCTION PROJECTS

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with its proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101, BABA and other related Made in America Laws, U.S. statutes, guidance, and FAA policies, by selecting one of the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (i.e., not both) by inserting a checkmark (\*) or the letter "X".

- □ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related U.S. statutes, guidance, and policies of the FAA by:
  - a) Only installing iron, steel and manufactured products produced in the United States;
  - b) Only installing construction materials defined as: an article, material, or supply other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials; aggregates such as stone, sand, or gravel; or aggregate binding agents or additives that are or consist primarily of non-ferrous metals; plastic and polymer-based products (including polyvinylchloride, composite building materials, and polymers used in fiber optic cables); glass (including optic glass); lumber or drywall that have been manufactured in the United States.
  - Installing manufactured products for which the Federal Aviation Administration (FAA)
    has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy
    American Waivers Issued listing; or
  - d) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- To provide to the Airport Sponsor or the FAA evidence that documents the source and origin of the iron, steel, and/or manufactured product.
- b) To faithfully comply with providing U.S. domestic products.
- c) To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.
- d) Certify that all construction materials used in the project are manufactured in the U.S.
- □ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:
  - a) To the submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the responsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested.

Exhibit D to the Agreement
Required Subcontract Provisions

D-51 | Page

## PROCUREMENT – SCHEDULE 8 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – EQUIPMENT/BUILDING PROJECTS

Complete and return with your bid.

Include as an attachment on Building Connected.

## SCHEDULE 8 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – EQUIPMENT/BUILDING PROJECTS

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with their proposal. The bidder or offeror must indicate how they intend to comply with 49 USC § 50101, and other Made in America Laws, U.S. statutes, guidance, and FAA policies by selecting one on the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (not both) by inserting a checkmark ( $\checkmark$ ) or the letter "X".

- □ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related U.S. statutes, guidance, and policies of the FAA by:
  - a) Only installing steel and manufactured products produced in the United States;
  - b) Only installing construction materials defined as: an article, material, or supply other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials; aggregates such as stone, sand, or gravel; or aggregate binding agents or additives that are or consist primarily of non-ferrous metals; plastic and polymer-based products (including polyvinylchloride, composite building materials, and polymers used in fiber optic cables); glass (including optic glass); lumber or drywall that have been manufactured in the United States.
  - Installing manufactured products for which the Federal Aviation Administration (FAA) has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing; or
  - Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- To provide to the Airport Sponsor or FAA evidence that documents the source and origin of the steel and manufactured product.
- To faithfully comply with providing U.S. domestic product.
- To furnish U.S. domestic product for any waiver request that the FAA rejects.
- To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.
- □ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for a Type 3 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:
  - a) To submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the responsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested.

Exhibit D to the Agreement Required Subcontract Provisions D-54 Page

## PROCUREMENT – SCHEDULE 9 CERTIFICATION REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

### SCHEDULE 9 CERTIFICATION REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

The applicant must complete the following two certification statements. The applicant must indicate its current status as it relates to tax delinquency and felony conviction by inserting a checkmark  $(\checkmark)$  in the space following the applicable response. The applicant agrees that, if awarded a contract resulting from this solicitation, it will incorporate this provision for certification in all lower tier subcontracts.

#### Certifications

- 1) The applicant represents that it is ( ) is not ( ) a corporation that has any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.
- The applicant represents that it is ( ) is not ( ) is not a corporation that was convicted of a criminal violation under any Federal law within the preceding 24 months.

#### Note

If an applicant responds in the affirmative to either of the above representations, the applicant is ineligible to receive an award unless the sponsor has received notification from the agency suspension and debarment official (SDO) that the SDO has considered suspension or debarment and determined that further action is not required to protect the Government's interests. The applicant therefore must provide information to the owner about its tax liability or conviction to the Owner, who will then notify the FAA Airports District Office, which will then notify the agency's SDO to facilitate completion of the required considerations before award decisions are

### **Term Definitions**

Felony conviction: Felony conviction means a conviction within the preceding twentyfour (24) months of a felony criminal violation under any Federal law and includes conviction of an offense defined in a section of the U.S. code that specifically classifies the offense as a felony and conviction of an offense that is classified as a felony under 18 U.S.C. 8 3559.

Tax Delinquency: A tax delinquency is any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted, or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.


Exhibit D to the Agreement Required Subcontract Provisions D-57 I Pag

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification, Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



## PROCUREMENT – AFFIDAVIT OF UNCOMPLETED WORK



## SUBMIT WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED, SIGNED AND NOTARIZED

(BAM, CAM, PAM)	1					THE WORK	1				SUBCON	TRACTOR	1.1		1	1		1
AGGREGATE BASE AND FILL						D					TYPE OF	WORK	+				_	
FOUNDATION						rK.							$\perp$					
(CAISSON & PILE)						ST.					SUBCON	TRACT PRICE						
HIGHWAY						AL					AMOUNT	UNCOMPLETED	$\Box$					
STRUCTURES SEWER & DRAIN		_			_	CAULKING	_						_					
STRUCTURES						CAULKING					I. bein	g duly sworn do hereby	declare	e that this affida	avit is a true and co	rrect statement relatin	g to ALL uncomple	ted contracts
PAINTING						ous					of the	undersigned for Federal	, State,	County, City a	nd private work in			
PAVEMENT MARKING						1	_				not yet	awarded or rejected, as	nd AL	estimated com	pletion dates.			
						<b>⅃</b> 【					Subscr	ibed and sworn to before	re me	Sie	oned			
SIGNING												day of		20 Co	mpany			
LANDSCAPING						1					_		- 1	Ad	dress			
DEMOLITION					_	<b>↓</b>					My co	mmission expires	$\dashv$					
						1							- 1					
FENCING						11							- 1					
				 	_	- <del> </del>					_		- 1					
										-	_		- 1					
										- 1			- 1					
										- 1	CMAR	Federally Funded I 3 Improvements	- 1	Instru	ctions and Execution Do		S5-45	
CMAR Federally Funded		Instructions and Execu								- 1	Termina	1 3 Improvements	- 1		Bid Package No.: 1.4		83-43	
Terminal 3 Improvements		Bid Package N	o.: 1.4		S5-43					- 1			- 1					
										- 1			- 1					
										l			-					
													- 1					
													- 1					
					CMAR	ederally Funded			and Execution Docu	aments			- 1					
					Termin	3 Improvements		Bid	Package No.: 1.4			S5-44	- 1					
													- 1					

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



# PROCUREMENT – CERTIFICATE REGARDING REMOVAL OF ALL WASTE MATERIALS AND IDENTIFICATION OF ALL LEGAL DUMP SITES

Complete and return with your bid. If this does not apply to your trade, mark as NA.

PHONE:  Disposal site submitted shall be of sufficient capacity as to insure acceptance of the volume of Construction and/or Demolition Debris received for the period of this Contract. These disposal sites must meet all zoning and other requirements hat may be necessary.  If requested by the Chief Procurement Officer, the Contractor shall submit copies of all contractual agreements, sanitary andfill permits and/or licenses for these disposal site(s) proposed by the Contractor.  Revised 6/30/2000)	ANDI	DENTIFICATION OF ALL LEGAL DUMP SITES	
EGAL NAME OF LANDFILL/DISPOSAL SITE:  [The Contractor must provide to the Commissioner or his/her designated representative with copies of all dump tickets, nanifests, etc.)  [OCATION ADDRESS:	Contractor to show here the name	and location of the ultimate disposal site he/she is proposing to use for the subject proje	ect:
(The Contractor must provide to the Commissioner or his/her designated representative with copies of all dump tickets, nanifests, etc.)  OCATION ADDRESS:	SPECIFY THE TYPE OF MATE	RIALS TO BE DISPOSED OF:	
DOCATION ADDRESS:	LEGAL NAME OF LANDFILL/I	DISPOSAL SITE:	
PHONE:  Disposal site submitted shall be of sufficient capacity as to insure acceptance of the volume of Construction and/or Demolition Debris received for the period of this Contract. These disposal sites must meet all zoning and other requirements hat may be necessary.  If requested by the Chief Procurement Officer, the Contractor shall submit copies of all contractual agreements, sanitary andfull permits and/or licenses for these disposal site(s) proposed by the Contractor.  Revised 6/30/2000)	(The Contractor must provide to manifests, etc.)	the Commissioner or his/her designated representative with copies of all dump tick	kets,
Disposal site submitted shall be of sufficient capacity as to insure acceptance of the volume of Construction and/or formolition Debris received for the period of this Contract. These disposal sites must meet all zoning and other requirements that may be necessary.  If requested by the Chief Procurement Officer, the Contractor shall submit copies of all contractual agreements, sanitary and fill permits and/or licenses for these disposal site(s) proposed by the Contractor.  Revised 6/30/2000)	LOCATION ADDRESS:		
Disposal site submitted shall be of sufficient capacity as to insure acceptance of the volume of Construction and/or bemolition Debris received for the period of this Contract. These disposal sites must meet all zoning and other requirements hat may be necessary.  If requested by the Chief Procurement Officer, the Contractor shall submit copies of all contractual agreements, sanitary and fill permits and/or licenses for these disposal site(s) proposed by the Contractor.  Revised 6/30/2000)	PHONE:		
Demolition Debris received for the period of this Contract. These disposal sites must meet all zoning and other requirements that may be necessary.  If requested by the Chief Procurement Officer, the Contractor shall submit copies of all contractual agreements, sanitary and fill permits and/or licenses for these disposal site(s) proposed by the Contractor.  Revised 6/30/2000)	CONTACT PERSON:		
andfill permits and/or licenses for these disposal site(s) proposed by the Contractor.  Revised 6/30/2000)			
			itary
MAR Enterplic Funded Instructions and Execution Documents	(Revised 6/30/2000)		
MAR Enterplic Funded Instructions and Execution Documents			
MAR Enterply Funded Instructions and Execution Documents			
MAR Enderally Funded Instructions and Execution Documents			
MAR Enterply Funded Instructions and Execution Documents			
MAR Enderally Funded Instructions and Execution Documents			
MAR Enderally Funded Instructions and Execution Documents			
MAR Federally Funded Instructions and Execution Documents			
SINK Peterany random instructions and account on the second instruction and account on	CMAR Federally Funded	Instructions and Execution Documents	

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification, Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



## PROCUREMENT - BIDDER'S FINANCIAL STATEMENT

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a financial statement dated not earlier then the end of said Bidder's last fiscal year period. This will be kept on file by the Construction Manager as a representative statement for a period of one year only. If a Bidder does not have such statement on file, it must submit a copy with its bid. Failure to have a current financial statement on file at the Construction Manager at time of bid opening may be cause for the rejection of the Trade Contractor's Bid

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

ensure that any contract entered into pursuant to this advertisement, disadvantaged business enterprises will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award."

### B. Affidavit of Non-Collusion

Each Bidder shall fully execute an affidavit, in the form provided, to the effect that the Bidder has not colluded with any other person, firm, or corporation in regard to any bid submitted. Such affidavit shall be attached to the bid.

### C. DBE Commitments

The goal for DBE participation for this Contract is 21% DBE.\* Each Bidder shall submit with its Bid Schedule Cs and Schedule D, affidavits and supporting documents describing the extent to which DBE firms will participate in the Contract in accordance with Schedule 3 "Special Conditions Regarding DBE Participation."

### D. Affidavit of Uncompleted Work

The Bidder is required to submit a fully executed Affidavit of Uncompleted Work, which declares, among other things, the value and estimated completion date of all uncompleted contracts to be completed with Bidder's own forces and to be subcontracted to others. Such affidavit shall be attached to the bid on the form provided.

### E. Bidder's Financial Statement

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a financial statement dated not earlier then the end of said Bidder's last fiscal year period. This will be kept on file by the Construction Manager as a representative statement for a period of one year only. If a Bidder does not have such statement on file, it must submit a copy with its bid. Failure to have a current financial statement on file at the Construction Manager at time of bid opening may be cause for the rejection of the Trade Contractor's Bid.

### F. Disclosure Affidavit

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a fully executed Disclosure Affidavit. If a Bidder does not have such statement on file, it must submit a copy with its bid.

### G. Statement of Bidder's Qualifications

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a fully executed Statement of Bidder's Qualifications or a Qualification Submittal in response to a Request for Qualifications (RFQ). Construction Manager reserves the right to request additional information regarding the capability of the Bidder to perform the Contract.

### H. Economic Disclosure Statements (EDS)

Exhibit D to the Agreement Required Subcontract Provisions D-2 Page

<sup>\*</sup> The overall contract goal for is 21% DBE, with a construction sub-goal of20%. In consultation with the City a given trade bid package may have a different DBE goal specific to that bid package, and individual subcontracts may have different DBE goals.

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification, Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents

## DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this. Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



## PROCUREMENT – FAA CERTIFICATIONS

CERTIFICATION REGARDING LOBBYING AND INFLUENCING

The Contractor certifies, to the best of his or her knowledge and belief,

to any person for influencing or attempting to influence an officer or en

of Congress, an officer or employee of Congress, or an employee of a N

connection with the awarding of any Federal contract, the making of any

any Federal loan, the entering into of any cooperative agreement, and th

renewal, amendment, or modification of any Federal contract, grant, loa

for influencing or attempting to influence an officer or employee of any

an officer or employee of Congress, or an employee of a Member of Cong

Federal contract, grant, loan, or cooperative agreement, the undersigned

If any funds other than Federal appropriated funds have been par

No Federal appropriated funds have been paid or will be paid, by

### CERTIFICATE REGARDING DEBARMENT AND SUSPENSION

By submitting a bid/proposal under this solicitation, the bidder or offeror certifies that a the bidder or offeror submits its proposal that neither it nor its principals are presently debar suspended by any Federal department or agency from participation in this transaction.

### CERTIFICATION REGARDING DEBARMENT AND SUSPENSION (SUCCESSFU REGARDING LOWER TIER PARTICIPANTS)

The successful bidder, by administering each lower tier subcontract that exceeds \$25,000 transaction", must verify each lower tier participant of a "covered transaction" under the presently debarred or otherwise disqualified from participation in this federally assisted prosuccessful bidder will accomplish this by:

- 1. Checking the System for Award Management at website: http://www.sam.gov
- 2. Collecting a certification statement similar to the Certificate Regarding Debarm Suspension (Bidder or Offeror), above.

### CERTIFICATION OF NONSEGREGATED FACILITIES

The federally-assisted construction contractor certifies that she or he does not maintain or provide, for his employees, any segregated facilities at any of his establishments and that she or he does not permit his employees to perform their services at any location, under his control, where segregated facilities are maintained. The federally-assisted construction contractor certifies that she or he will not maintain or provide, for his employees, segregated facilities at any of his establishments and that she or he will not permit his employees to perform their services at any location under his control where segregated facilities are maintained. The federally-assisted construction contractor agrees that a breach of this certification is a violation of the Equal Opportunity Clause in this contract.

As used in this certification, the term "segregated facilities" means any waiting rooms, work areas, restrooms, and washrooms, restaurants and other eating areas, time clocks, locker rooms and other storage or dressing areas, parking lots, drinking fountains, recreation or entertainment areas. transportation, and housing facilities provided for employees which are segregated by explicit directives or are, in fact, segregated on the basis of race, color, religion, or national origin because of habit, local custom, or any other reason. The federally-assisted construction contractor agrees that (except where she or he has obtained identical certifications from proposed subcontractors for specific time periods) she or he will obtain identical certifications from proposed subcontractors prior to the award of subcontracts exceeding \$10,000 which are not exempt from the provisions of the Equal Opportunity

#### IFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE -CONSTRUCTION PROJECTS

responsiveness, the bidder or offeror must complete, sign, date, and submit this certification proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101, related Made in America Laws, U.S. statutes, guidance, and FAA policies, by selecting one of ification statements. These statements are mutually exclusive. Bidder must select one or the oth) by inserting a checkmark (✓) or the letter "X".

r offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related tutes, guidance, and policies of the FAA by:

Only installing iron, steel and manufactured products produced in the United States;

Only installing construction materials defined as: an article, material, or supply - other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials;

### SUBMIT ONE (1) OF EACH FAA CERTIFICATION WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED

	Lobbying		Facilities	BABA Certification	
Debarment	CMAR Federally Finded Instructions and Execution Documents Terminal 3 Improvements Hid Package No.: 1.4	85-47	Non- Segregated	CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bird Package No.: 1.4 S5-49	
Signature of Authorized Representative  CMAR Federally Funded Instructions and Execution Documents Biol Package No.: 1.4	55	CMAR Federally Funded Terminal 3 Improvements	Instructions and Execution Documents Bid Package No.: 1.4	der or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences SC § 50101(a) but may qualify for a Type 3 or Type 4 waiver under 49 USC § 50101(b). By g this certification statement, the apparent bidder or offeror with the apparent low bid agrees: To the submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the sesponsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested. That failure to submit the required documentation within the specified timeframe is cause for a non-responsive determination that may result in rejection of the proposal. To faithfully comply with providing U.S. domestic products at or above the approved U.S. domestic content percentage as approved by the FAA. To furnish U.S. domestic product for any waiver request that the FAA rejects. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.	
Date  By  Name and Title of Authorized Representative	Business Name  Date By	Name and Title of Authorized Representative ting this certification statement, the bidder or offeror agrees:  To provide to the Airport Sponsor or the FAA evidence that documents the source at the iron, steel, and or manufactured product.			
	1	Date	My	regulation suspens 22,100.	

Lobbying

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. ☐ Bid Bond; S5-54.



## PROCUREMENT – SEXUAL HARASSMENT AFFIDAVIT

Complete and return with your bid.

Include as an attachment on Building Connected

#### SEXUAL HARASSMENT POLICY AFFIDAVIT (SECTION 2-92-612)

The policy	prohibiting	sexual	harassment	as described	l in Sectio	n 2-92-6	12 of the	Municipal	Code of	Chicago	("MCC") i	S
applicable t	o contracts	paid fro	m funds bel	onging to or	administer	ed by the	City.					

Specification #:

In accordance with requirements set forth in Section 2-92-612 of the MCC, Contractor hereby attests that Contractor has a written policy prohibiting sexual harassment in compliance with Section 6-10-040 of the MCC.

In accordance with Section 6-10-040 of the MCC, Contractor's written policy prohibiting sexual harassment shall include, at a minimum, the following information:

- (i) a statement that sexual harassment is illegal in Chicago;
- (ii) the following definition of sexual harassment: "Sexual harassment' means any (i) unwelcome sexual advances or unwelcome conduct of a sexual nature; or (ii) requests for sexual favors or conduct of a sexual nature when (1) submission to such conduct is made either explicitly or implicitly a term or condition of an individual's employment, or (2) submission to or rejection of such conduct by an individual is used as the basis for any employment decision affecting the individual, or (3) such conduct has the purpose or effect of substantially interfering with an individual's work performance or creating an intimidating, hostile, or offensive working environment; or (iii) sexual misconduct, which means any behavior of a sexual nature which also involves coercion, abuse of authority, or misuse of an individual's employment position.";
- (iii) a requirement that all employees participate in: (1) sexual harassment prevention training annually, (a) Employees shall participate in a minimum of one hour of sexual harassment prevention training annually, and (b) Anyone who supervises or manages employees shall participate in a minimum of two hours of sexual harassment prevention training annually, and (2) one hour of bystander training annually;
- (iv) Examples of prohibited conduct that constitute sexual harassment;
- (v) Details on: (1) how an individual can report an allegation of sexual harassment, including, as appropriate, instructions on how to make a confidential report, with an internal complaint form, to a manager, employer's corporate headquarters or human resources department, or other internal reporting mechanism; and (2) legal services, including governmental, available to employees who may be victims of sexual harassment; and
- (vi) A statement that retaliation for reporting sexual harassment is illegal in Chicago.

Contractor understands that it may be required to produce records to the CPO to verify the information provided. Under penalty of perjury the person signing below: (1) warrants that he/she is authorized to execute this Affidavit on behalf of Contractor, and (2) warrants that all certifications and statements contained in this Affidavit are true, accurate, and

Name of Contractor:
(Print or Type)
Signature of Authorized Officer:
(Signature)
Title of Signatory:
(Print or Type)
State of
County of
Signed and swom (or affirmed) to before me on (date) by
(name/s of person/s making statement).
(Signature of Notary Public)
(Seal)

Bid Package No.: 1.4

CMAR Federally Funded Instructions and Execution Document Terminal 3 Improvements

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidat The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic subm through Building Connected: ☐ Building Connected Bid Form; properly completed online Document Acknowledgement: ii ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25 ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Affidavit of Non-Collision Collision re symmetral postumente de la distriction de la companya de la com ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents CMAR Federally Funded Bid Package No.: 1.4

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services - Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54.



### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: \$5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects ☐ Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents

### DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 ☐ Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54.



#### PROCUREMENT - BID BOND

Bid Bonds are Required. Follow all instructions.

Include as an attachment on Building Connected.

#### INSTRUCTIONS FOR BID BOND FORM

	Bidders/Proposers	: Gr	ve these instructions to your surety	·-				
1.	The Bond must be on the CMAR's form	m. N	substitutions will be acceptable.					
2.	Copies of the form are acceptable. How the paper, and page 2 on the opposite side		DPS Version 04/25/2017			·		
3.	The amount of the Bond must be that sta the bond should be expressed as a percent		KNOW ALL MEN BY THESE PRESENTS		BID BOND we ere insert full name and add	lease or local title o	f Suban	
4.	All blank spaces to be filled in must be indicated. Determinations of legibility w be accepted, nor will any Bond form on w	ill	Principal, hereinafter called the Principal, an (here ins under the laws of the laws of the State of	d	name and address or legal to	itle of Surety) a cor	rporation	n duly organized
5.	Insert the full legal name and business ad form. If the Bidder/ Proposer is bidding stated in the same space as the full legal n	ur	bound unto CLARK - W.E. O'NEIL JV, h bid for the payment of which sum well and t heirs, executors, administrators, successors a	ruly to	be made, the said Principal	and the said Surety	, bind o	•
6.	The address of the Principal must be con as well, as bonds to be returned will be m		WHEREAS, the Principal has submitted a bid in accord Terminal 3 Improvements, Chicago, IL.	lance wit	h the Bid Package for Specification	Section(s)		, for
7.	The Bond must include the Surety's name	e, th	NOW, THEREFORE, if the Obligee shall ac	cept th	e bid of the Principal and th	e Principal shall, w	rithin the	e specified
8.	The Bid Package number must appear on	the	period of time, one hundred twenty (120) da					
9.	The Surety executing the bond must appeart within the limitations listed therein.	ear	faithful performance of the Work, all as prov Contract Documents, including addenda, of in full force and effect.			•		
10.	The names and titles of the people signing	g th	In the event the Obligee determines the Prince	ainal ha	- failed to comply with any		footh in	the manualine
11.	Corporations executing the bond shall aff "seal not required" in the space where the		paragraph, then the Principal shall pay to the between the amount specified in the Principal	Oblige	ee the difference, not to exce	ed the full penal st	um set fo	orth above,
12.	A person authorized to bind the Bidder/Pr	орс	another party to perform the work covered b	y said b	oid, together with all court co	osts, all attorney's f	fees and	any other
13.	The Bond must be signed by an attorn identifies the surety company's signatory		IN TESTIMONY WHEREOF, the said Princ	cipal ar	nd said Surety have caused the	his instrument to be	e signed	by their
14.	The date on which the Surety's Power of the bond was signed by the Surety.	Atı	respective officers and their corporate seals t	o be he	ereunto affixed thisd	lay of	_A.D. 20	)
15.	In its application to negotiated contracts,	he				(Principal)		(Seal)
			Witness:		(B	usiness Address)		
			Or Secretary's Attest	E	(Signature)	(7	Title)	
						(7)		(T - D
						(Surety)		(Seal)
			Witness:		(B	susiness Address)		
			Or Secretary's Attest		By(Signature)	(7	Title)	_
	ederally Funded Inst 3 Improvements	tuct	CMAR Federally Funded Terminal 3 Improvements	Instruc	tions and Execution Documents Bid Package No.: 1.4			S5-54

#### PROCUREMENT – PAYMENT & PERFORMANCE BOND

See P&P bond forms in Exhibit C of the Subcontract Agreement in Part Two B and also Owner Agreement Exhibit D, see Master Agreement Schedule 6.

Include as an attachment on Building Connected.

\*At COT3 option, you may be enrolled into the Subcontractor Default Insurance (SDI) program

DPS Version 04/25/2017

#### \*RIDER ATTACHED CONTRACTORS PERFORMANCE & PAYMENT BOND

See P&P bond forms in Exhibit C of the Subcontract Agreement in Part Two B.

CMAR Federally Funded Terminal 3 Improvements Instructions and Execution Documents

S5-55

#### PROCUREMENT – BID SUBMISSION CHECKLIST

BOOK 1 is not required to be submitted with the bid in its entirety

All required forms must be included with the bid.

Upload as an attachment with your submission on Building Connected.

Check all forms for signature, initials, notarizations, etc. requirements.



Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

SUBMIT ANY QUESTION REGARDING

REQUIRED BID FORMS AS A RFI TO

ProjectCOT3.inquiries@clarkconstruction.com or on BuildingConnected

	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
	s checklist is intended to assist Bidders but does not necessarily reference all documents required in this cification. Bidders should review this entire Part One for additional requirements. Missing forms may invalida
foll	following Documents are to be returned with your proposal; a completed bid package will include each of the owing documents without exception. Please attach the following documents to your electronic submission bugh Building Connected:
	Building Connected Bid Form; properly completed online.
	Document Acknowledgement; ii.
	Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5.
	Addenda (if any) acknowledged on the Proposal Page.
	DBE Schedules completed:
_	☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25.
	Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30.
	☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed,
	signed, and notarized; S5-31.  Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33.
	Exhibit A DBE Requirement for Bidders List; S5-41.
	DBE Utilization Report; S5-36.
п	Owner Agreement Exhibit D, See Master Agreement
_	Schedule 1 - Affidavit of Non-Collusion
	<ul> <li>Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours</li> </ul>
	☐ Schedule 4 – Statement of Bidders Qualifications
	☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit
	☐ Schedule 6 – Contractors Payment and Performance Bond
	☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects
	□ Schedule 8 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects     □ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions
	Affidavit of Uncompleted Work completed, signed, and notarized; S5-43
	Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6.
	Bidder's Financial Statement.
	Certifications (FAA)
	☐ Debarment; S5-46.
	☐ Lobbying; S5-47.
	□ Non-Segregated Facilities; S5-58.
	☐ BABA Certification; S5-51
	Sexual Harassment Affidavit; S1-8
	G-11 Covered Telecommunications Equipment or Services - Subcontractor Representation; See subcontract Exhibits.
	Bid Bond; S5-54.
	AR Federally Funded Instructions and Execution Documents

### PROCUREMENT - BID DOCUMENTS

### BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

Contains various requirements impacting the work and its administration

### PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents


Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

### PROCUREMENT - SUBCONTRACT EXHIBITS A, B & C

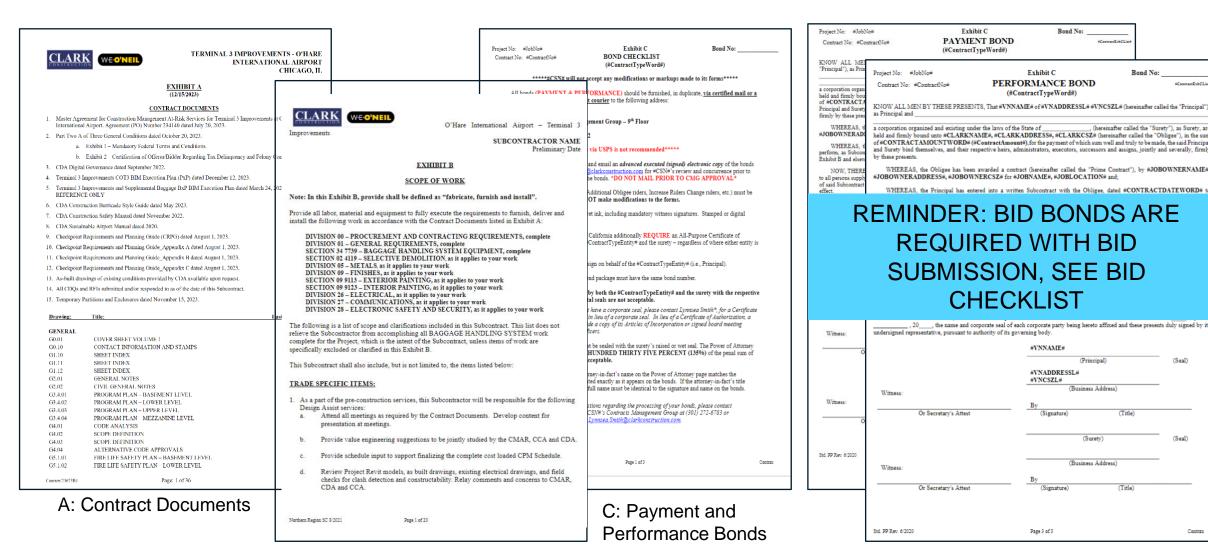

B: Scope of Work

+ContractEnhCLi

Rond No:

(Seal)

Contra

(Title)

(Title)

### PROCUREMENT – SUBCONTRACT EXHIBITS D, D-1, D-3, D-4



D-1: Labor Agreement

### PROCUREMENT - SUBCONTRACT EXHIBIT E

### Insurance Requirements



#### TERMINAL 3 IMPROVEMENTS AT O'HARE INTERNATIONAL AIRPORT CHICAGO, IL

#### EXHIBIT E (10/20/2023)

#### INSURANCE REQUIREMENTS

Clark Project No.: 23073B1

#### OWNER CONTROLLED INSURANCE PROGRAM

#### 1) OVERVIEW:

The Owner (Sponsor) may elect to provide certain insurance coverages under an Owner Controlled Insurance Program (OCIP). The OCIP is more fully described in the Sponsor's OCIP Insurance Manual (hereinafter "Insurance Manual") that is incorporated in this Exhibit E by this reference and made a part hereof. All Eurolled Parties are strongly encouraged to read the OCIP Manual and the OCIP Insurance Policies in detail prior to enrolling in the OCIP. The OCIP will provide to Eurolled Parties (as defined below) workers' compensation, employer's liability insurance, and excess liability insurance ("OCIP Coverage's"), as summarily described below, in connection with the performance of the subcontract work. In the event that there are any discrepancies between this Exhibit and the OCIP Manual, the most strict terms shall apply.

#### 2) ENROLLED PARTIES AND THEIR INSURANCE OBLIGATIONS:

OCIP Coverages shall cover Eurolled Parties. Eurolled Parties are: Sponsor, eligible Subcontractors and all of their subcontractors at any tier, who enroll in the OCIP, and such other persons or entities as Sponsor in its sole discretion may designate (each such party who is insured under OCIP is collectively referred to as an "Eurolled Party"). Parties performing labor or services at the Project site as defined in the Insurance Manual, are eligible to enroll in the OCIP unless designated by Sponsor as an Excluded Party (as defined below). Enrolled Parties (Subcontractors) shall obtain, maintain, and require all of their subcontractors at any tier to obtain and maintain, the insurance coverages specified below and the Insurance Manual.

#### 3) EXCLUDED PARTIES AND THEIR INSURANCE REQUIREMENTS:

OCIP insurance does not cover the following "Excluded Parties":

- a) Hazardous materials remediation, removal and/or transport companies and their consultants;
- b) Architects, surveyors, engineers, soil testing engineers, and their consultants;
- c) Vendors, suppliers, fabricators, material dealers, truckers, haulers, drivers and others who merely transport, pick up, deliver, or carry materials, personnel, parts or equipment or any other items or persons to or from the Project site.
- d) Any entity who does not perform any actual labor on the Project site;
- Any parties or entities not specifically identified in this Exhibit E, or excluded by Sponsor in its sole discretion, even if otherwise eligible.

#### 4) OCIP COVERAGES:

The summary descriptions of the OCIP Coverages in this Exhibit E or the Insurance Manual are not intended to be complete, or to alter or amend any provision of the actual OCIP Coverages. In the event any provision of this Exhibit E, the Insurance Manual, the Contract Documents, or the summary below conflicts with the OCIP insurance policies, the provisions of the actual OCIP insurance policies shall govern.

OCIP Coverages shall apply only to those operations of each Eurolled Party performed at the Project site in connection with the subcontract work and only to Eurolled Parties that are eligible for the OCIP, even if erroneously enrolled in the OCIP. The OCIP shall provide only the following insurance to eligible and Eurolled Parties:


Contrax/23073B1

Page: 1 of 7

**Telecommunications** 

**Equipment or Services** 

### PROCUREMENT -SUBCONTRACT EXHIBITS G2, G3, G4, G8, G11

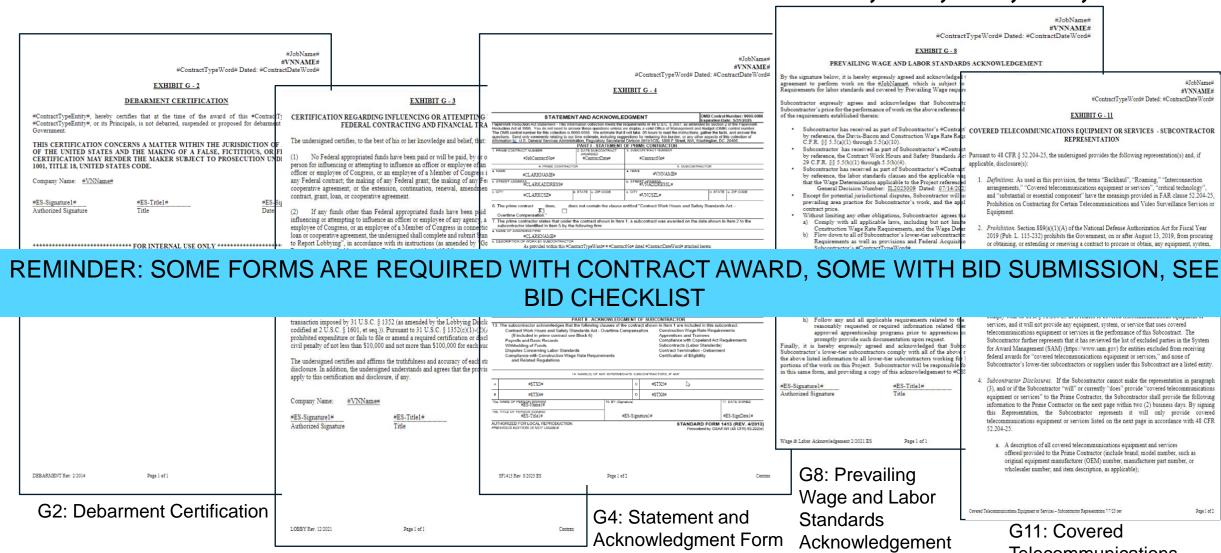

G3: Disclosure of Lobbying Activities

IMAGE IS FOR REFERENCE ONLY – USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

Form

### PROCUREMENT - SUBCONTRACT EXHIBIT J & J-1

J: Owner Required Flowdowns

J-1: Self Certification Form



TERMINAL 3 IMPROVEMENTS - O'HARE INTERNATIONAL AIRPORT CHICAGO, IL

Address

EXHIBIT J (08/31/2023)

#### OWNER REQUIRED FLOWDOWNS

Preliminary Exhibit J - Subject to Change Upon Execution of the Fina

- [Subcontractor/Supplier/Consultant/Designer/Provider/Lessor] (hereinafer:
   "Subcontractor") shall comply with all terms, conditions, and provisions that are
   or set forth in full text in, or otherwise comprise a part of or are applicable to the
   Construction Management At-Risk Services for Terminal 3 Improvements at D'I
   (hereinafter referred to collectively as the "Prime Contract"). All such terms, co
   hereby incorporated by reference and shall have the same force and effect as at
   if forth in full text in this [Subcontract/Order/Agreement/Lease Order] (hereina
   "Subcontract"). In the event of a conflict between the terms and conditions included in the Subcontract this Exhibit J shall g
   are offered the subcontract this Exhibit J shall g
   are offered the subcontract this Exhibit J shall g
   are offered the subcontract this Exhibit J shall g
   are offered the subcontract this Exhibit J shall g
   are offered to subcontract this Exhibit J shall g
   are offered to subcontract this Exhibit J shall g
   are offered to subcontract this Exhibit J shall g
   are offered to subcontract this Exhibit J shall g
   are offered to subcontract this Exhibit J shall g
   are offered to subcontract this Exhibit J shall g
   are offered to subcontract this exhibit subco
- Subcontractor hereby agrees to include all clauses included herein in all of its sul Subcontractor enters into a lower tier subcontract at any time during the perform copy of those lower tier subcontracts must also be provided to Clark: O'Neil. Thi to any and all lower tier subcontractors related to the performance of this Subcor

#### Exhibit D - Required Subcontract Provisions

II. <u>Standard of Performance</u>. Construction Manager will require that its Trace C minimum, meet the standard of performance set forth herein.

In addition to performing the Work in full compliance with the Contract Documents, perform, or cause to be performed, all Work required of it under the terms and coadir that degree of skill, care, and diligence normally exercised by qualified and experient performing work in projects of a scope and magnitude comparable to the Project. Unmaterials and equipment will be new, and of such quality as required to comply with The Trade Contractor will, when required, furnish statistactory evidence as to kind ar and equipment. All labor will be performed by workers skilled in their respective rabe of good quality so that first class work in accordance with the standards of contract Contract Documents will result.

III. <u>Permits, Licenses and Regulations.</u> Subcontracts must contain the following permits, licenses and regulations.

#### A Permits

- The Trade Contractor will not be responsible for the building permit cost. How
  specific permits, applicable licenses and associated fees will be the responsibility of
- 2. The nature of the foundation systems required on portions of this Project may permits, and coordination will be required with the City of Chicago Bureau of Unier required by the Contract, the Trade Contractor, representing its familiarity with these processes, is responsible for any and all submittals, fees, coordination, and any other approvals required by the authorities having jurisdiction for the installation of their.

Contrax/23073B1

Page: 1 of 66

#JobName# #VNNAME#

#ContractTypeWord# Dated: #ContractDateWord#

#### EVHIRIT I - I

#### SELF CERTIFICATION FORM

y Name: #VNNAME# #VNADDRESSL# te, Zip: #VNCSZL#

I. Business Concern Self Certification [SELECT <u>AT LEAST</u> ONE (1) BOX THAT APPLIES TO YOUR ORGANIZATION]:):

#50# Large Business (LB)

#51# Small Business Enterprise (SBE)

#512# Certified Disadvantaged Business Enterprise (DBE)

#\$13# Minority Business Enterprise (MBE) #\$14# Woman Business Enterprise (WBE)

#\$11# Other: #\$TX2#

#### II. Commercially Useful Function:

Attention is directed to Exhibit B of your #ContractTypeWord#, in which you agree that each Disadvantaged Business Enterprise ("DBE"), if any, with which you subcontract for work within the scope of your #ContractTypeWord# will perform a Commercially Useful Function as defined in Department of Transportation Regulations, 49 C.F.R. § 26.55. See pages 3-3 of this Exhibit J-1 for information concerning regulatory and #ClarkName# (hereinafter "#CSN#") requirements regarding "Commercially Useful Function." #ContractTypeEntity# further agrees to assure that each DBE lower tier subcontracts, if applicable, possesses a sufficient DBE certification for all within the scope of such lower tier subcontract.

III. In Section I above, Business Concern Self Certification:

Select here #\$RD0E# and skip the rest of Section III if you are <u>NOT</u> a Certified Disadvantaged Business Enterprise (DBE).

If you checked the box for "Certified Disadvantaged Business Enterprise (DBE)", complete the below items that apply to your organization:

The Illinois Unified Certification Program (ILUCP): (check the subset that applies to this Project)

#\$1\$# CERTIFIED U/DBE by the Illinois Department of Transportation (IDOT)...

Certification #: #\$1X10#

Date of Certification: #\$1X11#

\*Attach a copy of the Certification

(this space left intentionally blank)

II DRE CERTIFICATION 10/2017 ES

Dama 1 of

Contr

### PROCUREMENT -SUBCONTRACT EXHIBIT R

				Contract Numbe	#JobName# #VNNAME# #: #ContractNo# Dated: #ContractDateWord#	
	#JobName#		#JobName# #VNNAME#	EXHIBIT I	<u>R</u>	
Contract Number: #ContractNo# Dated: #Contr	#VNNAME# actDateWord#		Contract Number: #ContractNo# Dated: #ContractDateWord#	LOWER HER PARTIAL AFFIDAVIT AND PARTIAL #ClarkNames	UNCONDITIONAL RELEASE OF LIENS	
EXHIBIT R			EXHIBIT R	#ClarkAddrus# #ClarkCtZm	Project Number: adolyNos  Clark's #ContractTypeEntitys: #ContractTone #ContractTone #ContractTone	
AFFIDAVIT AND PARTIAL UNCONDITIONAL RELEASE OF LIENS/CLAIMS #ClarkName#	·	SUBCONTRACT	OR FINAL AFFIDAVIT, WAIVER OF LIEN, AND RELEASE #ClarkName#	Period From: To:	Contract Lieux	#JobName# #VNNAME#
#ClarkAddress# Project Number #0000m #ClarkC020 #Commed/palating #ClarkC020m	Contract Number: #Contrac	tNo: #ClarkAddress#	Project Number #Contract Type Entition Contract Date Contract Date Contract Date Contract Number #Contract Number #Contract Number #ContractOpe #ContractOpe	I. Certifications, Affirmations and Warrancies The undersigned, for and in considerations of payments made by stillationanes ("stillation performed in the construction of the above referenced Project purvaent to the above referenced Age 1. The undersigned has received payment in full, less retainings, for all work performed.	Contract Number	er: #ContractNo# Dated: #ContractDateWord#
Contract Date Co	EXHIBIT R	Period From: To: _	Payment Request No.:	and except for retainage, there are no outstanding claims against #ContractTypeExtity# and or its and guarantors, or the Project in connection with work performed in the construction of the Project	EXHIBIT:	
<ol> <li>Corrification. Affinantism and Warrandor.</li> <li>The information of the interest in the contract of the property of good and valuable consideration, to support to entidement to the payment requested in Pre- nal as provided in the uniceratest, purchase order, laste appearant, service agreement or other agreement (the "Agreement") between it and efficiently affiliance, certain and systems as followed:</li> </ol>	FORM A - OUTSTANDING CHANGE ORDER #ClarkName#	1 The major of first amount in the sec-	mets male to it by #ClaidMones, (#CDNe") or to a volcomments, materialisms, or supplier of the undersigned for labor con or the above-referenced project pursuant to the above-referenced control, heaving careful as a follows: your of \$	2. The undersigned has not assigned to approas any claim, may like, or my right to fills on screening for-times of the Project, and for its leaders and parameters, or the Project. 3. The undersigned has paid in full all laborate, and subject to remining an appearance materialism and others with respect to all owing portunes in the comparison of the Project through any claim, demand, like, assumbtance or action against #ContractTypeEntity# and or its sure materialism on the Project.	tan #ClarkName	*
affinio, certifica and variants in follows:  1. Primate Respont No.  1. Spread Respond No.	Notice of Carlot Advance Project  a the Control of Carlot Advance at Control of Carlot Of Carl		or common of said flood promotes and in consideration of the same havely profession in this to at a sametast to materials to district not consideration of the said flood promotes and in consideration of the manual havely affined these we are not consideration of the action with this project.  promote in fall, the undersigned does hereby waive, release, and quit claim in favor of #C.355s, the Owner of the project.	guarantees, or the arroject.  4. The undersigned has not given or executed any security interest for or in connection shink have been or are to be placed upon or installed in the Project, and is conveying good title to 5. The undersigned has point all amounts due benefit funds, applicable taxes, applicable performed in the construction of the Project.	#ClaricAddress# n no #ClaricAZ# tip: a Bas	Project Number: #IdobNom Clark's #CommentTypeEmisym #NoNtemen Comment Dens Comment Number: #CommentDawn Comment Number: #CommentSom
Construction of the project, much wire including means (i) through (v) is neverted collectively retrieve to its time work.  2. The understanded has received nowment in fall, less retrievances for all Work performed in the construction of the Project through the	of	Numb their successors and assigm all rights to said or making their successors and assigm all rights that presently a vartee of any law in the jurnification in which the land supplier, or materialmen to assert a lieu or claim again	permant in full, the undersigned does havely votive, release, and quit claim in favor of #CINNs, the Owner of the project, eleme on the project and the title company or companies extensioning and or instraint title to the project and any and all off or learned many cortex to the undersigned to assert a blue spon the land and understands companing the project by and improvements are charted or any assemblement of and law regarding the rights of a communer, valocuntractor, information project.	personnes in the construction for use evolucit.  6. The undexingued has complied with all applicable federal, state and local laws, codes of the Project.  7. The undexingued has the right, power and authority to execute this document.	The undersigned, for and in consideration of the payments made to it by #ClankNames, (the "Co-	Payment Request No.:
("Effective Dear"), and, stropy for possing change orders channe ("Classim") that we listed on the attached Form A, these we no constraining Classes suresies, the Owner of the Poyets and not in Indian's med gramation. On the Project, in consection with Works performed drough the Efficient Dear. In does not valuant a Form A with this Afflict's and Partal Salasse of Lians Classes, the undersigned, for good and valuable consideration, receipt of which forces undersign in right to such are the Classes which are the Classes of Lians Classes. The Classes Classes in the Classes of Classes are the Classes of Lians Classes of Lians Classes. The undersigned, for good and valuable consideration, receipt of which forces undersign in right to such are Classes without are reliable and the Classes Classes.	s hars	to execute this Affidavit, Waiver of Lies, and Release	go any claim for payment or right to perfect a lies against the project and the undersigned has the right, power, and authority	II. Waiver and Release The undersigned does hereby forever make and release in favor of #ContractTypeEntity# and its guaranton, the Project, and the title company or companies examining and or insuring life to the	a mail or management attraction for the construction of the appropriate project, hereby centiles  age  I. Upon receipt of final payment in the amount of \$	as follows: sed has received payment in full for all deliveries of material to and/or for work idention of same hereby affirms that there are no outstanding claims against the
the Effective Des.  It multivargued has not excipated to suppose any Claim, may less, or any right to file or perfect a list, against eCDNs and or its various, and or its leaders and guarantees, or the Project.  It must undersigned him paid informers, and, subject to restrings no guarant than the percentage restrings half by wCDNs, all subcomments.	EC, ITEM NO. DESCRIPTION OF WORK	IV. The undersigned variants that all laborar the project have received population due and that none V. No security interest has been given or ex-	s and videountenture simpleyed by it and all supplies or materialisms from which it has acquired materials incorporated into a such laborars, subcontractors, supplies, or materialisms have any claim, demand, or lies against the project or such in the supplies of the project of the underlying for or in connection with any materials appliances, machinery, fintness, or financialisms placed.	presently exist or haveafter may accrue to the undersigned by reason of work performed in the co naver a lieu upon the land and or improvements comprising the Poject and (ii) to assert or bring a or now line against ContractTypeZinniye and or its sureties, CCNNs and or its sureties, the Owne III. Indemnification	Constantly yellouting and/or in surelies, the Company and/or in surelies, the Architect and the Company and/or in surelies, the Architect and the Company, the Owner of the project, each and/or yeary noty outpring this to and/or making a loss of the project and are made in their surelies assigns a fright not represently exist for hearth or the far project and are made in their surelies with a surgion affight not represently exist for presently exist for hearth and the control of the project of the surelies and the control of the surelies and the su	pulvy waive, release, and out claim in favor of the #ContractTypeEntity#, the
and others with support to all Word performed drough the Effective Data.  The undersigned has not given or executed are security interest for or in connection with any materials, equipment, appliances, manchines; have been or see to be placed upon or incelled in the Project, and in conveying good title to the same to all Different and or the Counce.  The undersigned has good and applicable travers, then, then, then designed and no beautif finish relating directly or indirectly to the	Table .	upon or installed in the project.  This Final Affidanti, Waiver of Lieu, and Release shall under any supplemental contract or contract, whether the respect to the approject subsequent to the association	If a mindependent covanism and shall operate and be effective with respect to work and labor done and materials famished coal or written, for extra or additional work on the project and for any further work done or materials famished at any time	The understandance for the design of the design of the design of the understanding and the sur- garantees, from any and all damages, costs, expenses, demands, and such, (including reasonable as filling by any party with respect to any (i) work performed in the construction of the Project or wor day of	comprising the project by virtue of any law in the jurisdiction in which the land and improvement subcontractor, laborer, supplier, or materialmen to assert a lieu or claim against the project.	to are situated or any amendment of said law regarding the rights of a contractor,
FORMS A	RE REQUIRED WI	TH APPLI	CATION FOR PAY	MENT, AS APPL	ICABLE	
and agrees the entiry for remissage and the Claims hand on the stacked from A due theory force or mains and mission all crimes of action, claims in Adapt, clarifythm, multiflicator or commission support claims), with and detaunch, known or indexes, the file undexingual over half, now has or in a Claim and the contract of the Claim Claims. On the Claim and the Claims are detauted that Claims are detauted to the Claims are detauted that Claims are detauted to the Claims are detauted to t	Marie 1 7 1	E	(Automore regionies) TITLE(Tris)		under any oupplemental contract or contracts, whisting one or written, for extra or additional work with respect to the project solvengeant to the extension haveo!  IN WITNESS WHEREOF, this Affident, Whoter of Lies, and Ralessa has been executed this.	
and appear due excipt to receiving and the Chinan loads (or the standed from A that I heady forever wish and indexes of cross of series, chinan in deep, charged an efficiency or consistent request chinan), with and demands, increase an indexes, that the understand of the indexes and the consistency of the China of the China of the Project and or in Indexes and generation, or the Project by massin of milling in, milling from or in consecutions, the China of the China of the Project by massing the Effective Date.	Admin / selfer S S S S S S S S S S S S S S S S S S S	Subscribed and svorm before me this day of Stree of	(Assistant against) TITLE	Debotribed and events before me this day of	with respect to the project subsequent to the execution hereof.	
and appear the entiry for restrings and the Claims load on the stacked from A that of ben'y fiver written and valence at claims of action, claims to, dainy, chargetine medicineary or considers support claims), with and demands, increase or indicates, the demands are related to the COSM and for so coverage, the Commer of the Project and or in incident and guarantees, or the Project, by means of, relating to, mixing from or in content of the COSM and in the COSM and in content, and the Commer of the Project and in incident and guarantees. The undersugant heavily against the commercial heavily and the COSM and in content, and the Commercial to Project and in incident and guarantees. The undersugant heavily against the commercial heavily and the COSM and the COSM and in content, and the Commercial to Project and in incident and present and guarantees. The content of the Project and the content of the Project and the COSM and the CO	Marin	Subscribed and wroten before one this	(Assistant against) TITLE	Dubscribed and system before one this day of	with respect to the project subsequent to the execution hereof.	
and appear that entripf for reminings and the Climan listed on the attached from A that it benefy flower within a sed values at Climan of a strine, climan in, sideary, chargetine, medicineary or committees appear channel, with and determine, for mental control and the second chargetine and the and the second	Shade	Subscribed and snoon before me this day of Street of	(Assistant against) TITLE	Dubscribed and system before use thisday of	with respect to the project subsequent to the execution hereof.	
and appear that every the rectinage and the Climan loads on the strated from A that a bready force or various and values and climans of action, claims, in allege, chargetine, auditionary or consistent support channel, with and demands, increase or unbowned, the climan of a strategy of the SCNDs and for severate, the Consect of the Poyant and nor in incident and guarantees, or the Poyant, by manual of, mixing the mixing climans (the mixing of the Poyant or the Consect of the Poyant or the Consect of the Poyant of the Consect of the Consect of the Poyant or the Consect of the Consect of the Poyant or the Consect of the Consect of the Poyant or the Consect of the Consect of the Poyant or the Indian or the Consect of the Consect of the Poyant of the Indian with the Consect of the Poyant of the Indian of the Consect of the C	Marie   S	Subscribed and snoon before me this day of Street of	(Assistant against) TITLE	Dishecribed and owners before use this day of	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
and appear that entripy for rentinenge and the Climan bined on the attached from A that it hereby force or mistore, and climans of action, climan in along, clamping, and climans of action, climan in along, climping, and climans or consistent appear climan), with and demands, increase or unknown, the the undersquared were had, seen has consistent and consistent and consistent and climans of the	Marie   S	Subscribed and snoon before me this day of Street of	(Assistant against) TITLE	Buharahad and swoms before one false	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
and appear that entire for reminings and the Climan bland on the attached from A due it heavily flower various and values at Climan of station, climan to, skape, chargetine, and flowers or consultance aspects climan, with an electronic form, and the Climan of the analysis of the state of the Access of the Section of the Access of the Section of the Access of the A	Marie   S	Subscribed and snoon before me this day of Street of	(Assistant against) TITLE	Buharshed and system before use thisday of	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
and appear that entiry for rentances and the Climan loated on the attached from A that it heavily force or matrice and columns of action, climan in along, clamprian, auditionates or consultance impact climan, can be made, force or real-covers, the the undersuged over both given from its midental force or real-covers, the these medium and the project on from its columns. The consultance is required to the project of the project or project, by reasons of princip, to stongs the run is a column of the columns of the project or the columns of the project or the project or project or project or and in loading and the project or the project or proj	Section 5 S S S S S S S S S S S S S S S S S S	Subscribed and snoon before me this day of Street of	(Assistant against) TITLE	Bubuchhad and swom before me this day of	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
and appear that entire for reminings and the Climan bland on the attached from A due it heavily flower various and values at Climan of station, climan to, skape, chargetine, and flowers or consultance aspects climan, with an electronic form, and the Climan of the analysis of the state of the Access of the Section of the Access of the Section of the Access of the A	Section 5 S S S S S S S S S S S S S S S S S S	Subscribed and snoon before me this day of Street of	(Assistant against) TITLE	Steas of	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
said appear that entire for rentances and the Climan bland on the attached from A that it heavily force entires and columns of cation, chains to daily, chargetine, auditionacy or consistent appear chains), with and demand, locotes or subcream, that the undersquared even had, seen has contained to the contained of the contained	Section 5 S S S S S S S S S S S S S S S S S S	Subscribed and snoon before me this day of Street of	TITLE	Release of Liens & CLADAS, Ray 072022 Page 4 of 5	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
and appear that entire for reminings and the Climan bland on the attached from A due it heavily flower various and values at Climan of station, climan to, skape, chargetine, and flowers or consultance aspects climan, with an electronic form, and the Climan of the analysis of the state of the Access of the Section of the Access of the Section of the Access of the A	Section 5 S S S S S S S S S S S S S S S S S S	Subscribed and women before me thinday of _ States of	TITLE	RELEASE OF LIENS & CLAIMS_Rev.972022 Page 4 of 5  Lower tier partial	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
said appear that entire for rentances and the Climan bland on the attached from A but at heavily force or native and obtains all climans of nation, climan in daily, chargenine, mufficiency or committees appear chains), cuts and demands, locores or subcrease, that the undersquared own had, soon has come for the committees appeared to the committees and parameters, or the project by practice of the project by practice of prices; by the committee, the committees and parameters, or the project by practice of prices; the practice of the project or not in leading and the committees and parameters, the committees are present to industry and held families of Climan of the C	Section 5 S S S S S S S S S S S S S S S S S S	Subscribed and women before me thinday of _ States of	TITLE	RELEASE OF LIENS & CLADIS, Res. 072021 Page 4 of 3  Lower tier partial affidavit and	with regard to the project volumenant the execution hereof.  NO WITHOUGH THE MEDICAL data Affiliates, Writing of Linux, and Rakins has been executed this	
said appere that enterpt for rentances and the Climan load on the articles from A that it havely flower various and values at Climan of a state, climan in Aday, damption, intelligence or considered support channels, when and demands, become or unknown, that the unknown of a state, climan in a class of a state, or the contract of the	Souther S S S S S S S S S S S S S S S S S S S	Subscribed and women before me thinday of _ States of	TITLE	RELEASE OF LIENS & CLADIC, Par-072022 Page 4 of 5  Lower tier partial affidavit and partial	with regard to the project robusquest the estation level.  N. WILLIAGE WEEDLOF, this Affilient Writer of Lies, and Saless has been estated this	day of
said appear that entire for rentances and the Climan bland on the attached from A but at heavily force or native and obtains all climans of nation, climan in daily, chargenine, mufficiency or committees appear chains), cuts and demands, locores or subcrease, that the undersquared own had, soon has come for the committees appeared to the committees and parameters, or the project by practice of the project by practice of prices; by the committee, the committees and parameters, or the project by practice of prices; the practice of the project or not in leading and the committees and parameters, the committees are present to industry and held families of Climan of the C	Section 5 S S S S S S S S S S S S S S S S S S	Subscribed and women before me thinday of _ total of	TITLE	RELEASE OF LIENS & CLADIS, Res. 072021 Page 4 of 3  Lower tier partial affidavit and	with regard to the project relanguage to the execution hereof.  N. WILLINGS WESSELD, this Affilient. Writer of Lies, and Saless has been executed this	Contract   Contract

#### PROCUREMENT – SUBCONTRACT EXHIBIT V

V: Building Information Modeling

Applies only to trades with a BIM requirement



O'Hare International Airport Terminal 3 Improvements

#### EXHIBIT V (12/12/2023)

Definitions: (Definitions included below are specific for this Exhibit)

- "2D" means two dimensional.
- "3D" means three dimensional.
- "BIM Detailer" means person(s) responsible for the detailing of each Subcontractor's BIM content.
- "Construction Team" means Clark-W.E. O'Neil JV and all of its subcontractors and suppliers
  of any tier.
- "Contract Drawing" means a two-dimensional document derived from the three-dimensional model produced by a designer.
- "Coordinated Model" means a Federated Building Information Model (BIM) which has been coordinated with the Construction Team and Design Team to eliminate virtual clashes and installation constraints and is sufficient to create Contract Drawings/Shop Drawings for installation of the Work.
- "Coordination Model Schedule" means the schedule that dictates the time by which different
  areas, trades, and/or floors are to be coordinated, signed off, and submitted necessary to achieve
  the ultimate project schedule with input from the Construction Team and approved by
  Clark-WE. O'Neil JV.
- 8. "Data Hosting Site" means the web site(s) used to transfer, store, and share electronic data.
- "Deliverables" means 2D drawings in PDF and DWG format, 3D models in native authoring format, models in NWC/NWD format (to be coordinated in Revisto), Shop Drawings, or submittals.
- 0. "Design Team" means the Architect and all of its consultants at any tier.
- 11. "Electronic Information" means 2D and 3D digital data.
- 12. "Lead Coordinator" means the responsible party for creating a Coordinated Model for their coordination scope, performing clash detection, analyzing clashes and coordinating solutions, grouping and logging clashes, importing and assigning clashes in the tracking system designated by Clark-W.E. O'Neil Jv. The Lead Coordinator will prioritize clashes according to priority system and assign issues to the responsible party during coordination meetings using the designated issue tracker. Clark-W.E. O'Neil Jv will be the final authority on model issues.
- 13. "Model" means a digital representation of the physical and functional characteristics of the project and is referred to in this Exhibit as the "Model(s)", which may be used to describe a Model Element, a single Model, or multiple Models used in aggregate.
- 14. "Model Element" means a portion of a Model representing a component, system, or assembly within a building or building site.
- "Shop Drawing" means a two-dimensional document derived from the three-dimensional model produced by a Subcontractor.


Page: 1 of 15

Contrax/XXXXXXX

### PROCUREMENT – SUBCONTRACT EXHIBIT W, W-1

W: Certification of Compliance with Wage Laws

W-1: Authorized Individual for Signing Certification of Compliance with Wage Laws

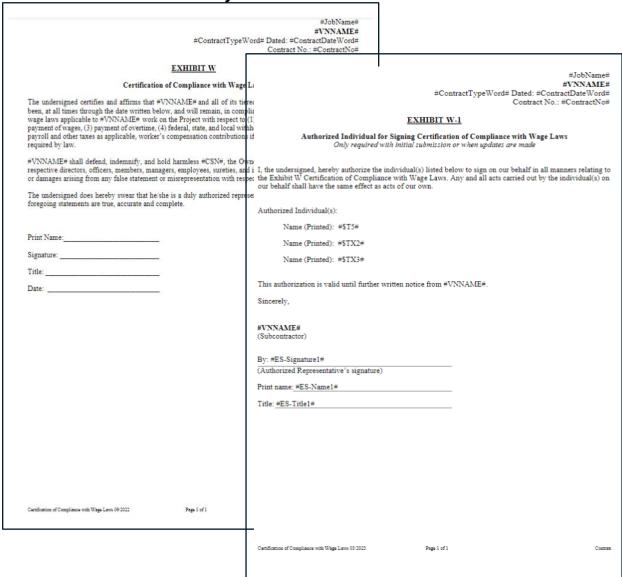

# PROCUREMENT – SUBCONTRACT ATTACHMENT, PRELIMARY PROJECT SCHEDULE- DRAFT



O'HARE INTERNATIONAL AIRPORT – TERMINAL 3 IMPROVEMENTS CHICAGO, IL

ATTACHMENT (12/22/2023)

#### PRELIMINARY PROJECT SCHEDULE - DRAFT

This attachment contains a preliminary project schedule titled "O'Hare T3I Preliminary Schedule DD 12.21.23" (77 pages).

Subcontractor acknowledges that the preliminary project construction schedule may require further development, including, but not limited to logic revisions, resequencing, resource-stacking, etc., as the work progresses; and has included all provisions necessary to maintain the Project Schedule.

The dates in the following schedule are Early Start and Finish Dates.

Contrax/23073B1 Page: 1 of 77

ite Printed: 22-Dec	2-23 10:35	Layout	: T3I - (1) Detailed Sch	edule		Data Date: 21-Dec
ity ID	Activity Name	Original Duration	Remaining Early Start Duration	Early Finish	Total Float T	2024 2025 2028 2027
[2 Improvement	ts - Preliminary Schedule - Data Date: 12/21/2023	946	841 21-Dec-23	13-Apr-27	0	OND THE WAM THE SUID THE WAM THE SUID THE WAM THE SUID THE WAM
MILESTONES	ts - Freimmary Schedule - Data Date. 12/21/2025	946	753 21-Dec-23	13-Apr-27	0	
PROJECT MLEST	TONICE	1360	1082 21-Dec-23	13-Apr-27	0	
MILE-130	PRE-CON NTP (7/24/2023)	0	0 21-Dec-23	15-Apr-21	0	E-CONNTP (7/24/2023)
MILE-130	CONSTRUCTION NTP (ANTICIPATED 4/26/2024)	0	0 21-Dec-23	26-Apr-24	,	◆ CONSTRUCTION NTP (ANTICIPATED 4/26/2024)
MILE-010	SUBSTANTIAL COMPLETION	0	0	10-Feb-27	2	◆ SUBS
	FINAL COMPLETION		0		0	↓3333 4 FI
MILE-120 LD MILESTONES		0 492	-	13-Apr-27	0	
LD-1000	LD - AA CLUB SHELL READY FOR TENANT FIT OUT BY OTHERS	0	492 04-Mar-25	10-Feb-27 04-Mar-25	492	◆ LD - AA CLUB SHELL READY FOR TENANT FIT OUT BY O
LD-1000		0	0			LD - GATE K1 INCEUDING PARTIAL HOLD RE
	LD - GATE K1 INCLUDING PARTIAL HOLD-ROOM FIT OUT	0	0	22-Aug-25	371 371	◆ LD - GATE L2A INCLUDDING PARTIAL HOLD
LD-1020	LD - GATE L2A INCLUDDING PARTIAL HOLD ROOM FIT OUT	-	0	22-Aug-25		◆ LD - CONCESSION SHELL READY FOR TE
LD-1030	LD - CONCESSION SHELL READY FOR TENANT FIT OUT	0	0	17-Sep-25	354	◆ LD CONCESSION SHELL READY FOR TEL
LD-1040	LD - SUBSTANTIAL COMPLETION	0	0	10-Feb-27	0	• LD-3
INTERIM MILESTO		1150	1022 21-Dec-23	10-Feb-27	62	DESIGN COMPLETE
MILE-150	DESIGN COMPLETE	0	0	21-Dec-23		Y
MILE-140	PERMITTING COMPLETE	0	0	24-Apr-24	1084	◆ PÉRMITTING COMPLETE
MILE-160	PURCHASING COMPLETE	0	0	24-May-24	1054	◆ PURCHASING COMPLETE
MILE-170	LONG LEAD MATERIAL PROCUREMENT COMPLETE	0	0	02-Jun-25	680	♦ LONG LEAD MATERIAL PROCUREMENT COMPLET
MILE-230	CONSTRUCTION - MECHANICAL COMPLETE	0	0	13-Nov-25	516	
MILE-180	CONSTRUCTION - CORE & SHELL COMPLETE	0	0	07-May-26	341	
MILE-190	CONSTRUCTION - STRUCTURAL/ENCLOSURE INFILL/OPENING COMPLETE	0	0	19-Oct-26	176	
MILE-210	CONSTRUCTION - RESTROOMALTERATIONS COMPLETE	0	0	01-Feb-27	71	◆ const
MILE-220	CONSTRUCTION - BAGGAGE HANDLING SYSTEM COMPLETE	0	0	03-Feb-27	69	♦ CONS
MILE-200	CONSTRUCTION - INTERIOR ALTERATIONS COMPLETE	0	0	10-Feb-27	62	◆ CONS
AAMILESTONES		451	451 29-Apr-24	06-Feb-26	300	
AA FLAG SHIP CH	1ECK-IN	189	189 13-May-24	10-Feb-25	552	
AA-1000	AA FLAGSHIP CHECK-IN SUMMARY (CALENDAR DAYS)	267	267 13-May-24	03-Feb-25	730	AA FLAGSHIP CHECK-IN SUMMARY (CALENDAR DAYS)
AA-1030	AA FLAGSHIP CHECK-IN START	0	0 13-May-24		683	AA FLAGSHIP CHECK-IN \$TART
AA-1040	AA FLAGSHIP CHECK-IN COMPLETE	0	0	03-Feb-25	469	◆ AA FLAGSHIP CHECK-IN COMPLETE
CDA-1000	UL - AA FLAGSHIP - FF&E MOVE IN PERIOD	5	5 04-Feb-25	10-Feb-25	469	■ UL-AAFLAGSHIP FF8E MOVE IN PERIOD
AAPPS		120	120 29-Apr-24	16-Oct-24	631	
AA-1010	AA PPS SUMMARY (CALENDAR DAYS)	171	171 29-Apr-24	16-Oct-24	7	AA PPS SUMMARY (CALENDAR DAYS)
AA-1050	AA PPS START	0	0 29-Apr-24		693	♦ AAPPS STARIT
AA-1060	AA PPS COMPLETE	0	0	16-Oct-24	573	◆ AAPPS COMPLETE
AACLUBTI		236	236 05-Mar-25	06-Feb-26	0	
CDA-1010	UL - AA CLUB TI START	0	0 05-Mar-25		69	♦ UL-AACLUB TISTART
AA-1020	UL - AA CLUB TI SUMMARY (CALENDAR DAYS)	339	339 05-Mar-25	06-Feb-26	0	UL - AA CLUB TI SUMMARY (CAL
CDA-1050	UL-AACLUBTICOMPLETE	0	0	06-Feb-26	0	↓UL-AACLUBTICOMPLETE
GATE CLOSURE		320	320 21-May-24	25-Aug-25	415	
GATE K1 CLOSU		320	320 21-May-24	22-Aug-25	415	
GATE-K1-1000		459	459 21-May-24	22-Aug-25	537	GATE K1 CLOSURE WINDOW (CALENDAR D
CDA-1100	UL- GATEK1 CLOSURE START	0	0 21-May-24	EE-ring-E0	677	↓ UL - GATEK1 CLOSURE START



T3I-231221-ForMarket | T3 Improvements - Preliminary Schedule - Data Date: 12/21/2023
Terminal 3 Improvements at O'Hare International Airport
City of Chicago: Chicago Department of Aviation





### PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)


Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

### PROCUREMENT – BID DOCUMENTS, Part Three of Three

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Available on BuildingConnected:

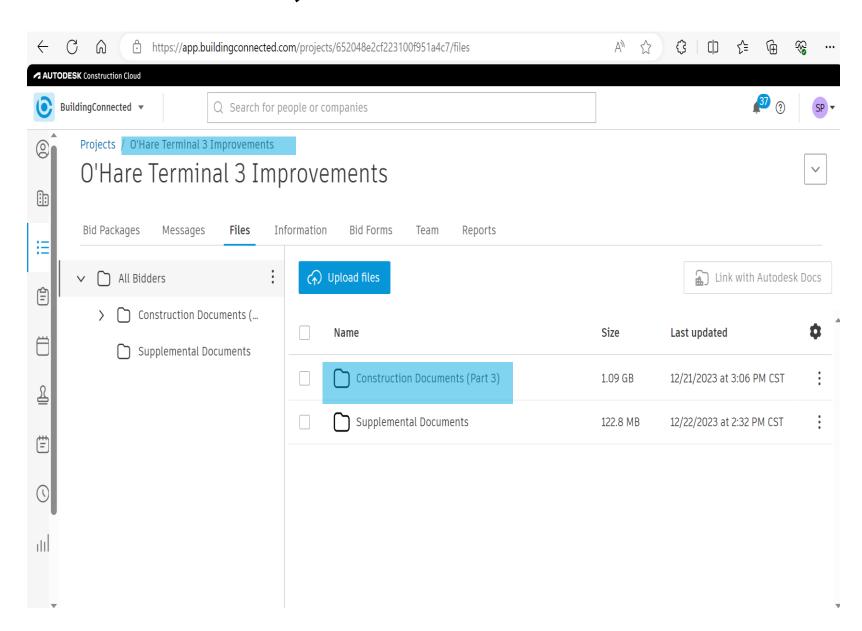

### PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)


Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

### PROCUREMENT – BID DOCUMENTS, Supplemental Documents


# Available on BuildingConnected:

- CDA Construction Barricade Style Guide\_May 2023
- CDA Construction Safety Manual FINAL 110922
- CDA Digital Governance Sept 2022
- CDA Smartsheet Standard Operating Procedure
- CDA Sustainable Airport Manual v4.0
- CDA-RFI Response Log\_2023.12.22
- COT3 Temporary Partitions and Enclosures
   Plan Rev1 202312120
- Exhibit 1- Mandatory Federal Terms and Conditions 20231020
- Exhibit 2 Tax Delinquency and Felony Convictions 20231020
- Master Agreement Exhibit E Bond Forms
- O'Hare T3I Preliminary Schedule DD 12.21.23 2
- ORD T3\_Geotechnical Report
- Terminal 3 Public Owner Contract
- Terminal 3 Improvements and Supplemental Baggage BIM Execution Plan 3-24-23
- TSA checkpoint-requirements-and-planningguide\_appendix-a
- TSA checkpoint-requirements-and-planningguide\_appendix-b
- TSA checkpoint-requirements-and-planningguide\_appendix-c

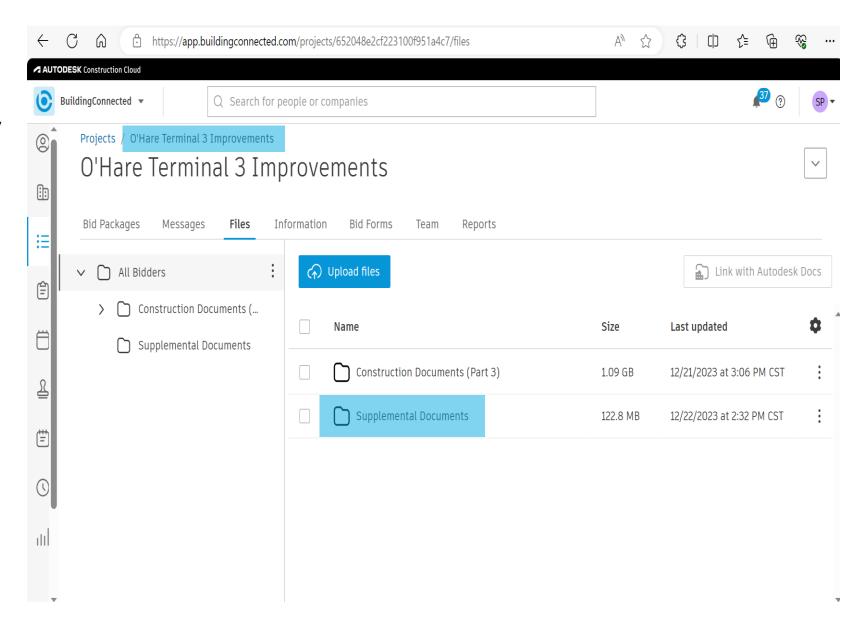


To begin, find the project in your Bid Board.

• From the "Accepted" tab on your Bid Board, click "Send or Log" on the right-hand side of the bid.

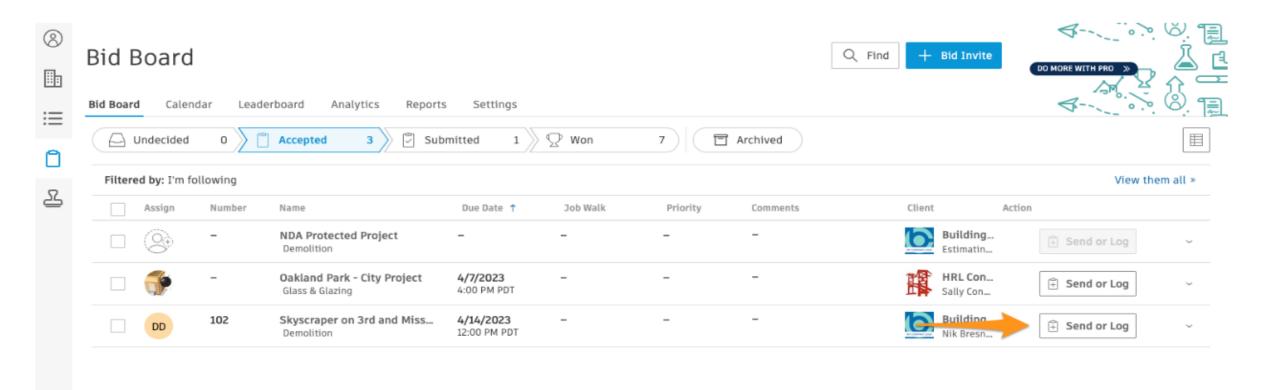

If you are already inside the project, click on the "Bid Form" tab or click "Bid Form" next to "Opportunity Summary"

Note: "Bid Form" appears next to the Opportunity Summary after you have indicated you are bidding. Select "Bidding" first see the "Bid Form" button.

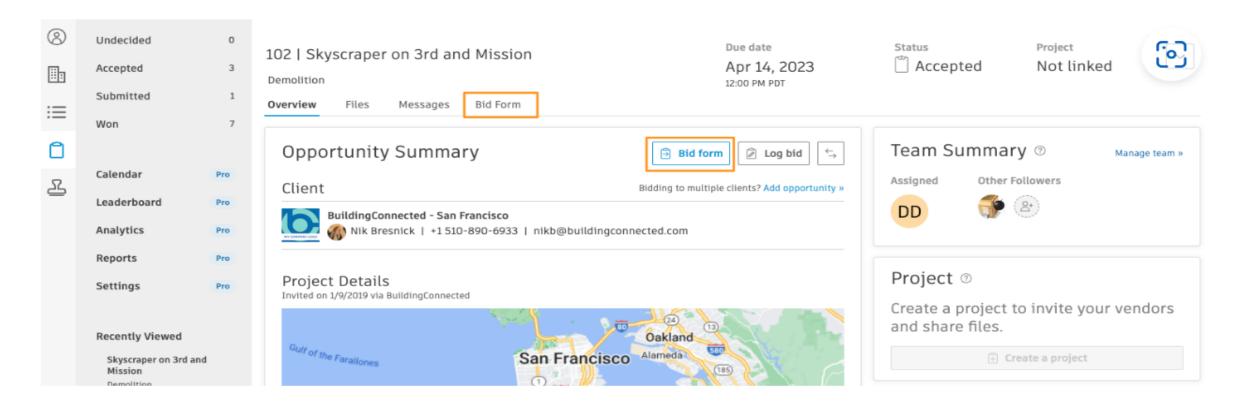


Enter all of the information requested in the form.


To attach the required documents, click "Attach your proposal" and select files from your computer. The files will immediately start uploading until they reach 100%. Upload more by clicking "Attach more".

Click "Print" to download or print a PDF copy of the bid form. The proposal will open in a new tab where there are options to download and print.


Once the bid form is complete, click "Preview & send".

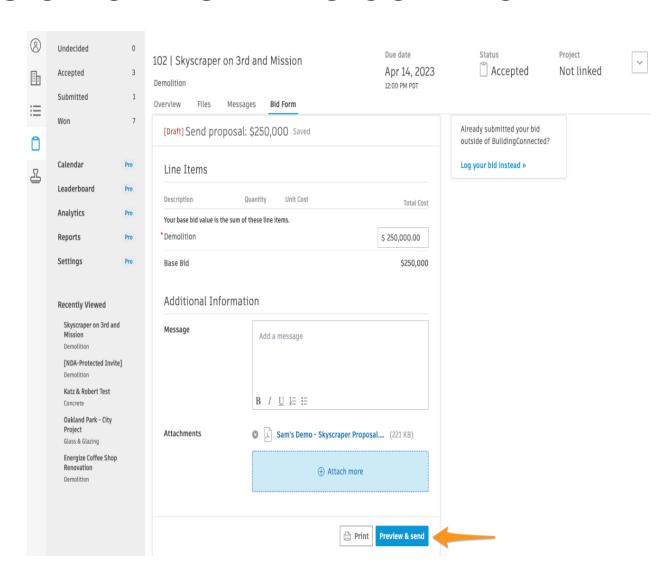


Please note that if you do not fill in all of the required questions, you will see any required items highlighted with a red flag. Fill them in accordingly and click "Preview & send" again.




Confirm all information on the bid form is correct and then click "Submit." Once you click "Submit," Clark-W.E. O'Neil JV will receive your proposal as well as an email notification.

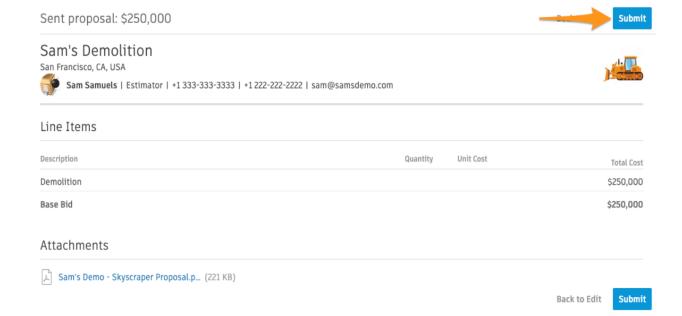


You will receive a confirmation.



You can ensure your bid was submitted successfully by checking that the "Status" has changed to "Submitted" and the bid form now says "Sent proposal" with the date and time the proposal was sent.

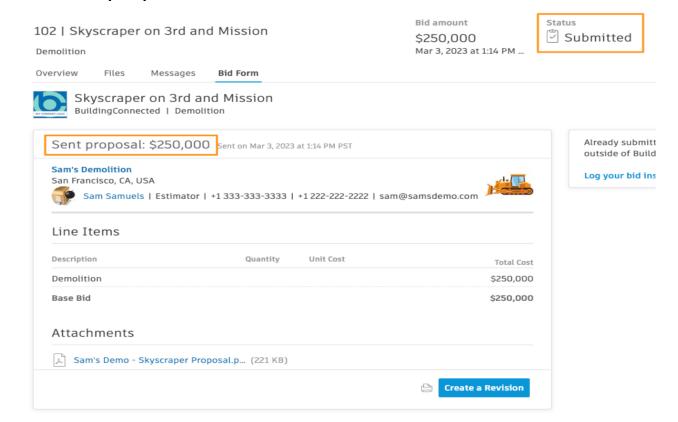

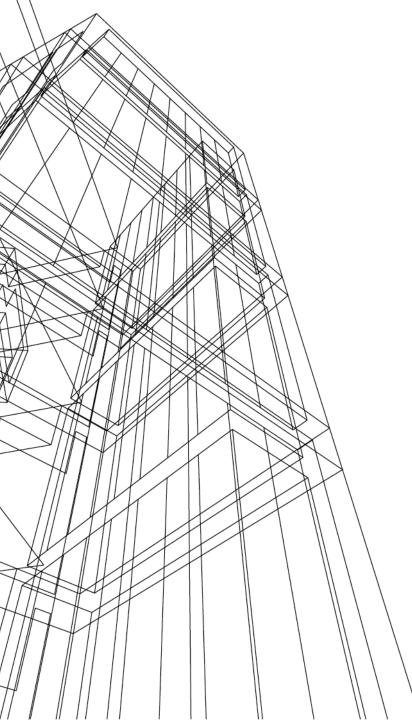


### PROCUREMENT - BID OPENING

Submit Bids on BuildingConnected prior to the bid opening date/time

Late bids will not be accepted

Hard copy bids accepted if needed prior to the bid opening date/time

Bid bonds required with your proposal

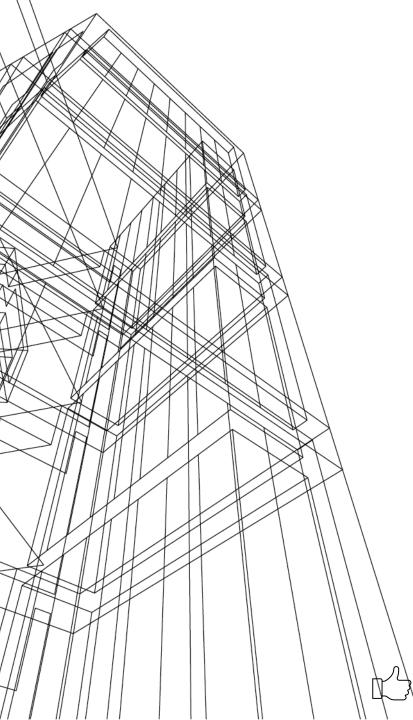

# PROCUREMENT – STEPS AFTER THE BID OPENING

Lowest responsive and responsible bidder to be brought in for post-bid meeting. BID THE SCOPE OF WORK, WITHOUT EXCLUSIONS/CLARIFICATIONS AND MEET OR EXCEED COMPLIANCE REQUIREMENTS.

If required, second or third responsive and responsible bidder to be brought in for a post-bid meeting


Upon completion of post-bid meeting, request for approval sent to CCA/CDA

Subcontract agreements issued upon approval by CDA. For long lead items, subcontractors may receive a Letter of Intent to commence with shop drawing preparations and potentially material/equipment procurement.

OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

### **CONCLUSION – NEXT STEPS**

- Meet the Primes
- Site Walk Through
- RFI'S are due no later than the Question Cut-Off Date / Time posted on <u>www.cot3.com</u> and <u>www.ord21.com</u>
- Review and acknowledge all Clarifications & Addenda
- Submit Bid(s) through Building Connected no later than the Bid Opening Date / Time posted on <a href="https://www.cot3.com">www.cot3.com</a>
   and <a href="https://www.ord21.com">www.ord21.com</a>

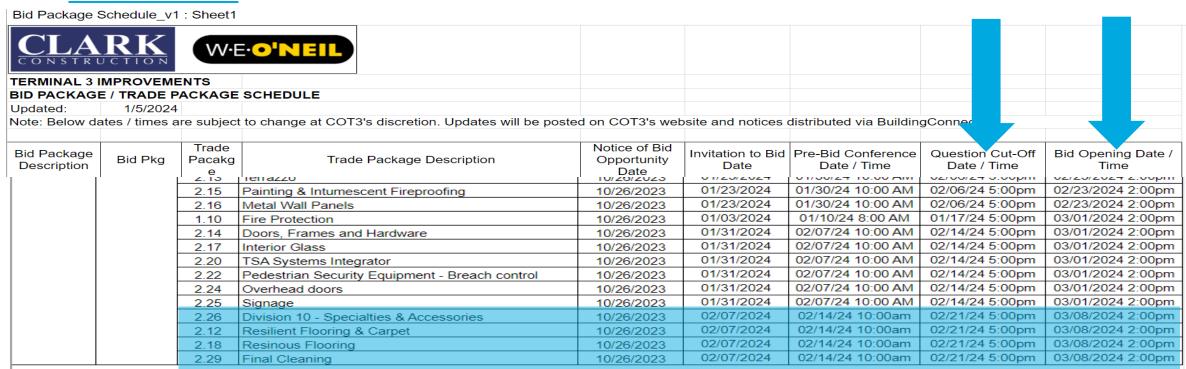

### **CONCLUSION – QUESTIONS**

#### Key takeaways:

- Return all documents needed with bid (reference the checklist)
- Be on the lookout for Addendums
- Complete the bid form in its entirety
- Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection
- Account for all Logisitics, DBE and Workforce requirements

#### SUBMIT ALL QUESTIONS

TO: ProjectCOT3.inquiries@clarkconstruction.com

NOTICE: NOTHING DISCUSSED TODAY IS INTENDED TO ALTER THE BID DOCUMENTS. ALL CLARIFICATIONS MUST BE SUBMITTED THROUGH THE REQUEST FOR INFORMATION (RFI) PROCESS FOR PROPER REVIEW AND RESPONSE.

IN CASE OF CONFLICTS BETWEEN TODAY'S DISCUSSIONS AND THE BID INFORMATION, BIDDERS SHOULD SUBMIT A PRE-BID RFI FOR CLARIFICATION AND GUIDANCE

## **Site Tour**

TERMINAL 3

LOWER LEVEL

NEAR BAGGAGE CLAIMS CAROUSEL 6

\*\*\*BRING YOUR DRIVERS LICENSE IF YOU ARE NOT BADGED\*\*\*

# **Meet the Primes/ Potential Bidders**

Division 10 – Resilier Flooring & Carpe	Flooring	Final Cleaning	
Meccor Lavoro Services Corp Interior Concepts Diverzify Ready Tile Co Office Environments Maman Corp	Diverzify CCI Flooring Menconi Terrazzo Stonhard	Construction Cleaning Company  Laboro Services Corp  Superior Labor Solutions  Scrub King	
