O'Hare Terminal 3 Improvements

COT3 Non-Mandatory Pre-Bid Conference Meeting & Meet The Primes Event





Terminal 3 Partners

This presentation and a copy of the sign-in sheet will be published to www.cot3.com

If you are attending virtually, please type your name, company name, email address and phone # in the chat NOTICE: NOTHING DISCUSSED TODAY IS INTENDED TO ALTER THE BID DOCUMENTS. ALL CLARIFICATIONS MUST BE SUBMITTED THROUGH THE REQUEST FOR INFORMATION (RFI) PROCESS FOR PROPER REVIEW AND RESPONSE.

IN CASE OF CONFLICTS BETWEEN TODAY'S DISCUSSIONS AND THE BID INFORMATION, BIDDERS SHOULD SUBMIT A PRE-BID RFI FOR CLARIFICATION AND GUIDANCE.

Agenda

- I. Introductions
- II. Project Overview
- III. Trade Packages
- IV. Compliance
- /. Contract Administration
- VI. Safety
- VII. Quality
- VIII. Procurement
- IX. Conclusion & Next Steps
- X. Meet the Primes / Potential Prime Contractors

Main points:

- Return all documents needed with bid (reference the checklist)
- Be on the lookout for Addendums
- Complete the bid form in its entirety
- Bid the full scope of work, without exception
- Account for all Logisitics, DBE and Workforce requirements



INTRODUCTIONS

- **OWNER**: Chicago Department of Aviation (CDA)
- **PROGRAM MANAGER:** Connect Chicago Alliance (CCA)
- CONSTRUCTION MANAGER AT RISK (CMAR): Clark-W.E. O'Neil JV (COT3)
 - Partner Firms
 - Cotter Consulting, Inc.
 - McKissack & McKissack Midwest, Inc.



PROJECT OVERVIEW - SCOPE OF WORK

- Expansion of the Departures and Arrivals levels to create room for a new outbound baggage makeup area, additional hold-room space and a new American Airlines Club space
- Demolition of an existing bag claim area and construction of a new inbound bag claim area
- Reconfiguration of the TSA checkpoints
- Reconfiguration of vertical transportation (elevators and escalators)
- Renovation of the existing restrooms
- Demolition and reconfiguration of existing airport/airline support spaces



Roof replacement of Terminal 3

PROJECT OVERVIEW – T3 IMPROVEMENTS & SUPPLEMENTAL BAGROOM – SCHEDULE & LIQUIDATED DAMAGES

NOTICE TO PROCEED: ANTICIPATED 4/26/24

SUBSTANTIAL COMPLETION: 2/10/27

REFER TO PUBLISHED SCHEDULE FOR MORE DETAIL

TIME OF COMPLETION/LIQUIDATED DAMAGES/WEATHER AND MORATORIUM DAYS TABLE

SECTION 4

NO.	MILESTONE	MILESTONE DATE	AMOUNT OF LIQUIDATED DAMAGES	
1.	AA Club Shell ready for tenant fit out by others (Schedule activity CDA-1010, UL - AA Club TI Start)	4-Mar-25	\$5,000 per calendar day	
2.	Gate K1 including partial hold-room fit out (Schedule activity CS-AA-1990, Complete Gate Opening Checklist for K1 – Hold Rooms & AA Club)	22-Aug-25	\$5,000 per calendar day	
3.	Gate L2A including partial hold-room fit out (Schedule activity CS-AA-2010, Complete Gate Opening Checklist for L2A- Hold Rooms & AA club)	22-Aug-25	\$5,000 per calendar day	
4.	Concession shell ready for tenant fit out (Schedule activity IA-UL-2G.A1360, Final Acceptance and Turnover – Airline Ops & Commercial)	17-Sep-25	\$5,000 per calendar day	
5.	Substantial Completion (Schedule activity Mile-110, Substantial Completion)	10-Feb-27	\$3,000 per calendar day	

PROJECT OVERVIEW – T3 IMPROVEMENTS & SUPPLEMENTAL BAGROOM – PRELIMINARY AIRSIDE LOGISTICS



O'Hare T3 Improvements

Airside Access – Trucking, Equipment Mobilization, & Deliveries

Keynotes

- 1. T3 Area of Work
- Construction Vehicle Inspection Area #5 (CVIA 5) – Gate Access to Airside

Legend

- Airside
- = Landside
- Active Taxiway



**Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required.

PROJECT OVERVIEW – PRELIMINARY AIRSIDE LOGISTICS


Airside Access – Trucking, Equipment Mobilization, & Deliveries

Keynotes

- Primary Vehicular Access via Construction Vehicle Inspection Area #5 (CVIA 5) – Gate Access to Airside.
- During full duration of expansion work: Stabilized construction entrance w/ trackout control (synthetic/movable). Full-time tire wash by trades. Full-time sweeper by trades.
- During full duration of expansion work: Full time dedicated flaggers required by trades



- Construction Vehicular Traffic
- Construction Foot Traffic
- Guard Post

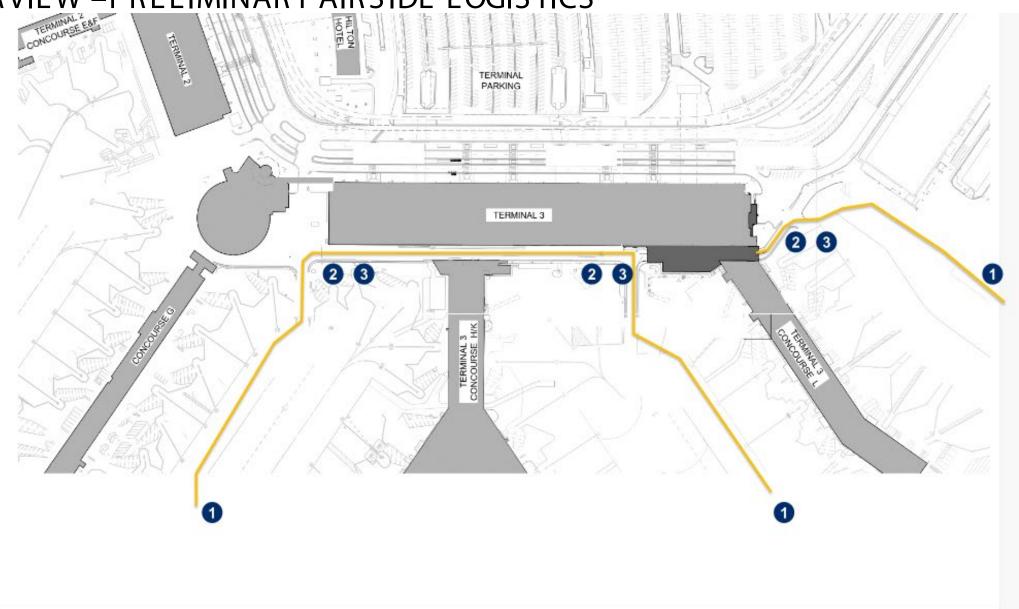

PROJECT OVERVIEW – PRELIMINARY AIRSIDE LOGISTICS


Airside Access – Trade Access On Foot	TERMINAL PARKING
Keynotes	
 Airside trade access on foot through existing Guard Post #8 & #10 	
2. Guard Post #8	
3. Guard Post #10	TERMINAL 3
Legend Construction – Vehicular Traffic Construction - Foot Traffic	
Guard Post	

PROJECT OVERVIEW – PRELIMINARY LANDSIDE LOGISTICS

Landside Access – Trucking, Equipment Mobilization, & Deliveries (NIGHT WORK)

Keynotes

- 1. Primary Vehicular Access for Landside Construction
- Landside Construction Deliveries As Req'd to Service Work Areas. Schedule According to Area "Work Rules"
- Full-time sweeper required by trades during expansion area construction at VSR & haul routes
- Full time dedicated flaggers required by trades during expansion construction at VSR & haul routes.

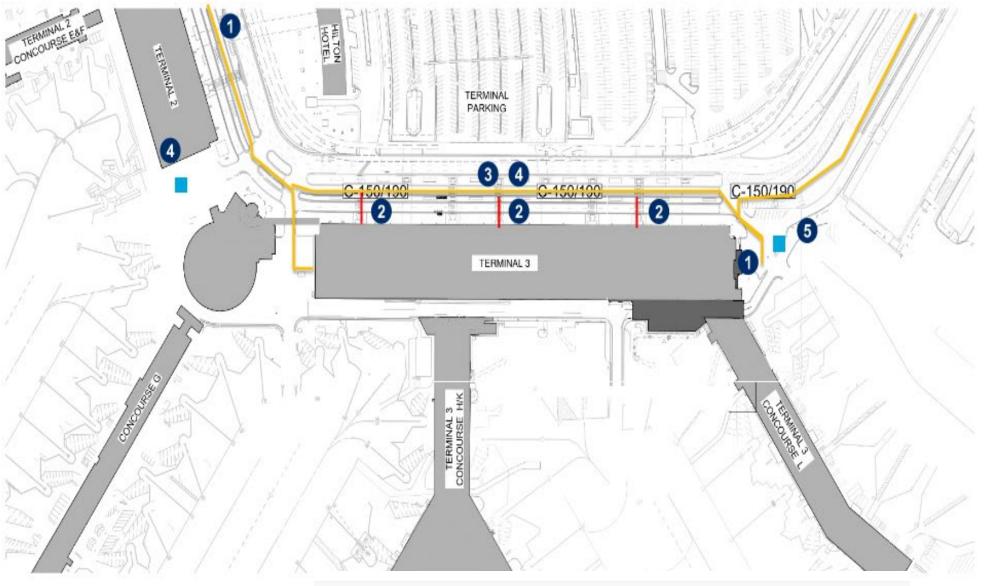

**Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."

PROJECT OVERVIEW – PRELIMINARY APRON WORK LOGISTICS

Apron - Work Rules

General Notes

- Subcontractor is responsible for maintaining tug traffic access to OH to all baggage areas including through the overhead doors at all times during operations.
- Gate K2 will remain operational. Work adjacent K2 must be scheduled & coordinated in advance with Owner and Clark-WE O'Neil JV
- During full duration of expansion work: Stabilized construction entrance w/ trackout control (synthetic/movable). Full-time tire wash by trades. Full-time sweeper by trades, by trades performing work on the VSR as required
- Full-time sweeper required by trades during expansion area construction at VSR & haul routes

Legend

- Jersey Barricade Construction Area
- Jersey Barricade Temp Scheduled outing w/ Gate K2


OH Protection

🔶 Flagger

Tire-Wash/Track-out Control

OH Door

Stair Tower - Landing at Apron, Upper Level, Roof Level

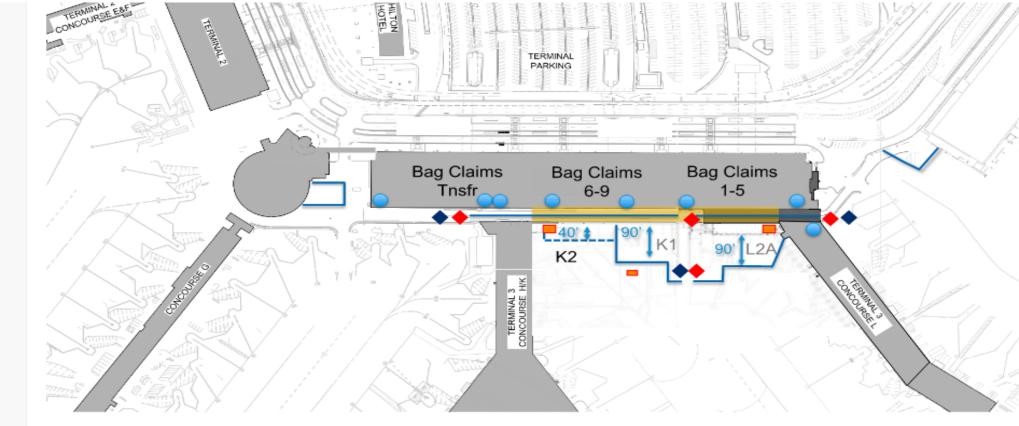

INCL. IN YOUR BID AS NEEDED FOR YOUR WORK

**Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."




BIDDERS MUST CONDUCT A SITE INSPECTION TO UNDERSTAND THE CONDITIONS, FACILITIES, AND SITE LOGISTICS RELEVANT TO THE WORK OUTLINED IN THE CONTRACT.

THE FAILURE TO VISIT THE SITE DOES NOT EXEMPT OR CHANGE THE BIDDER'S RESPONSIBILITY TO COMPLETE THE WORK IN ACCORDANCE WITH THE CONTRACT DOCUMENTS.

TRADE PACKAGES: BID PACKAGE 1, TRADE PACKAGES 2.6, 2.7, 2.9, 2.10, 2.19

Bid Package Schedule_v1 : Sheet1

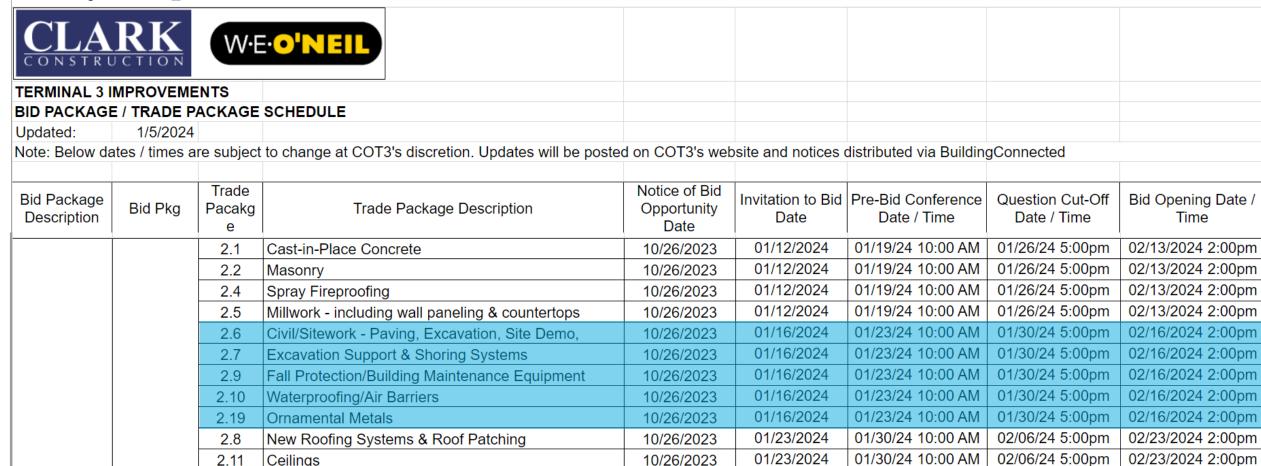

01/23/2024

01/23/2024

01/23/2024

10/26/2023

10/26/2023

10/26/2023

01/30/24 10:00 AM

01/30/24 10:00 AM

01/30/24 10:00 AM

02/06/24 5:00pm

02/06/24 5:00pm

02/06/24 5:00pm

02/23/2024 2:00pm

02/23/2024 2:00pm

02/23/2024 2:00pm

Remaining Trades 2.13

2.15

2.16

2

Terrazzo

Metal Wall Panels

Painting & Intumescent Fireproofing

COMPLIANCE- REQUIREMENT SUMMARY

DBE Requirements

- Participation at any level
- Trade specific range: 24% - 30%+ depending on trade

City Resident & Project Area Resident Requirements

- 50% City Residents
- 7.5% Project Area Residents
- Norwood Park
- Edison Park
- Jefferson Park
- Dunning
- Forest Glen
- Portage Park

Affirmative Action Requirements

- Minority
 participation: 19.6%
- Female participation:
- 6.9%

Buy America Build America (BABA) Project

 See specifications for complete requirements

Workforce Commitments

COMPLIANCE- DBE PARTICIPATION

- DBE Certification must be from the **Illinois Unified Certification Program** ("IL UCP") for the participation to apply towards the project requirements
- The DBE Contract Specific Goals set during the contract bid are applicable to any adjustments made to the contract after award.
- The contribution towards meeting the Contract Specific Goals only include the dollars paid to the DBE firm for the work performed within its certified Area of Specialty.
- All Subcontractors are required to use the B2Gnow system to track compliance and payments, including:
 - Entering all certified and non-certified Sub tier Subcontractors, including contract values.
 - Confirming payment(s) received and reporting sub tier Subcontractor payments made.
 - Ensure all sub tier Subcontractor commitments are current and all payments are confirmed.

OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

COMPLIANCE- DBE PARTICIPATION

ALC CASE	CITY OF CHICAGO Department of Procurement S	ervices							ASSIST	F AGENCY L	IST
	Aileen Velazquez, Chief Procurem 121 North LaSalle Street, Room	ent Officer		ATTACHMENT B (On Bidder/Proposer's Letterhead)		Assist Agencies are comprised interest of small, minority and/(Chief de tides				
	Chicago, Illinois 60602-128 Fax: 312-744-3281		RETURN RECEIPT REQUESTED	Re: Specification	(Date)	51#Street Business Asso 220 E. 51#Street	S00 E. 78th Street Chicago, IL 60810		imall Business Dev. 105 V	ago Minority Supplier D V. Adams, Suite 2300 Igo, IL 60603-6233	evelopment Council Inc. *
	L CONDITIONS FOR FAA/FTA/FHWA (IDOT) FUN STRUCTION, SERVICES, TASK ORDER SERVICES, AND		(Assist Agency Name and Address)	Description:	·	Chicego, IL 60615 773-285-3401 773-285-3407 the51ststreetbusinessess	admin@chaw	Greater Southwe 2601 W. 63rd Stree Chicago, IL 60626 773-362-3373	est Development Corporation et 9	Hispanic Ame Association (I 650 W. Lake S Chicago, IL 60	t., Unit 415
	ONDITIONS REGARDING DISADVANTAGED BUSINESS in following terms and conditions where Work or Services are fun to FHWA, FTA and FAA.		Bids are due on	ads to submit a bid/proposal in response to the abov 		www.51stStreetChicago.c Maintains list of certified Provides training for busir Angel of God Resource Co	Chicago Urb 4510 S. Michi	c.james@grea www.greatersc list of certified training for bus	South Shore Chamber, Inc. * 1750 E. 71 ^{ss} Street		Sustainable Options for Urban Living, Inc. (SOUL) 11803 S. Throop Street Chicago, IL
1.1. Policy and Terms In the event of a conflict be	tween these Special Conditions and 49 CFR Part 26, the provision	ns of 49 CFR Part 26 shall control.	The following areas have been identifi	ed for subcontracting opportunities on both a direc	t and indirect basis:	14527 S. Halsted Riverdale, IL 60827 708-392-9323	Chicago, IL 6 773-285-580(jjohnson@chi	HIRE360	Chicago, IL 60649-2000 773-955-9508 773-955-9554 Tonya Trice, Executive Director		60643 773-250-1770 Ext 702 773 250-1770
opportunity to participate fu against any person or busine must carry out applicable re	hat Disadvantaged Business Enterprises (DBEs) as defined in 49 (ally in the performance of contracts subject to 49 CFR Part 26. Co ess on the basis of race, color, national origin or sex in the perform squirements of 49 CFR Part 26 in the award and administration of ted contracts and take affirmative action to essure that businesses	ontractor must not discriminate nance of this Contract. Contractor United States Department of	Our efforts to identify potential subc ("DBC") contract goal. If you are ava please contact:	ontractors have not been successful in order to n re of any DBE firms that would be capable of per	meet the Disadvantaged Business Enterprise forming in any of the above-identified areas,	708-880-0121 info.sogro®gmaiil.com www.angelofgodresource Maintains list of certified Provides training for busir	Maintains list Provides trair Contractor A	2301 S Lake S Chicago, IL 60 312 575-2500 info@HIRE360 www.HIRE360 list of certified	info@southshorechamberinc.org www.southshorechamberinc.org Maintains list of certified firms: Yes Provides training for businesses: Y The Monroe Foundation		Cundil@soul- program.com www.soul- program.com Maintains list of certified firms: Yes Provides training for businesses: Yes Turn 2 Growth
-	have full opportunity to participate.		Name of Company		Address/phone	Austin African American 5820 W. Chicago Ave.	Chicago, IL. 6	training for bus	1547 South Wolf Road Hillside, Illinois 60162 773-315-9720		15475 S. Park South Holland, IL 60473 708-913-4700
Failure to carry out the com	all DBE Program Goal of 30%. mitments and policies set forth in this Article constitutes a materi the Contract or such remedy as the CMAR deems appropriate.	al breach of the Contract and may	within (10) ten working days of receip Due to our inability to identify an ap to participate as a subcontractor or	t of this letter. ppropriate DBE firm(s) certified by the Illinois joint venture partner on this project, a request	Unified Certification Program ("IL UCP") for the waiver of the contract goals will be	Chicego, IL 60651 773-626-4497 info@esebna.org www.seabna.org	info@contrac www.contract list of certified	Illinois Hispar 222 Merchand Chicago, IL 60 312-425-9500	omonroe@themonroefoundation.c www.themonroefoundation.org Maintains list of certified firms: No		info@turn2growth.org www.turn2growth.org Maintains list of certified firms: Yes
1.1.1. Contract-Specif	fic DBE Participation Goal et-specific goals for participation in furtherance of reaching its ov	erall DBE Program Goal.		idder/Proposer's) waiver request may be directe		Maintains list of certified Provides training for busir	Council of B	info@ihccbusir www.ihccbusin Maintains list c	Provides training for businesses:) US Minority Contractors Associ		Provides training for businesses: Yes Women's Business Development Center *
For purposes of this con	ntract, the CMAR has set the following contract goal:		Program Manager Connect Chicago Alliance 10510 West Zemke Road			Black Contractors Owner 7811 S. Stony Island Ave.	1 South Wack Chicago, IL 6	Provides traini	1250 S. Grove Ave. Suite 200 Barrington, IL 60010		8 S. Michigan Ave., Suite 400 Chicago, IL 60603
Contract DBE Partici			Chicago, IL 60666 (Timely Information Open Im	madistaly)		Chicago, IL 60649 773-346-5658	312-960-123§ msutton@infr	JLM Busines	847-352-5010 847-382-1787		312-853-3477x220 312-853-0145
	: task-order based, goals will be set for the individual task orders; pply to those task order goals as (f they were an overall contract g		If you wish to discuss this matter, plea			773-346-5659 admin@bcoechicago.org www.bcoechicago.org	Maintains list	Center* 2622 1 Chicago, IL 60 773-826-3064	arry.bullock@usminoritycontracto www.USMinorityContractors.org Maintains list of certified firms: Yes		edimence@wbdo.org www.wbdc.org Maintains list of certified firms: Yes
	be rejected as non-responsive if the bidder/proposer fails to subm ts good faith efforts to meet the Contract DBE Participation Goal		Sincerely,			Maintains list of certified Provides training for busir	420 Lake Coc	773-359-4021 lady930@prod www.jlmcenter	Provides training for businesses: \ Women Construction Owners & Chicago Caucus		Provides training for businesses: Yes
	BE compliance plan demonstrating how the bidder/proposer plans cipation Goal (Schedule D, D-1 or D-3 and Schedule(s) C, C-1 or					BOP Project 5000 NFP 644 E. 79 th Street Chicago, IL 60619 773-891-5939	847-453-889(iscifers@scig www.elitesdv	Maintains list c Provides traini	308 Circle Avenue Forest Park, IL 60130 708-366-1250 mkm@mkmservices.com		
B. Docu	amentation of Good Faith Efforts to obtain DBE participation in th	his contract.				773-304-1903		Native Americ 100 N. Riversi	www.wcoeusa.org Maintains list of certified firms: Yes	5	
	C are used for contracts for construction work. Schedules D-1 a s D-3 and C-3 are used for task order based contracts.	nd D-3 are used for contracts for				bopbizcenter@gmail.com list of certified firms: Yes Provides training for busir	Federation o	Chicago, IL 60 630-926-1700 info@nacc-il.o	Provides training for businesses: N		
reflected in Schedule I meet the Contract DBI Efforts to meet the gos	ust make good faith efforts to obtain DBE participation in this D, D-1 or D-3. The bidder/proposer must document that it has o E Participation Goal set forth above or, if unsuccessful in doing al (see <u>Section 1.7</u> "Good Faith Efforts"). If awarded the Contr ercentage of the total Contract Price (including any amendme	btained enough DBE participation to g so, has made adequate Good Faith act, Contractor must expend not less	CMAR Federally Funded	Instructions and Execution Documents			Chicago, IL 6 312-380-1122 info@fwcchic www.fwcchic; Maintains list Provides trair	www.nacc-il.or Maintains list c Provides traini Rainbow/PUS 930 E. 50 th Stn Chicago, IL 60			
total contract value. Th amendments and modif modification and amen	ting bidder proposer's responsiveness, the Contract DBE Participa the Contract DBE Participation Goal applies to the total value of th fications. The Chief Procurement Officer also has the authority to dment that by itself or aggregated with previous modification/am- reent of the minital award or \$50,000, whichever is greater, for opp ved in the contract. Instructions and Essentian Dersonemts	te contract, inclusive of all preview each proposed contract endment requests, increases the	Terminal 3 Improvements	Bid Pedage No: 1.1	S5-24	*Prime Contract Rev. July 2020 – I	*Prime	773-255-9087 773-256-2768 imitchell@rain www.rainbowp Maintains list c Provides traini			
Tenninal 3 Improvements	Bid Package No.: 1.1	\$5-7					Rev. Ji		*Rrime Contractors should contact	t seeney with subcentractin	a appartualities to compact partitied from

"Prime Con act agency with subcontracting oppor Rev. July 2020 - Information subject to change - visit www.chicago.gov/dps for the most recent list

CITY OF CHICAGO



OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

COMPLIANCE- WORKFORCE COMMITMENTS

Fe	deral

Requirements Minority Worker Requirement – 19.6%

Chicago Requirements

City of Chicago Residency Requirement – 50%

Project Area Worker Requirement – 7.5%

Female Worker Requirement – 6.9%

The Contract requires compliance with Chicago Residency Ordinance, Section 2 92 330 of the Chicago Municipal Code.

Failure to meet these requirements will result in assessment of penalties in the form of liquidated damages

1/20 of 1% (0.05%), 0.0005, of the approved contract value shall be assessed to the prime Subcontractor for each percentage of shortfall toward the stipulated residency requirement.

CONTRACT ADMINISTRATION- SOFTWARE

Administrative

- B2Gnow
- DocuSign
- LCP Tracker
- Oracle Textura
- Wrap X

Project Management

- Revisto
- E-Builder
- Primavera P6
- Procore

CONTRACT ADMINISTRATION- SCHEDULE OF VALUES REQUIREMENTS

Subcontract shall include line items on their Schedule of Values for the following work activities (at the following percentages relative to total Subcontract value):

- Close-out Documentation and Submittals including but not limited to As-builts, Warranty Documents, LEED and Training (2%)
- Punch List (2%)
- Demobilization (2%)
- Cleanup (2%)
- Safety (2%)

Subcontractor shall include a line item on their Schedule of Values for the city's residency requirements as outlined in Exhibit B and in the Chicago Municipal Code section 2-92-330. The line item shall consist of the maximum possible of the liquidated damages associated with the project area and city resident requirements. Subcontractor shall be allowed to invoice this line item periodically, and only to the extent that these residency requirements have been met and confirmed through certified payroll. At the end of the Project an accounting will be tabulated to determine any liquidated damages owed by Subcontractor related to unmet residency requirements, and these damages will be funded from this line item in the Subcontractor Schedule of Values.

CONTRACT ADMINISTRATION- SCHEDULE

Schedule Resource Loading will be required by each Subcontractor:

- Manpower (Crew Size and Hours)
- Equipment (Type, Quantity and Equipment Hours)

CONTRACT ADMINISTRATION- PAYMENT APPLICATIONS

MANDATORY WITH EACH PAYMENT REQUEST:

- G702 AND G703
- STATEMENT OF SUBCONTRACTOR TO COT3
- CONDITIONAL WAIVER AND RELEASES ON PROGRESS
 PAYMENTS
- WAIVER OF LIEN TO DATE
- CHANGE ORDER REQUEST LOG
- IF APPLICABLE, CITY OF CHICAGO C&D DEBRIS RECYCLING COMPLIANCE FORMS
- IF APPLICABLE, DIESEL EMISSIONS COMPLIANCE FORM
- IF APPLICABLE, STORED MATERIAL DOCUMENTATION
- OTHER SAM DOCUMENTATION, AS APPLICABLE

CONTRACT ADMINISTRATION- INSURANCE

Owner Controlled Insurance Program (OCIP)

Insurance Administrator – Alliant

Each Subcontractor, along with all lower-tier subcontractors, including professional services and suppliers, must undergo the enrollment process. Alliant will assess and notify if any firm is ineligible for participation in the program.

The Subcontractor must input all lower-tier subcontractors into WrapX. The actual labor, categorized by classification, needs to be documented through monthly payroll entries in the WrapX portal.

Review and approval of insurance will be handled directly between the Subcontractor and Alliant.

Additional insurance requirements outside of OCIP. See Sample Subcontract – Exhibit E

CONTRACT ADMINISTRATION- OCIP

Enrolled Parties

- All Eligible Prime Subs
- All Eligible Subcontractor Tiers performing labor or services at the Project Site
- Other Parties Enrolled at Owners Discretion

- Excluded Parties

- Demolition
- Hazardous Materials Contractors/Transporters
- Vendors, Suppliers, Fabricators, Material Haulers, Truckers, Cranes
- Subcontractors of any tier not eligible for and are excluded from the OCIP

CONTRACT ADMINISTRATION- OCIP ENROLLMENT

Contract signed with Subcontractor

• The Awarding Contractor Notifies Alliant through a Notice of Award (NOA) Letter

Enrollment in project

- Alliant works directly with the subcontractor for enrollment
- Enrollment must be completed online and be accepted before commencing work onsite
- If a subcontractor is onsite prior to enrollment, Carrier is not obligated to cover any accidents- there is no coverage.
- Backdating coverage is challenging if a contractor is discovered onsite without enrollment

Enrollment – requires the following information:

- Onsite Enrollment Form
- Insurance Cost Worksheet with WC/GL/XS Rate & Declaration Pages
- Offsite proof of insurance COI & Policy Endorsements (All Tiers)

Ongoing Subcontractor Responsibilities:

- Submit monthly payroll to Alliant through online entry
- Provide renewal offsite COI & Endorsements (All Tiers)

CONTRACT ADMINISTRATION- PROFESSIONAL LIABILITY INSURANCE

CDA'S PPL INSURANCE PROGRAM IS A REQUIREMENT FOR ALL SUBCONTRACTORS THAT HAVE A SCOPE OF WORK THAT INCLUDES DESIGN AND ENGINEERING



THE COST OF PARTICIPATING INTO THE PROGRAM IS 34% AND WILL BE DEDUCTED FROM THE CONTRACT AMOUNT



NO CHANGE ORDERS WILL BE ISSUED IF THIS FEE IS NOT RETURNED IT APPEARS THIS COST HAS NOT BEEN RETURNED TO ANY CONTRACTOR TO DATE (YET)



- Chicago Department of Aviation Construction Safety Manual November 2022
- Clark-W.E. O'Neil JV Safety Manual
- Subcontractor is required to: (i) develop a sitespecific safety plan, and (ii) reference subcontract for additional safety requirements and dedicated on-site Safety representation



CONSTRUCTION SAFETY MANUAL

NOVEMBER 2022



QUALITY ASSURANCE / QUALITY CONTROL

Technical Specification 01 4000 – Quality Requirements

Prior to commencing work:

- The Subcontractor must submit a Quality Control Plan for approval by COT3
- The Subcontractor is responsible to conduct a Pre-activity meeting

Each Subcontractor is required to provide a dedicated Quality Control representative onsite at all times

PROCUREMENT – QUESTIONS, PRE-BID RFI'S & ADDENDUMS

Bid Package Schedule_v1 : Sheet1



TERMINAL 3 IMPROVEMENTS

BID PACKAGE / TRADE PACKAGE SCHEDULE

Updated: 1/5/2024

Note: Below dates / times are subject to change at COT3's discretion. Updates will be posted on COT3's website and notices distributed via BuildingConnec

Bid Package Description	Bid Pkg	Trade Pacakg e	Trade Package Description	Notice of Bid Opportunity Date	Invitation to Bid Date	Pre-Bid Conference Date / Time	Question Cut-Off Date / Time	Bid Opening Date / Time
		2.1	Cast-in-Place Concrete	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.2	Masonry	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.4	Spray Fireproofing	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.5	Millwork - including wall paneling & countertops	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.6	Civil/Sitework - Paving, Excavation, Site Demo,	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.7	Excavation Support & Shoring Systems	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.9	Fall Protection/Building Maintenance Equipment	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.10	Waterproofing/Air Barriers	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.19	Ornamental Metals	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.8	New Roofing Systems & Roof Patching	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.11	Ceilings	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.13	Terrazzo	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Remaining	2	2.15	Painting & Intumescent Fireproofing	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Trades	2	2.16	Metal Wall Panels	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm

PROCUREMENT – REQUEST FOR INFORMATION

SUBMIT ALL PROJECT RFI'S VIA EMAIL OR THROUGH BUILDING CONNECTED

Email: ProjectCOT3.inquiries@clarkconstruction.com

Subject: RFI T3 Improvements "Trade Package" – "Company Name"

NOTES:

- MAKE SURE TO SUBMIT ALL QUESTIONS VIA RFI BY THE QUESTION CUT-OFF DATE & TIME INDICATED. LATE QUESTIONS WILL NOT BE RESPONDED TO!
- ALL RESPONSES WILL BE PROVIDED VIA BID ADDENDUM.

PRE-BID ADDENDUM TIMELINE

ADDENDUMS, IF ANY, ARE PLANNED TO BE ISSUED FOR ISSUANCE NO LATER THAN ONE WEEK BEFORE THE BID OPENING

LIST OF ANTICIPATED ADDENDUMS:

- UPDATED PROJECT SCHEDULE
- UPDATED EXHIBIT B'S
- ADDENDUM #01 DESIGN UPDATES/CLARIFICATIONS
- ADDENDUM #02 DESIGN UPDATES/CLARIFICATIONS
- ADDENDUM #XXX PRE-BID RFI RESPONSES

PROCUREMENT – BID DOCUMENTS

BID DOCUMENTS Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT - CHECKLIST

DOCUMENT SUBMITTAL CHECKLIST DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate Building Connected Bid Form; properly completed online Document Acknowledgement: ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5 Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed: Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. The following Documents are to be returned with your proposal; a completed bid package will include each of the Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, following documents without exception. Please attach the following documents to your electronic submission signed, and notarized; S5-31. Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. through Building Connected: Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement Schedule 1 - Affidavit of Non-Collusion Building Connected Bid Form; properly completed online. Schedule 2 - Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours Document Acknowledgement; ii. □ Schedule 4 – Statement of Bidders Qualifications Schedule 5 - Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects Addenda (if any) acknowledged on the Proposal Page. Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 DBE Schedules completed: Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. Non-Segregated Facilities; S5-58 BABA Certification: S5-51 Sexual Harassment Affidavit: S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Any exclusions, clarifications, or qualifications in your Bid Bond: \$5-54. proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions CMAR Federally Funder Instructions and Execution Documents Terminal 3 Improvement Bid Package No.: 1.4

through a pre-bid Request for Information (RFI).

PROCUREMENT – BID FORM (SUBMIT ONLINE)

		Proposal Bid Form: Trade Package: 1.3 - Demolition/Abatement	L F	Printed on Dec 22, 2023 at 9:34 AM CST
BUILDING CONNECTED BID FORM SECTIONS	Base Bid Line Items - Pricing	202141 : O'Hare Terminal 3 Improvements 10000 West Balmoral Avenue, Terminal 3, Chicago, IL 60666, United Sater W.E. O'Neil Construction Co. 1245 W Washington Blvd, Chicago, IL 60607, USA Rick, Jescrike I Sr. Estimator I +1773-244-4165 rjeschke@weoneil.c		(Keynil)
	Alternates	Description Quentity Unit Cest *01 - Demotition - Early trivestigative Demotition Work per Exhibit Bitters 51 *02 - Interior Selective Demotition (including escalator, non structural partitions, flooring etc.) *03 - Structural Demotition (including structural steel, floor openings and floor infilis) *04 - Exterior Enclosure Demotition (ucutain structural steel, floor openings and floor infilis) *04 - Exterior Enclosure Demotition (ucutain wall, precast etc.) *05 - Abatement * *06 - Maintenance of Traffic (MOT) Work * * * * *07 - Expreseing and Calculations Only for Means and Methods of Demotitiogper Exhibit Efferms 21, 25, 26, 40, 50) * * *08 - Other * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * * *		Total Cost S S S S S S S S
	Inclusions *Scope included per Exhibit B			\$ \$ \$0
	Scope-Specific Information and Unit Costs	Engineer licented in the State of Illinologi Kemporary shoring. "DEDUCTIVE ALTERNATE 2 - Provide Deduct Alternate to use dump O'Neil JV in lieu of using dumpsters provided by Subcortractor. Inclusions "Scope included per Exhibit B Scope-Specific Information and Unit Costs	sters provided by Clark-WE	S Mark "yes" to all yes no questions » Ves O No
		"Asbestos Abatement of 3" LTWR Pipe Insulation (\$ per Linear Foot) "Asbestos Abatement of 3" LTWR Pipe Insulation (\$ per Linear Foot) "Asbestos Abatement of 4" LTWR Pipe Insulation (\$ per Linear Foot) Page 1 of 5		per linear foot \$ per each \$ per linear foot \$ wrond by (© BUILDINGCONNECTED

PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Scope-Specific Information and Unit -Costs (continued from above)

General Acknowledgements

202141 : O'Hare Terminal 3 Improvements 0000 West Baimoral Avenue, Terminal 3, Chicago, IL 60666, United States of America			
"Asbestos Abatement of 4" LTWR Fittings (\$ per Each)	per each \$	5	
"Lead Based Paint Abatement of door frames (\$ per Each)	per each \$	5	
"Lead Based Paint Abatement of wide flange beams (\$ per SF)	per square foot	5	
"Lead Based Paint Abatement of pipe hangars (\$ per Each)	per each S	5	
"Lead Based Paint Abatement of valve wheels (\$ per Each)	per each \$	5	
*Lead Based Paint Abatement of electrical boxes (\$ per Each)	per each \$	5	
"Lead Based Paint Abatement of pipe - assume 4" OD (\$ per Linear Foot)	per linear foot	5	
"Lead Based Paint Abatement of bollards or pipe guards (\$ per Each)	per each \$		
"Lead Based Paint Abatement of handrail/guard rail (\$ per Linear Foot)	per linear foot		
General Acknowledgments	Mark "yes" to all y	yes/no q	ques
*Have you prepared your proposal in accordance with the Plans and Specifications?	0) Yes	C
"Have you reviewed all Division 0 and 1 of the Specifications?	0) Yes	C
"Have you reviewed the requirements for shift work and included premium cost as applicable?	0) Yes	C
"Does your scope require design services or engineering?	0) Yes	0
[°] If Yes to Design Services and Engineering, have you included 3/4% of your Bid total in you Bid for Project Professional Liability Insurance that may not be refunded at the end of the Job?	0) Yes	0
⁵ Subcontractor acknowledges their responsibility for all liquidated damages as a result of their performance and Work, as defined in the Owner Master Agreement, No. 234140.	0) Yes	C
⁵ Subcontractor acknowledges that they shall be responsible for any Builders Risk and General Liability deductibles associated with a claim resulting from your Work, as outlined in Exhibit D or E of the Subcontract Agreement.	0) Yes	C
*The Bidder agrees to submit its bid without limitations or exceptions, except as permitted by the Contract Documents.	0) Yes	C
[*] The Bidder further agrees that if awarded the Contract, the Bidder shall perform the Contract with no limitations or exceptions.	0) Yes	C
"The Contract Base Bid shall include the entire scope of Work and requirements of Part One, Part Two, Part Three and the Contract Drawings of the Contract Documents.	0) Yes	C
* The Contract will be awarded to the responsive and responsible Bidder offering the lowest Contract Base Bid, as determined by the Chief Procurement Officer.	0) Yes	0
"The contractor acknowledges that they may be asked to proceed with a Letter of Intent.	0) Yes	0
Bids will be compared based on the Bid Amount(s) and any combination of Alternates of each Trade Package, correctly computed, and a contract, if awarded, will be to the lowest response and responsible bidder, as determined by the CMAR.	0) Yes	0

PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

General Acknowledgements (continued from above)

Checklist of Required Documents to attached to your electronic bid submission through building connected

DBE Schedules (as applies)

02141 : O'Hare Terminal 3 Improvements 000 West Belmoral Avenue, Terminal 3, Chicago, L. 60666, United States of America			
UUU vreet permotei inversie, leimina 3. Chicago, L. BODOS, Umted States of America			
		0.00	
¹ Confirm that if alternative materials are included Bidder has noted that the product data and all other defining information of the product requirection evaluate the product as an equal or greater product to that which is specified is obtached.		() Yes	0
Subcontractor acknowledges that they have compiled with the base fine requirement for DBE participation per the 54h tBL DBE participation in the exceeds the baseline expectation for this task with batecard in the BB observing process. Subcontractors are encoursigned to network additional participation in the Base Bid or provide voluntary Atemates for additional DBE participation.		⊖ Yes	0
What percentage of DBE participation is included within the Base Bid?	input response here		
THE POLLOWING DOCUMENTS ARE TO BE RETURNED WITH YOUR PROPOSAL; A COMPLETED BID P FOLLOWING DOCUMENTS WITHOUT EXCEPTION. PLEASE ATTACH THE FOLLOWING DOCUMENTS TO THROUGH BUILDING CONNECTED:			
*Building Connected Bid Form property completed online		⊖ Yes	0
*Document Acknowledgement		O Yes	0
* Appropriate Proposal Page completed, signed and notarized		O Yes	0
*Addenda (if any) acknowledged on the Proposal Page.		O Yes	0
D BE SCHEDULES COMPLETED:			
*Schedule B: Afficiavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and noterized.		⊖ Yes	0
*Schedule C: DBELeiter of Intent to Perform as Subcontractor or Supplier, completed and signed.		O Yes	0
⁵ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized.		O Yes	0
*Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized.		⊖ Yes	0
*Exhibit A DBE Requirement for Bidders List;		O Yes	0
"DBE Utilization Report;		() Yes	0
*BABA Certification;		O Yes	0
* Owner Agreement Exhibit D		O Yes	0
*Schedule1-Afficiavit of Non-Collusion		() Yes	0
*Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours		O Yes	0
*Schedule 3 – Socio-Economically Disadvantaged Areas		O Yes	0
Schedule 4 – Statement of Bidders Qualifications		O Yes	0
*Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit		O Yes	0
* Schedule 6 – Contractors Payment and Performance Bond		NCLUDE EACH OF THE	

PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Checklist of Required Documents to attached to your electronic bid submission through building connected

FAA Certifications

Other Requirements

Subcontract Exhibits

	rinled on Dec 22, 2023 at 9:34 AM CS1
141 : O'Hare Terminal 3 Improvements	
West Bahmoral Avenue. Terminal 3, Chicago, L. 60666, United States of America	
² Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects	⊖ Yes ⊖ N
*Scheckule 8 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects	⊖ Yas ⊖ N
Schedule 9 - Certification Regarding Tax Delinquency and Felony Convictions	⊖ Yes ⊖ N
Affidevit of Uncompleted Work completed, signed, and notarized.	⊖ Yes ⊖ N
*Certificate regarding Removal of All Waste Materials and Dump Sites.	O Yes O N
Contractor's Statement of Experience and Financial Condition on file	⊖ Yes ⊖ N
RTIFICATIONS (FAA):	
Debarment	O Yes O N
Lobbying	⊖ Yes ⊖ N
"Non-Segregated Facilities	⊖ Yes ⊖ N
HER REQUIREMENTS:	
"Sexual Harassment Afficiavit	⊖ Yes ⊖ N
Covered Telecommunications Equipment or Services – Subcontractor Representation	⊖ Yes ⊖ N
"Bid Bond Form	⊖ Yes ⊖ N
Letter of Intert Form	⊖ Yes ⊖ N
NEW THE FOLLOWING DOCUMENTS AND MARK YES TO EACH ITEM TO CONFIRM ACKNOWLEDGEMENT AND INCLUSION WIT EPTION:	HOUT
BCONTRACT EXHIBITS:	
Exhibit A Contract Documents	⊖ Yes ⊖ N
"Exhibit B Scope of Work	⊖ Yes ⊖ N
"Exhibit C Payment & Performance Bonds	O Yes O N
"Exhibit D General Requirements	⊖ Yes ⊖ N
	⊖ Yes ⊖ N
Exhibit D-1 Labor Agreement	⊖ Yes ⊖ N
Exhibit D-1 Labor Agreement Exhibit D-2 Temporary Work and Fac IRies Requirements	ų ų
	⊖ Yes ⊖ N
Exhibit D-2 Temporary Work and Facilities Requirements	
Exhibit D-2 Temporary Work and Facilities Requirements Exhibit D-3 Site Utilization and Logistics Plans	⊖ Yes ⊖ N
Exhibit D-2 Temporary Work and Facilities Requirements Exhibit D-3 Sile Utilization and Logistics Plans "Exhibit D-4 Tax Exempt Letter and Cartificatio	⊖ Yes ⊖ N ⊖ Yas ⊖ N
Exhibit D-2 Temporary Work and Facilities Requirements Exhibit D-3 Sile Utilization and Logistics Plans "Exhibit D-4 Tex Exempt Letter and Cartificatio "Exhibit E Insurance Requirements	 Yes N Yes N Yes N

PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Subcontract Exhibits (continued)

Subcontract Attachments

Certifications

Attachments

202141 : O'Hare Terminal 3 Improvements		
0000 West Beimorel Avenue, Terminal 3, Chicago, I., 60666, United States of Ame	rice	
* Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment	⊖ Yes	0
[®] Exhibit G-11 Covered Telecommunications Equipment or Services – Sub Representation	acontractor O Yes (0
"Exhibit J Owner Required Flowdowns	O Yes	0
*Exhibit J-1 Self Certification Form	O Yes	0
"Exhibit R Release of Liens and Claims	O Yes	0
*Exhibit V Building Information Modeling (BIM) Requirements	O Yes	0
*Exhibit W Certification of Compliance with Wage Laws	O Yes I	0
*Exhibit W-1 Authorization for Signing Certification of Compliance with W	Aege Laws O Yes (0
SUBCONTRACT ATTACHMENTS:		
*Project Schedule	O Yes	0
Certifications		
'Is your firm a certified Disadvantaged Business?	O Yes	0
"If yes, please list your certification.	Input response here	
"If yes, please list your certification.	input response here	
Attachments	input response here	
Attachments		

PROCUREMENT – CHECKLIST (list of items to be returned with bid)

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. Doportinte Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed. Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Solicitations, completed, signed, and notarized; S5-33. Schedule D: Affidavit of Non-Collusion Schedule 1- Affidavit of Non-Collusion Schedule 1- Affidavit of Non-Collusion Schedule 2- Regulations of the Department of Procurement Services for Percentages of City and Project Area Regidents Working Hours Schedule 4- Statement of Bidders Qualifications Schedule 4- Statement of Bidders Qualifications Schedule 5- Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8- Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9- Certification and Performance Bond Schedule 9- Certification and Complience with FAA Buy American Preference – Equipment/Building Projects Schedule 9- Certification and Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9- Certification and Complience with FAA Buy American	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed:
Charlendows (PAA) Debarment; \$5-46. Lobbying; \$5-47. Non-Segregated Facilities; \$5-58. BABA Certification; \$5-51 Sexual Harassment Affidavit; \$1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; \$5-54. CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No: 1.4	Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (REI)

infough a pre-bid Request for information (RFI).

PROCUREMENT – DOCUMENT ACKNOWLEDGEMENT

Complete and return with your bid.

Include as an attachment on Building Connected.

This checklist is intended to assist Bidders but does not necessarily reference all documents required in this particular Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate a bid. Review the following Documents and initial each item to confirm acknowledgement and inclusion without exception: Subcontract Exhibits: Exhibit A Contract Documents Exhibit B Scope of Work Exhibit C Payment & Performance Bonds Exhibit D General Requirements Exhibit D-1 Labor Agreement Not Used Exhibit D-3 Site Utilization and Logistics Plans Exhibit D-4 Tax Exempt Letter and Certificate Exhibit E Insurance Requirements 10 Exhibit G-2 Debarment Certification 11. Exhibit G-3 Disclosure of Lobbying Activities Exhibit G-4 Statement and Acknowledgement of Form SF 1413 12 Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment 13. Exhibit G-11 Covered Telecommunications Equipment or Services - Subcontractor Representation 14 15. Exhibit J Owner Required Flowdowns Exhibit J-1 Self Certification Form 16. 17. Exhibit R Release of Liens and Claims Exhibit V Building Information Modeling (BIM) Requirements 18. Exhibit W Certification of Compliance with Wage Laws 19 Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws 20. Subcontract Attachments: Project Schedule Letter of Intent Authorized Signature Date Title I hereby acknowledge all of the above documents and certify that all associated costs are included in our proposal CMAR Federally Funded Instructions and Execution Documents

Bid Package No.: 1.4

Ferminal 3 Improvement

DOCUMENT ACKNOWLEDGEMENT (Federally Funded)

DOCUMENT SUBMITTAL CHECKLIST DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate Building Connected Bid Form; properly completed online Document Acknowledgement: ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5 Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed: Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. The following Documents are to be returned with your proposal; a completed bid package will include each of the Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, following documents without exception. Please attach the following documents to your electronic submission signed, and notarized; S5-31. Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. through Building Connected: Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement Schedule 1 - Affidavit of Non-Collusion Building Connected Bid Form; properly completed online. Schedule 2 - Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours □ Schedule 4 – Statement of Bidders Qualifications Document Acknowledgement; ii. Schedule 5 - Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects Addenda (if any) acknowledged on the Proposal Page. Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 DBE Schedules completed: Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. Non-Segregated Facilities; S5-58 BABA Certification: S5-51 Sexual Harassment Affidavit: S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Any exclusions, clarifications, or qualifications in your Bid Bond: \$5-54. proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions CMAR Federally Funder Instructions and Execution Documents Terminal 3 Improvement Bid Package No.: 1.4

through a pre-bid Request for Information (RFI).

PROCUREMENT – PROPOSAL PAGES S5-1 - S5-5 (as applies)

PROPOSAL TO BE EXECUTED BY A PARTNERSHIP

Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Submittal

Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless indicated here)

Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that

Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an EDS on behalf of the

Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are true, accurate and

complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of this

proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted that would render

Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership interests have been withheld and the information provided therein to the best of its knowledge is current and the undersigned has not entered into

any agreement with any other bidder (proposer) or prospective bidder (proposer) or with any other person, firm or

corporation relating to the price named in this proposal or any other proposal, nor any agreement or arrangement under which

any certification in the EDS false, inaccurate or incomplete,

the partnership has taken express written exception thereto in the sections of this specification designated for that purpose.

, and affirms that the partnership shall be bound by all the terms and conditions contained in the

SECTION 5 PROPOSAL TO BE EXECUTED BY A CORPORATION

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions. 4) Cont Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Cri and and Calendard

Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unle , and affirms that the corporation shall be bound by all the terms and condition Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except on the corporation has taken express written exception thereto in the sections of this specification designated

Under penalty of periury, the undersigned: (1) warrants that he/she was authorized to submit an ED Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted any certification in the EDS false, inaccurate or incomplete.

Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership withheld and the information provided therein to the best of its knowledge is current and the undersigned any agreement with any other bidder (proposer) or prospective bidder (proposer) or with any other corporation relating to the price named in this proposal or any other proposal, nor any agreement or arrange any act or omission in restraining of free competition among bidders (proposers) and has not disclosed to corporation the terms of this bid (proposal) or the price named herein.

Proposals must be submitted with original signatures in the space provided. Proposals not properly signed

PROPOSAL TO BE EXECUTED BY A SOLE PROPRIETOR

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Decuiromente (If DED/DEC) (a) Drowsal Pages, 7) Certifications and 8) Addenda Nos. (none unless indi-

the sole proprietor shall be bound by all the terms and conditions c ther a complete set thereof is attached to this proposal, except only The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, ritten exception thereto in the sections of this specification designa including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract

> ned: (1) warrants that he/she was authorized to submit an EDS on b hat all certifications and statements contained in the EDS are true, abmitted on-line; and (3) further warrants that, as of the date of sub inges in Circumstances since the date that the EDS was submitted t curate or incomplete

> orn deposes and says on oath that no disclosures of ownership inte therein to the best of its knowledge is current and the undersigned oposer) or prospective bidder (proposer) or with any other person in this proposal or any other proposal, nor any agreement or arran ee competition among bidders (proposers) and has not disclosed to sal) or the price named herein.

nal signatures in the space provided. Proposals not properly signed

PROPOSAL TO BE EXECUTED BY A JOINT VENTURE

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Submittal Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless indicated here)

, and affirms that the Joint Venture shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the Joint Venture has taken express written exception thereto in the sections of this specification designated for that purpose.

Under penalty of periury, the undersigned: (1) warrants that he/she was authorized to submit an EDS on behalf of the Disclosing Party on-line: (2) warrants that all certifications and statements contained in the EDS are true, accurate and complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of this proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted that would render any certification in the EDS false, inaccurate or incomplete

Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership interests have been withheld and the information provided therein to the best of its knowledge is current and the undersigned has not entered into ny agreement with any other hidder (proposer) or prospective hidder (proposer) or with any other person, firm o

SUBMIT ONE (1) OF THE APPLICABLE PROPOSAL EXECUTION FORMS WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED, SIGNED AND NOTARIZED

vote: in the event that this bid (proposal) is signed by other than the President, attach hereto a certification of the signed by other than the president attach hereto a certification of the signed by other than the president attach hereto a certification of the signed by other than the president attach hereto a certification of the signed by other than the president attach hereto a certification of the signed by other the signed by other than the president attach hereto a certification of the signed by other than the president attach hereto a certification of the signed by other the sis signed by	Revised Statutes 1965 Chapter 96 Sec. 4 et seq.	s 1905 Chapter 90 Sec. 4 et seq.	JOINT VENTURE ADDRESS:	
that section of Corporate By-Laws or other authorization, such as a resolution by the Board of Direc			(Print or Type)	
permits the person to sign the offer for the Corporation.	Registration Number:			
ATTEST:	SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE PARTNERSHIP	(Print or Type)	If you are operating under an assumed name, provide County registration number herein under as provided	
(Corporate Secretary Signature)	(If all General Partners do not sign, indicate authority of partner signatories by attaching copy of partnership agreement or		in the Illinois Revised Statutes 1965 Chapter 96 Sec. 4 et seq.	
(Affix Corporate Seal)	other authorizing document):		Registration Number:	
State of	Partner Signature:		SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE JOINT VENTURE	
	(Signature)		(If all members of the Joint Venture do not sign, indicate authority of signatories by attaching copy of Joint	
County of	Address:	edged before me on this day of, 20 by	Venture agreement or other authorizing document):	
	(Print or Type)	as President (or other authorized officer) and		
This instrument was acknowledged before me on this day of , 20 by	Partner Signature:	(Corporation Name).	SIGNATURE OF	
			Authorized Party:	
as President (or other authorized officer) and	(Signature)		(Signature)	
as resident (or other authorized orneer) and	Address:		TITLE OF SIGNATORY:	
Secretary of (Corporation Name).	(Print or Type)		(Print or Type)	
(Seal)	Partner Signature:		(
(Seal)	(Signature)	prop	BUSINESS ADDRESS:	
Notary Public Signature	Address:		(Print or Type)	
Commission Expires:	(Print or Type)		ATTEST:	
Commission Expires:	State of		(Joint Venture Secretary Signature)	
	County of		(Affix Joint Venture Seal)	
			(Affix Joint Venture Seal)	
	This instrument was acknowledged before me on this day of, 20 by		OK Joint Venturer	
CMAR Federally Funded Instructions and Execution Documents	as President (or other authorized officer) and as			
Terminal 3 Improvements Bid Package No.: 1.4 S:	Secretary of (Corporation Name).		Signature:	
	(Seal)	Instructions and Execution Documents Bid Package No.: 1.4	(Signature)	
	()	Did Fackage No.: 1.4	Address:	
	Notary Public Signature		(Print or Type)	
	Commission Expires:			
	Commission Express			
	CMAR Federally Funded Instructions and Execution Documents		CMAR Federally Funded Instructions and Execution Documents	
	Terminal 3 Improvements Bid Package No.: 1.4 \$5-2		Terminal 3 Improvements Bid Package No.: 1.4 S5-4	
			1	
			1	
				_

IMAGE IS FOR REFERENCE ONLY - USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

DOCUMENT SUBMITTAL CHECKLIST DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate Building Connected Bid Form; properly completed online Document Acknowledgement: ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5 Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed: Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. The following Documents are to be returned with your proposal; a completed bid package will include each of the Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, following documents without exception. Please attach the following documents to your electronic submission signed, and notarized; S5-31. Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. through Building Connected: Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement Schedule 1 - Affidavit of Non-Collusion Building Connected Bid Form; properly completed online. Schedule 2 - Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours Document Acknowledgement; ii. Schedule 4 - Statement of Bidders Qualifications Schedule 5 - Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects Addenda (if any) acknowledged on the Proposal Page. Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 DBE Schedules completed: Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46 Lobbying: S5-47. Non-Segregated Facilities; S5-58 BABA Certification: S5-51 Sexual Harassment Affidavit: S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: \$5-54. Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions CMAR Federally Funder Instructions and Execution Documents Terminal 3 Improvement Bid Package No.: 1.4

through a pre-bid Request for Information (RFI).

PROCUREMENT – ADDENDA (if any) ACKNOWLEDGED ON PROPOSAL EXECUTION FORM

FILL IN THE BLANK ON YOUR APPLICABLE PROPOSAL EXECUTION FORM (S5-1 – S5-5) The undersigned hereby acknowledges having received **Bid Package No.** 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Submittal Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless indicated here) _______, and affirms that the Joint Venture shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the Joint Venture has taken express written exception thereto in the sections of this specification designated for that purpose.

							\backslash
							\backslash
/		1					\
SECTION 5			PROPOSA	L TO BE EXECUTED BY A SOLE PROPRIETOR			\
PROPOSAL TO BE EXECUTED BY A CO			The undersigned hereby acknowledge	s having received Bid Package No. 1.4 containing a full set of Contras	et Documents,		\
The undersigned hereby acknowledges having received Bid Package No. 1.4 including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General	Conditions 3) Special Conditions 4) Contract		including, but not limited to, 1) Instru Plans or Drawings (if applicable) \$15	ctions to Bidders (Proposers), 2) General Conditions, 3) Special Condit Installed Specifications or Scope of Services, Evaluation/Selection Criter	tions, 4) Contract ris and Submitted		<u> </u>
Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Servic Requirements (If RPFRFQ), 6) Proposal Pages, 7) Cartifications and 8) , and affirms that the corporation shall be bound by a	Addenda Nos. (none unless il the terms and conditions	PROPOSAL TO BE EXECUTED BY A PART hereby acknowledges having received Bid Package No. 1.4 con	NERSHIP	al Pages, 7) Certifications and 8) Addenda Nos. (none unless indir- the sole proprietor shall be bound by all the terms and conditions o ther a complete set thereof is attached to this proposal, except only		PROPOSAL TO BE EXECUTED BY A JOINT VENTURE	
 Contract Documents, regardless of whether a complete set thereof is attached the corporation has taken express written exception thereto in the sections of the 	is specification designated for including, but no	t limited to, 1) Instructions to Bidders (Proposers), 2) General Con st (imited to, 1) Instructions to Bidders (Proposers), 2) General Con st (if applicable) 5) Detailed Specifications or Scope of Services, E	iditions, 3) Special Conditions, 4) Contract	ritten exception thereto in the sections of this specification designat red: (1) warrants that he/she was authorized to submit an EDS on b	The undersigned hereb	y acknowledges having received Bid Package No. 1.4 containing a full set of Contract Docume	nts,
Under penalty of perjury, the undersigned: (1) warrants that he/she was an Disclosing Party on-line; (2) warrants that all certifications and statements	thorized to submit an EDS + Requirements () contained in the EDS are tr	[RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Adde and affirms that the partnership shall be bound by all th	enda Nos. (none unless indicated here) te terms and conditions contained in the	hat all certifications and statements contained in the EDS are true, i brnitted on-line; and (3) further warrants that, as of the date of sub-	Plans or Drawings (if a	of to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Cont pplicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Submi REOD, 6) Proposal Pages, 7) Certifications and 3) Addenda Nos. (none unless indicated he	ital
complete as of the date the EDS was submitted on-line; and (3) further wan proposal or bid, there have been no changes in Circumstances since the date any certification in the EDS false, inaccurate or incomplete.	that the EDS was submittee ti the partnership h	ents, regardless of whether a complete set thereof is attached to th as taken express written exception thereto in the sections of this sp	ecification designated for that purpose.	nges in Circumstances since the date that the EDS was submitted to curate or incomplete.	Contract Documents, n	and afferms that the Joint Venture shall be bound by all the torms and conditions contained in egarifiess of whether a complete set thereof is attached to this proposal, except only to the extent ken express written exception thereto in the sections of this specification designated for that purpose	the fast
Further, the undersigned being duly sworn deposes and says on oath that no withheld and the information provided therein to the best of its knowledge is c	disclosures of ownership int Disclosing Party	of perjury, the undersigned: (1) warrants that ho/she was author on-line; (2) warrants that all certifications and statements cont he date the EDS was submitted on-line; and (3) farther warrants	tained in the EDS are true, accurate and	orn deposes and says on oath that no disclosures of ownership inte therein to the best of its knowledge is current and the undersigned roposer) or prospective bidder (proposer) or with any other person.	Under penalty of perj	ary, the undersigned: (1) warrants that ho/she was authorized to submit an EDS on behalf of	the
any agreement with any other bidder (proposer) or prospective bidder (p corporation relating to the price named in this proposal or any other proposal,	roposer) or with any other proposal or bid, for any agreement or arrangen any certification	there have been no changes in Circumstances since the date that t in the EDS false, inaccurate or incomplete.		in this proposal or any other proposal, nor any agreement or arrang ee competition among bidders (proposers) and has not disclosed to	complete as of the dat	e; (2) warrants that all certifications and statements contained in the EDS are true, accurate the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of any benn no changes in Ciscursatances since the date that the LDS was submitted that would ren the end of the true of the date that the true the true that the true of the true that the true of the t	this
any act or omission in restraining of free competition among bidders (propose corporation the terms of this bid (proposal) or the price named herein.	Further, the und	ersigned being daly sworn deposes and says on earth that no disc information provided therein to the best of its knowledge is curren	closures of ownership interests have been at and the undersioned has not entered into	sal) or the price named herein. nal signatures in the space provided. Proposals not properly signer	any certification in the	EDS false, inaccurate or incomplete.	
Proposals must be submitted with original signatures in the space provided. Pr NAME OF CORPORATION:	oposals not properly signed wi any agreement corporation relat	with any other bidder (proposer) or prospective bidder (propo ing to the price named in this proposal or any other proposal, nor a	oser) or with any other person, firm or my agreement or arrangement under which		withheld and the inform	d being duly swern deposes and says on oath that no disclosures of ownership interests have b sation provided therein to the best of its knowledge is current and the undersigned has not entered it up other bidder (proposer) or groupective bidder (proposer) or with any other person, firm	into
NAME OF CORPORATION: (Print or Type) SIGNATURE OF PRESIDENT*:	any act or omiss corporation the t	ion in restraining of free competition among bidders (proposers) at erms of this bid (proposal) or the price named herein.	nd has not disclosed to any person, firm or	(Signature)	corporation relating to any act or omission in	the price named in this proposal or any other proposal, nor any agreement or arrangement under wh restraining of free competition among bidders (proposers) and has not disclosed to any person, firm	sich
(Or Authorized Officer) (Signature)	Proposals must b BUSINESS NAI	e submitted with original signatures in the space provided. Propos	sals not properly signed will be rejected.			(this bid (proposal) or the price named herein.	
TITLE OF SIGNATORY: (Print or Type)		(Print or Type)		(Print or Type)		nitted with original signatures in the space provided. Proposals not properly signed will be rejected	L
BUSINESS ADDRESS: (Print or Type)	BUSINESS AD	(Print or Type)		(Print or Type) assumed name, provide County registration number herein under as	JOINT VENTURE N	(Print or Type)	
*Note: In the event that this bid (popoul) is signed by other than the P that section of Corporate By-Laws or other authorization, such as a rese permits the person to sign the offer for the Corporation.	resident, attach hereto a certif Reviewd Statutes	ting under an assumed name, provide County registration numbe 1965 Chapter 96 Sec. 4 et seq.	er herein under as provided in the Illinois	assumed name, provide County registration number nerein under as i 1965 Chapter 96 Sec. 4 et seq.	JOINT VENTURE A	DDRESS: (Print or Type)	
ATTEST: (Corporate Secretary Signature) (Affix Comporate Seal)	SIGNATURES (If all General P	AND ADDRESSES OF ALL MEMBERS OF THE PARTNERSHI artners do not sign, indicate authority of partner signatories by at		(Print or Type)	If you are open in the Illinois I Registration N	rating under an assumed name, provide County registration number herein under as provided Revised Statutes 1965 Chapter 96 Sec. 4 et seq.	
(Afrix Corporate Seat) State of	other authorizinj Partner Signatus	e:			SIGNATURE	unter: S AND ADDRESSES OF ALL MEMBERS OF THE JOINT VENTURE s of the Joint Venture do not sign, indicate authority of signatories by attaching copy of Joint	
County of	Address:	(Signature) (Print or Type)		dged before me on this day of, 20 by as President (or other authorized officer) and	Venture agree	ment or other authorizing document):	
This instrument was acknowledged before me on this day of				(Corporation Name).	SIGNATURE Authorized Pa	rty:	
as President (or other authorized officer) at	d Address:	(Print or Type)			TITLE OF SM	JNATORY: (Signature) (Print or Type)	
Secretary of (Corporation Name). (Seal)	Partner Signatur	c: (Signature)		000	BUSINESS A	0	
Notary Public Signature Commission Expires:	Address:	(Print or Type)			ATTEST:	(Print or Type)	
	State of County of					(Joint Venture Secretary Signature) (Affix Joint Venture Seal)	
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Innewsements Bid Packase No. 1.4	5	as President (or other authorized officer) a	day of, 20 by and as		OR Joint Venturer Sienature:		
	Secretary of (Seal)	(Corporation Name).		Instructions and Execution Documents Bid Package No.: 1.4	Address:	(Signature)	
	Notary Public Si Commission Exp					(Print or Type)	
	CMAR Federally Fu Terminal 3 Improves		\$5-2		CMAR Federally Funded Terminal 3 Improvements	Instructions and Execution Documents Bid Package No: 1.4	\$54
				J			

DOCUMENT SUBMITTAL CHECKLIST DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate Building Connected Bid Form; properly completed online Document Acknowledgement: ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed: Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. The following Documents are to be returned with your proposal; a completed bid package will include each of the Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, following documents without exception. Please attach the following documents to your electronic submission signed, and notarized; S5-31. Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. through Building Connected: Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement DBE Schedules completed: Schedule 1 - Affidavit of Non-Collusion Schedule 2 - Regulations of the Department of Procurement Services for Percentages of City and Project Area Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. Residents Working Hours □ Schedule 4 – Statement of Bidders Qualifications Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule 5 - Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects signed, and notarized; S5-31. Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 Exhibit A DBE Requirement for Bidders List; S5-41. Bidder's Financial Statement. Certifications (FAA) DBE Utilization Report; S5-36. Debarment; S5-46 Lobbying: S5-47. Non-Segregated Facilities; S5-58 BABA Certification: S5-51 Sexual Harassment Affidavit: S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Any exclusions, clarifications, or qualifications in your Bid Bond: \$5-54. proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvement Bid Package No.: 1.4

through a pre-bid Request for Information (RFI).

PROCUREMENT – SCHEDULE B: AFFIDAVIT OF DBE/NON-DBE JOINT VENTURE

Complete and return with your bid.

Include as an attachment on Building Connected.

Note: I form.	If <u>all</u> joint venturers are DBEs, a written joint venture agreement between the DBE venturers may be submitted in lieu of this In <u>all proposed joint ventures</u> , each DBE venturer must submit a copy of its current Letter of Certification.
REFER	NFORMATION REQUESTED BY THIS SCHEDULE MUST BE ANSWERED IN THE SPACES PROVIDED. DO NOT R TO YOUR JOINT VENTURE AGREEMENT EXCEPT TO EXPAND ON ANSWERS PROVIDED ON THIS FORM. II TIONAL SPACE IS REQUIRED, ADDITIONAL SHEETS MAY BE ATTACHED.
I.	Name of joint venture:
	Phone number of joint venture:
	Identify each non-DBE venturer(s):
	Phone:
	Contact person for matters concerning DBE compliance:
III.	Identify each non-DBE venturer(s):
	Name of Firm: Address:
	Phone:
	Contact person for matters concerning DBE compliance:
IV.	Describe the role(s) of the DBE venturer(s) in the joint venture:
	Attach a copy of the joint venture agreement. In order to demonstrate the DBE venturer's share in the ownership, com management responsibilities, risks and profits of the joint venture, the proposed joint venture agreement must include spec details related to: (1) the contributions of capital and equipment; (2) work items to be performed by the DBE's own forces; work items to be performed under the supervision of the DBE venturer; and (4) the commitment of management, supervis and operative personnel employed by the DBE to be dedicated to the performance of the project.
	Ownership of the Joint Venture. A. What are the percentage(s) of DBE ownership of the joint venture? DBE ownership percentage(s) Non-DBE ownership percentage(s)
	B. Specify DBE percentages for each of the following (provide narrative descriptions and other details as applicable): Profit and loss sharing: Capital contributions: (a) Dollar amounts of initial contribution: (b) Dollar amounts of anticipated on-going contributions:
	Profit and loss sharing: Capital contributions: (a) Dollar amounts of initial contribution:

IMAGE IS FOR REFERENCE ONLY – USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

PROCUREMENT – SCHEDULE C: DBE LETTER OF INTENT TO PERFORM AS A SUBCONTRACTOR OR SUPPLIER

Complete and return with your bid.

Include as an attachment on Building Connected.

PERFERINCE DELECTORY DELECTORY Project Name:			
Perform as a Subcontractor of Supplier Project Name:			
Project Name:			
From: (Name of DBE Firm) To:			
(Name of DBE Firm) To:		Diu Fackage No	
The DBE status of the undersigned is confirmed by the attached City of Chicago or Illinois Uniform Certification Certification Letter. The undersigned is prepared to perform the following services in connection with the above named project/co more space is required to fully describe the DBE proposed scope of work and/or payment schedule, attach a sheets as necessary. The above described performance is offered for the following price and described terms of payment: Pay Item No./Description Quantity/Unit Price Total Pay Item No./Description Quantity/Unit Price Total Partial Pay Items Grand Total: \$	(Name of DBE Firm)		
The DBE status of the undersigned is confirmed by the attached City of Chicago or Illinois Uniform Certification Certification Letter. The undersigned is prepared to perform the following services in connection with the above named project/co more space is required to fully describe the DBE proposed scope of work and/or payment schedule, attach a sheets as necessary: The above described performance is offered for the following price and described terms of payment: Pay Item No./Description Quantity/Unit Price Total The above described performance is offered for the following price and described terms of payment: Pay Item No./Description Quantity/Unit Price Total Grand Total: S Partial Pay Items For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount Grand Total: S Grand Total: S Grand Total: S Grand Total: S % of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted. NOTICE: If any of the DBE scope of work with the solve of the work that will be subcontracted. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Name/Title-Please Print)	O:		and the City of Chicago.
more space is required to fully describe the DBE proposed scope of work and/or payment schedule, attach a sheets as necessary: The above described performance is offered for the following price and described terms of payment: Pay Item No./Description Quantity/Unit Price Total Pay Item No./Description Quantity/Unit Price Total Grand Total: \$ Partial Pay Items For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount Grand Total: \$ Motive deltar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted. Its the name of the vendor and attach a b explanation, description and pay item number of the work that will be subcontracted. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. [Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) [Name/Title-Please Print]	The DBE status of the undersigned is confirmed by th		
Pay Item No./Description Quantity/Unit Price Total Pay Item No./Description Quantity/Unit Price Total Construction Grand Total: \$	nore space is required to fully describe the DBE pro		
Grand Total: \$	he above described performance is offered for the fo	llowing price and described terms of	payment:
Partial Pay Items For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount SUB-SUBCONTRACTING LEVELS A zero (0) must be shown in each blank if the DBE will not be subcontracting any of the work listed or attached to schedule. % of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a b explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print) (Date)	Pay Item No./Description	Quantity/Unit Price	Total
Partial Pay Items For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount SUB-SUBCONTRACTING LEVELS A zero (0) must be shown in each blank if the DBE will not be subcontracting any of the work listed or attached to schedule. % of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a b explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print) (Date)			
Partial Pay Items For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount Grand Total: \$			
Partial Pay Items For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount Grand Total: \$			
For any of the above items that are partial pay items specifically describe the work and subcontract dollar amount Grand Total: \$	Partial Pay Items	Grand To	tal: \$
SUB-SUBCONTRACTING LEVELS A zero (0) must be shown in each blank if the DBE will not be subcontracting any of the work listed or attached to schedule. % of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a be explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print) (Date)	or any of the above items that are partial pay items s	pecifically describe the work and sub	contract dollar amount(s):
SUB-SUBCONTRACTING LEVELS A zero (0) must be shown in each blank if the DBE will not be subcontracting any of the work listed or attached to schedule. % of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a b explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print) (Date)			
SUB-SUBCONTRACTING LEVELS A zero (0) must be shown in each blank if the DBE will not be subcontracting any of the work listed or attached to schedule. % of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a b explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print) (Date)		Grand To	tal: \$
% of the dollar value of the DBE subcontract that will be subcontracted to non-DBE contractors. % of the dollar value of the DBE subcontract that will be subcontracted to DBE contractors. NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a be explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print)			
NOTICE: If any of the DBE scope of work will be subcontracted, list the name of the vendor and attach a be explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contract the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date)	A zero (0) must be shown in each blank if the DBE will	I not be subcontracting any of the wo	rk listed of attached to this
explanation, description and pay item number of the work that will be subcontracted. The undersigned will enter into a formal written agreement for the above work with you as a Prime Contractor, cor upon your execution of a contract with the CMAR, within three (3) business days of your receipt of a signed contra the CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS REQUIRE ORIGINAL SIGNATURES. (Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print)	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontract	ct that will be subcontracted to non-D	BE contractors.
(Signature of President/Owner/CEO or Authorized Agent of DBE) (Date) (Name/Title-Please Print)	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontrac % of the dollar value of the DBE subcontrac	ct that will be subcontracted to non-Di ct that will be subcontracted to DBE c	BE contractors. ontractors.
(Name/Title-Please Print)	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontrac % of the dollar value of the DBE subcontrac NOTICE: If any of the DBE scope of work will be su explanation, description and pay item number of the "the undersigned will enter into a formal written agreer ipon your execution of a contract with the CMAR, with	t that will be subcontracted to non-Di t that will be subcontracted to DBE c ubcontracted, list the name of the v he work that will be subcontracted ment for the above work with you as a	BE contractors. ontractors. rendor and attach a brief Prime Contractor, condition
	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontrac % of the dollar value of the DBE subcontrac NOTICE: If any of the DBE scope of work will be su explanation, description and pay item number of the the undersigned will enter into a formal written agreer ipon your execution of a contract with the CMAR, with he CMAR.	t that will be subcontracted to non-Di t that will be subcontracted to DBE c ubcontracted, list the name of the v he work that will be subcontracted, nent for the above work with you as a nin three (3) business days of your re-	BE contractors. ontractors. rendor and attach a brief Prime Contractor, condition ceipt of a signed contract fro
(Email & Phone Number)	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontract % of the dollar value of the DBE subcontract VOTICE: If any of the DBE scope of work will be su- explanation, description and pay item number of th fhe undersigned will enter into a formal written agreen upon your execution of a contract with the CMAR, with he CMAR.	that will be subcontracted to non-Di that will be subcontracted to DBE c ubcontracted, list the name of the v he work that will be subcontracted ment for the above work with you as a nin three (3) business days of your re-	BE contractors. ontractors. rendor and attach a brief Prime Contractor, condition ceipt of a signed contract fro
(Email & Phone Number)	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontract % of the dollar value of the DBE subcontract NOTICE: If any of the DBE scope of work will be su explanation, description and pay item number of th he undersigned will enter into a formal written agreen upon your execution of a contract with the CMAR, with he CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS RI (Signature of President/Owner/CEO or Authorized Agent of	that will be subcontracted to non-Di that will be subcontracted to DBE c ubcontracted, list the name of the v he work that will be subcontracted ment for the above work with you as a nin three (3) business days of your re-	BE contractors. ontractors. rendor and attach a brief Prime Contractor, condition ceipt of a signed contract fro
	A zero (0) must be shown in each blank if the DBE will schedule. % of the dollar value of the DBE subcontrac % of the dollar value of the DBE subcontrac NOTICE: If any of the DBE scope of work will be su explanation, description and pay item number of the undersigned will enter into a formal written agreen pon your execution of a contract with the CMAR, with he CMAR. NOTICE: THIS SCHEDULE AND ATTACHMENTS RI (Signature of President/Owner/CEO or Authorized Agent of (Name/Title-Please Print)	that will be subcontracted to non-Di that will be subcontracted to DBE c ubcontracted, list the name of the v he work that will be subcontracted ment for the above work with you as a nin three (3) business days of your re-	BE contractors. ontractors. rendor and attach a brief Prime Contractor, condition ceipt of a signed contract fro

PROCUREMENT – SCHEDULE D: AFFIDAVIT OF PRIME CONTRACTOR REGARDING DISADVANTAGED BUSINESS ENTERPRISE (DBEs)

Complete and return with your bid.

Include as an attachment on Building Connected.

Regard	SCHEDULE D Affidavit of Prime Contractor ling Disadvantaged Business Enterprises (DBEs) (FTA/FHWA and FAA Funded Projects)	
Project Name:		
Department Project No.:		
Bid Package No.:		
State of)	
County (City) of) :ss)	
In connection with the above	re captioned contract, I HEREBY DECLARE AN and duly authorized representative of	ND AFFIRM that I an
	(Name of Prime Contractor)	
and that I have personally reviewed the m Business Enterprises (DBE), Schedule Cs a	aterial and facts set forth in and submitted with the attac and Schedule Bs (if applicable), being such information.	ched Schedules of Disadvar
Names of DBE Firms	Type of Work to be Performed (in accordance with Schedule Cs)	Credit Toward DBE Goal
		S
		s s
		s
		s s
		s s s s s
		s s s s s s s
		s s s s s s s s s
		s s s s s s s s s s s
		s s s s s s s s s s s s s
		s s s s s s s s s s s s s s s s
		s s s s s s s s s s s s s
	Total DBE	S S S S S S S S S S S S S S S S S S S
	Total DBE	S S S S S S S S S S S S S S S S S S

\$5-33

PROCUREMENT – SCHEDULE F: REPORT OF SUBCONTRACTOR SOLICITATIONS

Complete and return with your bid.

Include as an attachment on Building Connected.

DPS Version 04/25/2017		
SCHEDULE F: Report of Subcontract (FHWA, FTA and FAA Funded Cont		
Project Name:		
Project Name: Specification #:		
I, on behalf of		
(Name of reporter) have either personally solicited, or permitted a duly authorized representative contract from the following subcontractors which comprise all DBE and non-D price information on this contract:	of this	
Name of Subcontractor		
Address of Subcontractor		
Contact Person		
Status: DBE Certified?	□Yes	🗆 No
Type of Work Solicited		
Years in Business (if available)		
Annual Gross Receipts (if available)		
······		
Name of Subcontractor		
Address of Subcontractor		
Contact Person		
Status: DBE Certified?	□Yes	🗆 No
Type of Work Solicited		
Years in Business (if available)		
Annual Gross Receipts (if available)		
Name of Subcontractor		
Address of Subcontractor		
Contact Person		
Status: DBE Certified?	□Yes	🗆 No
Type of Work Solicited		
Years in Business (if available)		
Annual Gross Receipts (if available)		
New of Sub-contractory		
Name of Subcontractor		
Address of Subcontractor		
Contact Person		
Status: DBE Certified?		
Type of Work Solicited		
Years in Business (if available) Annual Gross Receipts (if available)		
Annual Gross Receipts (II available)		
Name of Subcontractor		
Address of Subcontractor		
Contact Person		
Status: DBE Certified?	Ves	No
Type of Work Solicited	03	
Years in Business (if available)		
Annual Gross Receipts (if available)		

CMAR Federally Funded Terminal 3 Improvements Instructions and Execution Documents Bid Package No.: 1.1

PROCUREMENT – EXHIBIT A DBE REQUIREMENT FOR BIDDER/PROPOSER LIST

Complete and return with your bid.

Include as an attachment on Building Connected.


	DBE RI	EQUIREMENT FOR BIDDER/PROPOSER LIST
bidd requ on th	ing or proposing on prin ested to provide a list of a his contract. Failure to co	The CMAR is required to maintain a bidders list, consisting of all fin ne contracts and <u>bidding or quoting subcontracts</u> . The bidder/proposer all DBE <u>AND non-DBE subcontractors</u> who bid or quote price informatio operate may result in the bidder/proposer being deemed non-responsive oposer is requested to provide the following information:
Prim	e Contractor (Including a	Il partners to a Joint Venture, if applicable)
	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	
Subo	contractors (all DBE ANI) non-DBE subcontractors)
1.	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	
2.	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	

PROCUREMENT – DBE UTILIZATION REPORT

Complete and return with your bid.

Include as an attachment on Building Connected.

		DBE Utilization F	Report	
NOTICE:	AWARDED A CONTRAC BE REQUIRED TO SUBN	T TO BE COMPLETED AT T CT WITH AN APPROVED DBE MIT THIS REPORT IN ACCORDA IDITION REGARDING DISADV	THE TIME OF BID OR D WMBE/WBE Plan, The ance With The Report	PRIME CONTRACTOR WILL NG REQUIREMENTS STATED
Contract Admi	nistrator:		Bid Package No.	
Phone No			Purchase Order No.	
			Date of Award:	
STATE OF:	()	Utilization Report N	0
COUNTY (CIT	TY) OF: ()		
In connection v	with the above-captioned	contract:		
		I that I am the		
	rized representative of		(Title - Print or Type)	
and doily aprillo	inzed representative of		(Name of Comp any - Print or Typ	e)
		^{mpany)} Minority and Women Busin ng materials for, and renderin	ess Enterprises have bee	
furnished, or ar The following	llowing Disadvantaged, re furnishing and prepari Schedule accurately refl	Minority and Women Busin	ess Enterprises have bee g services stated in the co	(Phone) n contracted with, and have intract agreement.
furnished, or ar The following paid to each to	llowing Disadvantaged, re furnishing and prepari Schedule accurately refl	Minority and Women Busin ng materials for, and rendering	ess Enterprises have bee g services stated in the co	(Phone) n contracted with, and have intract agreement.
furnished, or ar The following paid to each to	Ilowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/M Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the co IBE/WBE sub-agreemen Amount of Contract	(Phone) n contracted with, and have nhract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to	Ilowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee g services stated in the co IBE/WBE sub-agreemen Amount of Contract	(Phone) n contracted with, and have ntract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to	Ilowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/M Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the co IBE/WBE sub-agreemen Amount of Contract	(Phone) n contracted with, and have ntract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to	Ilowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/M Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the co IBE/WBE sub-agreemen Amount of Contract	(Phone) n contracted with, and have ntract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to	Ilowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/M Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the co IBE/WBE sub-agreemen Amount of Contract	(Phone) n contracted with, and have ntract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to DBE/MBI	illowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/M Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the co /IBE/WBE sub-agreemen Amount of Contract S	(Phone) n contracted with, and have ntract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to DBE/MBI	illowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin, lects the value of each DBE/A Indicate Type of Firm (DBE/MBE/WBE)	Amount of Contract	(Phone) n contracted with, and have intract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to DBE/MBI	illowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/A Indicate Type of Firm (DBE/MBE/WBE)	Amount of Contract	(Phone) n contracted with, and have intract agreement. t and the amounts of money Amount Paid To-Date
furnished, or ar The following paid to each to DBE/MBI	Ilowing Disadvantaged, re furnishing and prepari Schedule accurately refl date. E/WBE Firm Name to City: o Prime Contractor:	Minority and Women Busin ng materials for, and renderin lects the value of each DBE/A Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the co /IBE/WBE sub-agreemen Amount of Contract S	(Phone) n contracted with, and have intract agreement. t and the amounts of money Amount Paid To-Date

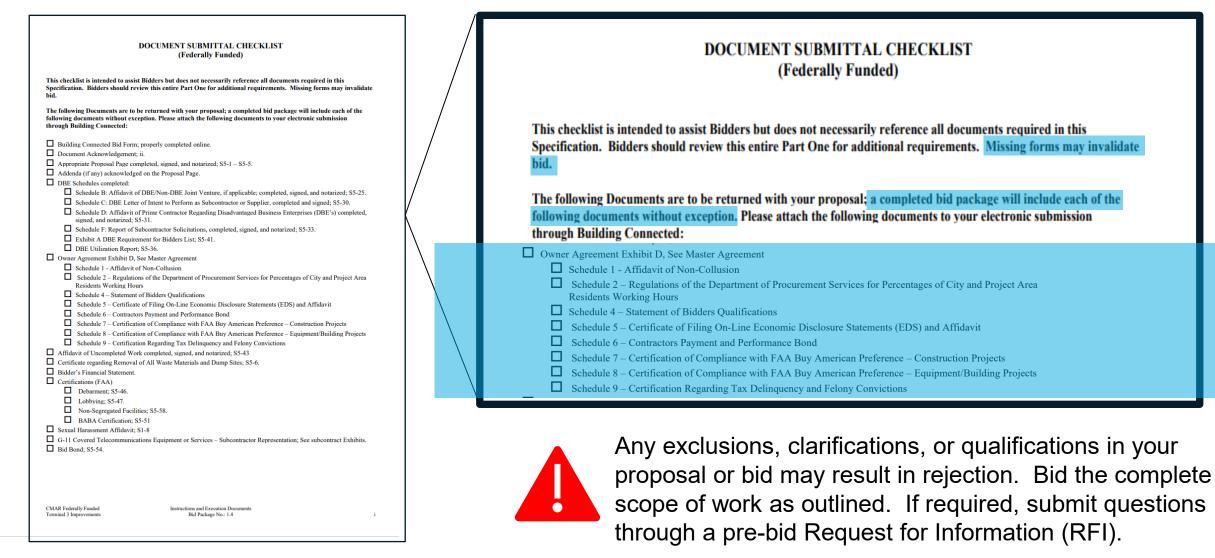

PROCUREMENT – SCHEDULE 1 AFFIDAVIT OF NON-COLLUSION

Complete and return with your bid.

Include as an attachment on Building Connected.

	Construction Management At-Risk Services for O'Hare 21 at O'Hare International Al Chicago Department of Aviation (Specification No.125)
SCHEDULE 1 AFFIDAVIT OF NON-COLLUS	SION
STATE OF ILLINOIS } SS COUNTY OF COOK }	
	, being first duly sworn, deposes and says that:
(1) He/She is	
(Owner, Partner, Authorized Offic	of eer, or Representative or Agent)
(Name of Organization/Firm)	
the Bidder that has submitted the a	attacked Did.
(4) Neither Bidder nor any of i employees, or parties in interest, in conspired, or agreed, directly or in collusive or sham bid in connectio submitted or to refrain from biddin directly or indirectly, sought by ag any other Bidder, firm, or person t other Bidder, or to fix any overhea or to secure through any collusion against the City of Chicago or any (5) The price or prices quoted any collusion, conspiracy, conniva its agents, representatives, owners (6) The Bidder is not barred fr	not a collusive or sham bid; its officers, partners, owners, agents, representatives, neluding this affiant, has in any way colluded, connived, directly, with any other Bidder, firm, or person to submit a n with the Contract for which the attached bid has been ng in connection with such Contract, or has in any manner, greement or collusion or communication or conference with the price or prices in the attached bid or in that of any ad, profit, or cost element of the bid price of any other Bidde , conspiracy, connivance or unlawful agreement any advanta person interested in the proposed Contract; and in the attached Bid are fair and proper and are not tainted by ance, or unlawful agreement on the part of the Bidder or any , employees, or parties in interest, including this affiant. om bidding as a result of having violated Illinois Criminal ging), 720 ILCS 5/33E-4 (Bid rotating) or the Prevailing Wa 10/7.
(Signed)	
(Title)	

PROCUREMENT – SCHEDULE 2 regulations of the department of procurement services for percentages of City and Project Area Residents working hours

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 2

REGULATIONS OF THE DEPARTMENT OF PROCUREMENT SERVICES FOR PERCENTAGES OF CITY AND PROJECT AREA RESIDENTS WORKING HOURS

A. GENERAL PROVISIONS

1. Statement of Authority

These regulations are issued pursuant to the following Section of the Municipal Code of Chicago:

Section 2-92-330 of Municipal Code of Chicago establishes a minimum number of hours to be performed by City Residents as well as a minimum number of hours to be performed by Project Area residents. Subsection (a) requires the Chief Procurement Officer to "develop standards and procedures for reducing or waiving these minimum percentages level of Chicagoans work hours for eligible residents when a bidder or contractor can demonstrate the impracticality or excessive cost of complying with these percentage levels for particular contracts or classes of employees." Subsection (f) authorizes the Chief Procurement Officer to "adopt, promulgate and enforce reasonable rules and regulations pertaining to the administration and enforcement" of the Section.

Subsection (a) provides that, for any construction project advertised, or if not advertised, awarded, by the City that has an estimated contract value of \$100,000 or more, and where not otherwise prohibited by federal, state or local law, the total hours worked by persons on the site of the construction project by employees of the contractor and subcontractors shall be performed (i) at least 50 percent by City Residents; and (ii) at least 7.5 percent by Project Area residents. Work hours performed by Project Area residents for purposes of calculating the minimum work hour percentage required to be performed by City Residents.

2. Application and Statement of Purpose

These regulations describe how the ordinance will be administered and enforced, including the right of the Chief Procurement Officer to waive the residency requirement.

B. <u>DEFINITIONS</u>

Unless otherwise specified, whenever used in these regulations, the following terms have the following meanings:

"City Residents" means persons domiciled within the City of Chicago.

Exhibit D to the Agreement Required Subcontract Provisions

PROCUREMENT – SCHEDULE 4 STATEMENT OF BIDDER'S QUALIFICATIONS

Complete and return with your bid.

Include as an attachment on Building Connected.

	Construction Management	At-Risk Services for O Chicago Department	Hare 21 at O'Hare International Airpo of Aviation (Specification No.125827
SCHEDULE 4 STATEMENT OF BIDDE	R'S QUALIFICATIONS		
At the request of the City, the capability of the Bidder to pe		additional infor	mation regarding the
Bidder:			
Submitted By:			
Title:			
Permanent Main Office Add	dress:		
Local Address:			
How many years operating a			
How many years operating a List of recently completed cc			
List of recently completed co	ontracts of similar dollar va	lue and scope o	f work:
List of recently completed co	ontracts of similar dollar va	lue and scope o	f work:
List of recently completed co	ontracts of similar dollar va	lue and scope o	f work:
List of recently completed cc Name/Address 1. 2. 3. 4. 5. 6. 7.	ontracts of similar dollar va	lue and scope o	f work:
List of recently completed co	Dollar Amount	Vear of Contract	f work: Nature of Project
List of recently completed cc Name/Address 1. 2. 3. 4. 5. 6. 7.	Dollar Amount	Vear of Contract	f work: Nature of Project
List of recently completed co	Dollar Amount Do	Vear of Contract	f work: Nature of Project
Name/Address 1. 2. 3. 4. 5. 6. 7. 8. The undersigned hereby auth requested by the City of Chic	Dollar Amount	Vear of Contract	f work: Nature of Project

PROCUREMENT – SCHEDULE 5 CERTIFICATE OF FILING ON-LINE ECONOMIC DISCLOSURE (EDS) STATEMENTS AND AFFIDAVIT

The bidder shall complete an online EDS prior to the bid due date. A bidder who does not file an electronic EDS prior to the bid due date may be found non-responsible and its bid rejected. If you are unable to complete the online EDS and print a Certificate of Filing prior to the bid/proposal due date, the City will accept a paper EDS provided written justification is submitted with the bid/proposal explaining the Bidder's good faith efforts to complete it before the bid/proposal due date and the reasons why on line EDS could not be completed

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 5

INSTRUCTIONS FOR COMPLETING ECONOMIC DISCLOSURE STATEMENT AND AFFIDAVIT (EDS) ON-LINE

The Bidder shall complete an online EDS prior to the bid due date. A Bidder who does not file an electronic EDS prior to the bid due date may be found non-responsive and its bid rejected. If you are unable to complete the online EDS and print a Certificate of Filing prior to the bid/proposal due date, the City will accept a paper EDS provided written justification is submitted with the bid/proposal explaining the Bidder's good faith efforts to complete it before the bid/proposal due date and the reasons why on line EDS could not be completed.

1.1. ONLINE EDS FILING REQUIRED PRIOR TO BID OPENING

The Bidder must complete an online EDS prior to the bid opening date.

A Bidder that does not file an electronic EDS prior to the bid opening will be found nonresponsive and its bid will be rejected, unless a paper EDS and justification is submitted with the bid as described above. Paper EDS forms may be obtained on the City's wesite at: http://www.cityofchicago.org/city/en/depts/dps/provdrs/comp/svcs/economic_disclosurestate mentseds.html

1.2. ONLINE EDS WEB LINK

The web link for the Online EDS is https://webapps.cityofchicago.org/EDSWeb

1.3. ONLINE EDS NUMBER

Upon completion of the online EDS submission process, the Proposer will be provided an EDS number. Bidders should provide this number here:

EDS Number:

1.4. ONLINE EDS CERTIFICATION OF FILING

Upon completion of the online submission process, the Proposer will be able to print a hard copy Certificate of Filing. The Proposer should submit the signed Certificate of Filing with its bid. Please insert your Certification of Filing following this page.

A Proposer that does not include a signed Certificate of Filing with its bid must provide it upon the request of the Chief Procurement Officer.

1.5. PREPARATION CHECKLIST FOR REGISTRATION

To expedite and ease your registration process, we recommend that you collect the following information prior to registering for an Online EDS user account:

Exhibit D to the Agreement Required Subcontract Provisions

PROCUREMENT – SCHEDULE 6 CONTRACTOR'S PERFORMANCE & PAYMENT BOND RIDER ATTACHED

Complete and return with your bid.

Include as an attachment on Building Connected.

IMAGE IS FOR REFERENCE ONLY – USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 6 CONTRACTOR'S PERFORMANCE AND PAYMENT BOND RIDER ATTACHED

CONTRACTOR'S PERFORMANCE & PAYMENT BOND

Know All Men by these Presents, That we,

COMPANY NAME STREET ADDRESS CITY, STATE ZIP CODE

Principal, hereinafter referred to as Contractor, and of the County of and State of OF CHICAGO in the penal sum of: , Surety , are held and firmly bound unto the CITY

--- Dollar Amount in Words and 00/100 Dollars (\$) --lawful money of the United States, for the payment of which sum of money, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

Sealed with our seals and dated this day of

, 20 .

The Condition of the Above Obligation is such, that whereas the above bounden Contractor has entered into a certain contract with the City of Chicago, bearing

Contract (PO) No. XXXXX and Specification No. XXXXXX all in conformity with said contract, for,

Furnishing the City of Chicago, Name of User Department, all labor, tools, material, and equipment required and necessary for the project known as:

PROJECT DESCRIPTION

* The attached rider is incorporated herein by reference.

Now, if the said Contractor shall in all respects well and truly keep and perform the said contract on its part, in accordance with the terms and provisions of all of the Contract Documents comprising said contract, and in the time and manner therein prescribed, and further shall save, indemnify, and keep harmless the City of Chicago against all loss, damages, claims, liabilities, judgments, costs and expenses which may in anywise accrue against said City of Chicago, in consequence of the granting of which may in anywise result therefrom, or which may result from strict liability, or which may in anywise result therefrom, or which may result from strict liability, or which may in anywise result strength, or in connection with, work performed or to be performed under said contract by said Contractor, its Agents, Employees or Workmen, assignces, subcontractors, or anyone else, in any respect whatever, or which may result on account of any infringement of any patent by reason of the materials, machinery, devices or apparatus used in the performance of said contract, and moreover, shall pay to said City any sum or sums of money determined by the Purchasing Agent, and/or by a court of competent jurisdiction, to be due said City by reason of any failure or neglect in the performance of the requirements of said contract, wherefore the said Purchasing Agent shall have elected to suspend or cancel the same, and shall pay all claims and demands whatsoever, which may accrue to each and every materialman and subcontractors, and to each and every person who shall be employed by the said Contractor or by its assignees and subcontractors, in or about the performance of said contract, and with wages paid at prevailing wage rates if so required by said contract, and shall insuit its liability to pay the compensation, and shall pay all claims and demands for compensation which may accrue to each and every person who shall be employed by them

Exhibit D to the Agreement Required Subcontract Provisions D-46|Page

PROCUREMENT – SCHEDULE 7 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE CONSTRUCTION PROJECTS

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 7 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE CONSTRUCTION PROJECTS

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with its proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101, BABA and other related Made in America Laws, U.S. statutes, guidance, and FAA policies, by selecting one of the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (i.e., not both) by inserting a checkmark (\checkmark) or the letter "X".

- □ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related U.S. statutes, guidance, and policies of the FAA by:
 - a) Only installing iron, steel and manufactured products produced in the United States;
 - b) Only installing construction materials defined as: an article, material, or supply other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials; aggregates such as stone, sand, or gravel; or aggregate binding agents or additives that are or consist primarily of non-ferrous metals; plastic and polymer-based products (including polyvinylchloride, composite building materials, and polymers used in fiber optic cables); glass (including optic glass); lumber or drywall that have been manufactured in the United States.
 - Installing manufactured products for which the Federal Aviation Administration (FAA) has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing; or
 - d) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- a) To provide to the Airport Sponsor or the FAA evidence that documents the source and origin of the iron, steel, and/or manufactured product.
- b) To faithfully comply with providing U.S. domestic products.
- c) To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

d) Certify that all construction materials used in the project are manufactured in the U.S.

[□] The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:

a) To the submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the responsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested.

PROCUREMENT – SCHEDULE 8 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – EQUIPMENT/BUILDING PROJECTS

Complete and return with your bid.

Include as an attachment on Building Connected.

SCHEDULE 8 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – EQUIPMENT/BUILDING PROJECTS

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with their proposal. The bidder or offeror must indicate how they intend to comply with 49 USC 50101, and other Made in America Laws, U.S. statutes, guidance, and FAA policies by selecting one on the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (not both) by inserting a checkmark (\checkmark) or the letter "X".

- □ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related U.S. statutes, guidance, and policies of the FAA by:
 - a) Only installing steel and manufactured products produced in the United States;
 - b) Only installing construction materials defined as: an article, material, or supply other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials; aggregates such as stone, sand, or gravel; or aggregate binding agents or additives that are or consist primarily of non-ferrous metals; plastic and polymer-based products (including polyvinylchloride, composite building materials, and polymers used in fiber optic cables); glass (including optic glass); lumber or drywall that have been manufactured in the United States.
 - Installing manufactured products for which the Federal Aviation Administration (FAA) has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing; or
 - Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- To provide to the Airport Sponsor or FAA evidence that documents the source and origin of the steel and manufactured product.
- b) To faithfully comply with providing U.S. domestic product.
- c) To furnish U.S. domestic product for any waiver request that the FAA rejects.
- d) To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.
- ☐ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for a Type 3 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:
 - To submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the responsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested.

Exhibit D to the Agreement Required Subcontract Provisions

PROCUREMENT – SCHEDULE 9 CERTIFICATION REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

Complete and return with your bid.

Include as an attachment on Building Connected. DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 9

CERTIFICATION REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

The applicant must complete the following two certification statements. The applicant must indicate its current status as it relates to tax delinquency and felony conviction by inserting a checkmark (\checkmark) in the space following the applicable response. The applicant agrees that, if awarded a contract resulting from this solicitation, it will incorporate this provision for certification in all lower tier subcontracts.

Certifications

- The applicant represents that it is () is not () a corporation that has any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.
- 2) The applicant represents that it is () is not () is not a corporation that was convicted of a criminal violation under any Federal law within the preceding 24 months.

Note

If an applicant responds in the affirmative to either of the above representations, the applicant is ineligible to receive an award unless the sponsor has received notification from the agency suspension and debarment official (SDO) that the SDO has considered suspension or debarment and determined that further action is not required to protect the Government's interests. The applicant therefore must provide information to the owner about its tax liability or conviction to the Owner, who will then notify the FAA Airports District Office, which will then notify the agency's SDO to facilitate completion of the required considerations before award decisions are made.

Term Definitions

Felony conviction: Felony conviction means a conviction within the preceding twentyfour (24) months of a felony criminal violation under any Federal law and includes conviction of an offense defined in a section of the U.S. code that specifically classifies the offense as a felony and conviction of an offense that is classified as a felony under 18 U.S.C. § 3559.

Tax Delinquency: A tax delinquency is any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted, or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected:	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. BABA Certification; S5-51.
CMAR Federally Funded Instructions and Execution Documents CMAR Federally Funded Instructions and Execution Documents id Package No.: 1.4 i	Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

PROCUREMENT – AFFIDAVIT OF UNCOMPLETED WORK

			OF UNCO! rm by either ty												DPS Version 04/25/2017					
PART I. WORK UNDER CONTRACT List below all work you have under contract as either a prime contractor or a subcontractor, including al pending low bids									+	PART III. WORK SUBCONTRACTED TO OTHERS. List below the work, according to each contract on the preceding nage, which you have asheotrated to others. Do NOT include work to be performed by another prime contractor in a joint venture. No lyork may be indicated as subcontracted to others on awards pending. If no work is subcontracted to others, show VONE.										
not yet awarded or reje		r contract as et	iner a prime co	ntractor or a s	subcontractor, 1	netuding a	ii pendi	ing low blus	4/25/2017						1 2 3 4 5					
	1	2	3	4	5	Awa	ards	٦							SUBCONTRACTOR	_				
		-	-		-	Pene					1	2		3	TYPE OF WORK					
PROJECT														_	SUBCONTRACT PRICE					
CONTRACT WITH								1	2						- AMOUNT UNCOMPLETED					
ESTIMATED								-							AMOUNTUNCOMPLETED					
COMPLETION DATE												-	-	+	SUBCONTRACTOR					
TOTAL CONTRACT PRICE								TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	L					+	TYPE OF WORK	_
UNCOMPLETED									.)					+	SUBCONTRACT PRICE					
DOLLAR VALUE							_		STEEL						AMOUNT UNCOMPLETED					
PART II. UNCOMPLETED WORK TO BE DONE WITH YOUR OWN FORCES.					ous						SUBCONTRACTOR									
List below the uncompleted dollar value of work for each contract to be completed with your own forces including all work indicated as awards pending. All work subcontracted TO others will be listed on PART III of this form. In a joint venture,					9						TYPE OF WORK									
mulcaled as awards pe	nung. An v	vork subcontrac	teu 10 others	will be listed (OILLAKT III OI	uns torm	. maje	sint venture,	1	1					SUDCONTRACT DRICE					

SUBMIT WITH YOUR BID

AS AN ATTACHMENT ON BUILDING CONNECTED, SIGNED AND NOTARIZED

ND FILL DC DV UNDATION K K CAUSON & PILE) T. GRWAY AL RE ACCAULKING VEWER & DRAIN RUCTURES AVEMENT MARKING	(DAM, CAM, FAM)										1 I		SUBCONTRACTOR				
ONESATION Implicit on the second	AGGREGATE BASE						D.		-			-					
ALSSON & PULE I <	AND FILL						- K				1 I		TYPE OF WORK				
AMSON & PLLE; Image: Control of the service of the							RT.		-				SUBCONTRACT PRICE				
INCLUENS Inclusion																	
WER & DANN INTO Image: State of the s							AL						AMOUNT UNCOMPLETED				
Interconstant Interconstant<																	
AINTING Image: Constraint of the index index of th							O CAUI	KING			1 I						
MILEON Image: Constraint of the section and Exection Documents Bistraction and Exection Documents S2-45							DI IO					_					
AVEMENG Image: Second Decements SS-4 Image: Second Decements SS-4	PAINTING						pus				1 I				including ALL subcor	stract work, ALL pendi	ing low bid
Image: Constraint of the section and Section and Section and Section Documents Solution and Section Documents S	DAVEMENT MADVING								-			-	not yet awarded or rejected, and AL	 estimated completion dates. 			
ANDSCAPING IN IN INVESTIGATION IN INVEST	PAVEMENT MARKING						ľ				1 I						
ANDSCAPING IN IN INVESTIGATION IN INVEST	SIGNING													Signed			
MARK Hole Image: Second Decenterity SS-43												_	this day of	Company			
EMOLITION IN INTEGENDE Parket No. 1 A S-45 CMAR Federally Field Interviews and Execution Documents Bid Package No. 1 A S5-43 CMAR Federally Field Interviews and Execution Documents Bid Package No. 1 A S5-43 CMAR Federally Field Interviews and Execution Documents Bid Package No. 1 A S5-43	LANDSCAPING										1 I		Ma commission anning	Address			
ENCING Intracional Execution Documents Bid Package No. 1.4 CMAR Federally Fauld Intracional Bid Package No. 1.4 CMAR Federally Fauld CMAR Federally Fault CMAR Federally Fau	DEMOLITION								-			-	My commission expires				
CMAR Federally Field Instructions and Execution Documents Bid Package No.: 1.4 S5-43 CMAR Federally Field Instructions and Execution Documents Bid Package No.: 1.4 S5-45 CMAR Federally Field Instructions and Execution Documents Bid Package No.: 1.4 S5-45	DEMOLITION																
CMAR Federally Field Instructions and Execution Documents Bid Package No.: 1.4 S5-43 CMAR Federally Field Instructions and Execution Documents Bid Package No.: 1.4 S5-45 CMAR Federally Field Instructions and Execution Documents Bid Package No.: 1.4 S5-45	FENCING						- 1					_					
CMAR Federally Fasded Instructions and Execution Documents Bid Package No. 1.4 S5-45 Terminal 3 Improvements Bid Package No. 1.4 S5-45																	
CMAR Federally Fasded Instructions and Execution Documents Bid Package No. 1.4 S5-45 Terminal 3 Improvements Bid Package No. 1.4 S5-45																	
CMAR Federally Fasded Instructions and Execution Documents Bid Package No. 1.4 S5-45 Terminal 3 Improvements Bid Package No. 1.4 S5-45												_					
CMAR Federally Fasded Instructions and Execution Documents Bid Package No. 1.4 S5-45 Terminal 3 Improvements Bid Package No. 1.4 S5-45																	
CMAR Federally Fasded Instructions and Execution Documents Bid Package No. 1.4 S5-45 Terminal 3 Improvements Bid Package No. 1.4 S5-45													CMAR Enderally Funded	Instructions and Execution	Documents		
Terminil 3 Improvements Bid Package No: 1.4 \$5-43													Terminal 3 Improvements			S5-45	
CMAR Federally Funded Instructions and Execution Documents	CMAR Federally Funded	Inst				ee 10											
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4 55-44	Terminal 3 improvements		Biu Fackage No.	0.174		50-40											
CMAR Fidenity Finded Instructions and Exercise Documents Terminal 3 Improvements Biel Packago No: 1.4 S5-44																	
CMAR Federally Funded Instructions and Execution Documents Terminal J Improvements Bid Package No.: 1.4 S5-44																	
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements II-14 S5-44																	
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4 S5-44														1			
CMAR Federality Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4 S5-44														1			
Terminal J Improvements Bid Package No.: 1.4 S5-44						CMAR	Federally Funde		Instructio	ons and Execution Doc	cuments			1			
						Termina	1 3 Improvement	5					S5-44	1			
														1			
														1			

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal: a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledged on the Proposal Page. DBE Schedules completed. Schedule D: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement Schedule 2 - Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours Schedule 4 - Centrification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 5 - Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 8 - Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 <td< td=""><td>This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. BABA Certification; S5-51</td></td<>	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. BABA Certification; S5-51
CMAR Federally Funded Instructions and Execution Documents CMAR Federally Funded Instructions and Execution Documents iii d Package No.: 1.4 i	Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

PROCUREMENT – CERTIFICATE REGARDING REMOVAL OF ALL WASTE MATERIALS AND IDENTIFICATION OF ALL LEGAL DUMP SITES

Complete and return with your bid. If this does not apply to your trade, mark as NA.

Include as an attachment on Building Connected.

Contractor to show here the name	he and location of the ultimate disposal site he/she is proposing to use for the subject project:
SPECIFY THE TYPE OF MATI	ERIALS TO BE DISPOSED OF:
LEGAL NAME OF LANDFILL	/DISPOSAL SITE:
(The Contractor must provide t manifests, etc.)	to the Commissioner or his/her designated representative with copies of all dump tickets
LOCATION ADDRESS:	
PHONE:	
CONTACT PERSON:	
Disposal site submitted shall b Demolition Debris received for t that may be necessary.	be of sufficient capacity as to insure acceptance of the volume of Construction and/o the period of this Contract. These disposal sites must meet all zoning and other requirement
	arement Officer, the Contractor shall submit copies of all contractual agreements, sanitary or these disposal site(s) proposed by the Contractor.
(Revised 6/30/2000)	

CONTRACTORS A FEIDAVIT DECADDINC DEMOVAL OF ALL

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents to your electronic submission through Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledged on the Proposal Page. DBE Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Non-Collusion Schedule J: Affidavit of Non-Collusion Schedule 1- Affidavit of Non-Collusion Schedule 1- Cartification of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours Schedule 4- Statement of Bidders Qualifications Schedule 4- Contractors Payment and Performance Bond Schedule 8- Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8- Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9- Certification of Compliance with FAA Buy American Preference – Equip	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. BABA Certification; S5-51.
CMAR Folerally Funded Instructions and Execution Documents CMAR Folerally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4	Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions

through a pre-bid Request for Information (RFI).

PROCUREMENT – BIDDER'S FINANCIAL STATEMENT

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a financial statement dated not earlier then the end of said Bidder's last fiscal year period. This will be kept on file by the Construction Manager as a representative statement for a period of one year only. If a Bidder does not have such statement on file, it must submit a copy with its bid. Failure to have a current financial statement on file at the Construction Manager at time of bid opening may be cause for the rejection of the Trade Contractor's Bid

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

ensure that any contract entered into pursuant to this advertisement, disadvantaged business enterprises will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award."

B. Affidavit of Non-Collusion

Each Bidder shall fully execute an affidavit, in the form provided, to the effect that the Bidder has not colluded with any other person, firm, or corporation in regard to any bid submitted. Such affidavit shall be attached to the bid.

C. DBE Commitments

The goal for DBE participation for this Contract is 21% DBE.^{*} Each Bidder shall submit with its Bid Schedule Cs and Schedule D, affidavits and supporting documents describing the extent to which DBE firms will participate in the Contract in accordance with Schedule 3 "Special Conditions Regarding DBE Participation."

D. Affidavit of Uncompleted Work

The Bidder is required to submit a fully executed Affidavit of Uncompleted Work, which declares, among other things, the value and estimated completion date of all uncompleted contracts to be completed with Bidder's own forces and to be subcontracted to others. Such affidavit shall be attached to the bid on the form provided.

E. Bidder's Financial Statement

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a financial statement dated not earlier then the end of said Bidder's last fiscal year period. This will be kept on file by the Construction Manager as a representative statement for a period of one year only. If a Bidder does not have such statement on file, it must submit a copy with its bid. Failure to have a current financial statement on file at the Construction Manager at time of bid opening may be cause for the rejection of the Trade Contractor's Bid.

F. Disclosure Affidavit

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a fully executed Disclosure Affidavit. If a Bidder does not have such statement on file, it must submit a copy with its bid.

G. Statement of Bidder's Qualifications

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a fully executed Statement of Bidder's Qualifications or a Qualification Submittal in response to a Request for Qualifications (RFQ). Construction Manager reserves the right to request additional information regarding the capability of the Bidder to perform the Contract.

H. Economic Disclosure Statements (EDS)

* The overall contract goal for is 21% DBE, with a construction sub-goal of20%. In consultation with the City a given trade bid package may have a different DBE goal specific to that bid package, and individual subcontracts may have different DBE goals.

Exhibit D to the Agreement Required Subcontract Provisions

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected:	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement.
Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Schedule 7 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 8 – Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51	 Didder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51
Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54. Security Funded Instructions and Excertion Documents Bid Package No.: 1.4 i	Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

PROCUREMENT – FAA CERTIFICATIONS

CERTIFICATE REGARDING DEBARMENT AND SUSPENSION		CERTIFICATION OF NONSEGREGATED FACILITIES	
By submitting a bid/proposal under this solicitation, the bidder or offeror certifies that a then bidder or offeror submits its proposal that neither it nor its principals are presently debare suspended by any Federal department or agency from participation in this transaction. CERTIFICATION REGARDING DEBARMENT AND SUSPENSION (SUCCESSFL REGARDING LOWER TIER PARTICIPANTS) The successful bidder, by administering each lower tier subcontract that exceeds \$25,000 as transaction [*] , must verify each lower tier participant of a "covered transaction" under the pro- presently debarred or otherwise disqualified from participation in this federally assisted pro- successful bidder will accomplish this by: 1. Checking the System for Award Management at website: http://www.sam.gov 2. Collecting a certification statement similar to the Certificate Regarding Debarmen	me the CERTIFICATION REGARDING LOBBYING AND INFLUENCT The Contractor certifies, to the best of his or her knowledge and belief, 1) No Federal appropriated funds have been paid or will be paid, by to any person for influencing or attempting to influence an officer or en of Congress, an officer or employee of Congress, or an employee of a N ornenction with the awarding of any Federal contract, the making of an any Federal loan, the entering into of any cooperative agreement, and th renewal, amendment, or modification of any Federal contract, grant, loo 2) If any funds other than Federal appropriated funds have been pa	permit his employees to perform their services at any location under his control where segregated facilities are maintained. The federally-assisted construction contractor agrees that a breach of this certification is a violation of the Equal Opportunity Clause in this contract. As used in this certification, the term "segregated facilities" means any waiting rooms, work areas, performs, and washrooms, restaurants and other eating areas, time clocks, locker rooms and other storage or dressing areas, parking lots, drinking fountains, recreation or entertainment areas, transportation, and housing facilities provided for employees which are segregated by explicit directives or are, in fact, segregated on the basis of race, color, religion, or national origin because of habit, local custom, or any other reason. The federally-assisted construction contractor agrees that (except where the base bits of base) to be the set of the transportation or a transportation is the base of the interval.	17 IFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – CONSTRUCTION PROJECTS d responsiveness, the bidder or offeror must complete, sign, date, and submit this certification a proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101, related Made in America Laws, U.S. statnets, guidance, and FAA policies, by selecting one of tification statements. These statements are mutually exclusive. Bidder must select one or the th) by inserting a checkmark (*) or the letter "X". or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related natures, guidance, and policies of the FAA by: Duy installing incursed and manufactured products produced in the United States;
 Concerning a certification statement similar to the Certificate Regarding Department Suspension (Bidder or Offeror), above. 	for influencing or attempting to influence an officer or employee of any an officer or employee of Congress, or an employee of a Member of Co Federal contract, grant, loan, or cooperative agreement, the undersigned	as she or he has obtained identical certifications from proposed subcontractors for specific time periods) she or he will obtain identical certifications from proposed subcontractors prior to the award of	Only installing construction materials defined as: an article, material, or supply – other than an tem of primarily iron or steel; a manufactured product; cement and cementitious materials;

SUBMIT ONE (1) OF EACH FAA CERTIFICATION WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED

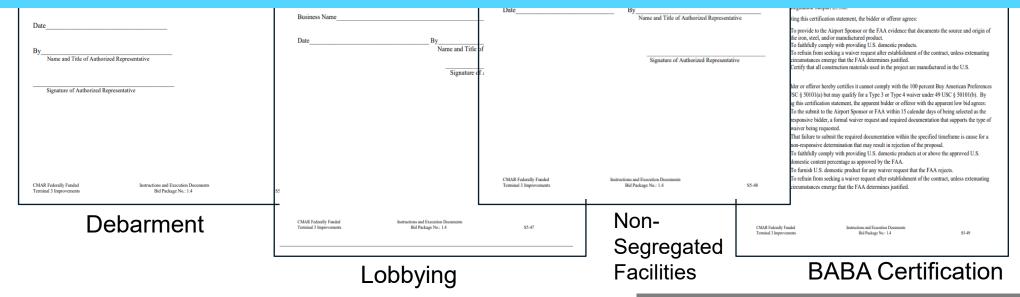


IMAGE IS FOR REFERENCE ONLY - USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents to your electronic submission through Building Connected Bid Form; properly completed online. Description of the proposal Page completed, signed, and notarized; 55-1 – 55-5. Addenda (if any) acknowledgement; ii. DBE Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed, signed, and notarized; 55-25. Schedule D: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; 55-30. Schedule D: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; 55-30. Schedule D: Affidavit of OBE/Non-DBE Joint Venture, if applicable; completed and signed; 55-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; 55-31. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; 55-35. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; 55-36. Owner Agreement Exhibit D, See Master Agreement Schedule 1- Affidavit of Non-Collusion Schedule 1- Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours Schedule 4 – Statement of Bidders Qualifications Schedule 4 – Statement of Bidders Qualifications Schedule 4 – Certificator of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects Schedule 9 – Certification of C	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits.
Certifications (FAA) Debarment; SS-46. Lobbying; SS-47. Non-Segregated Facilities; SS-58. BABA Certification; SS-51 Sexual Harassment Affdavit; S1-8 Constructions and Execution Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54.	 Bid Bond; S5-54. Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If

the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

S1-8

PROCUREMENT – SEXUAL HARASSMENT AFFIDAVIT

Complete and return with your bid.

Include as an attachment on Building Connected.

SEXUAL HARASSMENT POLICY AFFIDAVIT (SECTION 2-92-612)

The policy prohibiting sexual harassment as described in Section 2-92-612 of the Municipal Code of Chicago ("MCC") is applicable to contract spaid from funds belonging to or administered by the City. Contract title:

Specification #:_____

In accordance with requirements set forth in Section 2-92-612 of the MCC, Contractor hereby attests that Contractor has a written policy prohibiting sexual harassment in compliance with Section 6-10-040 of the MCC.

In accordance with Section 6-10-040 of the MCC, Contractor's written policy prohibiting sexual harassment shall include, at a minimum, the following information:

(i) a statement that sexual harassment is illegal in Chicago;

(ii) the following definition of sexual harassment: ""Sexual harassment' means any (i) unwelcome sexual advances or unwelcome conduct of a sexual nature; or (ii) requests for sexual favors or conduct of a sexual nature when (1) submission to such conduct is made either explicitly or implicitly a term or condition of an individual's employment, or (2) submission to or rejection of such conduct by an individual is used as the basis for any employment decision affecting the individual, or (3) such conduct has the purpose or effect of substantially interfering with an individual's work performance or creating an intimidating, hostile, or offensive working environment; or (iii) sexual misconduct, which means any behavior of a sexual nature which also involves coercion, abuse of authority, or misuse of an individual's employment position.";

(iii) a requirement that all employees participate in: (1) sexual harassment prevention training annually, (a) Employees shall participate in a minimum of one hour of sexual harassment prevention training annually, and (b) Anyone who supervises or manages employees shall participate in a minimum of two hours of sexual harassment prevention training annually, and (2) one hour of bystander training annually;

(iv) Examples of prohibited conduct that constitute sexual harassment;

Terminal 3 Improvements


(v) Details on: (1) how an individual can report an allegation of sexual harassment, including, as appropriate, instructions on how to make a confidential report, with an internal complaint form, to a manager, employer's corporate headquarters or human resources department, or other internal reporting mechanism; and (2) legal services, including governmental, available to employees who may be victims of sexual harassment; and

(vi) A statement that retaliation for reporting sexual harassment is illegal in Chicago.

Contractor understands that it may be required to produce records to the CPO to verify the information provided. Under penalty of perjury the person signing below: (1) warrants that he/she is authorized to execute this Affidavit on behalf of Contractor, and (2) warrants that all certifications and statements contained in this Affidavit are true, accurate, and complete as of the date of execution.

Name of Contractor:	
	or Type)
Signature of Authorized Officer:	¥# /
	(Signature)
Title of Signatory:	
(Print	or Type)
State of	
County of	
	efore me on (date) by rson/s making statement).
(Signature of Notary Public)	
(Seal)	
()	
CMAR Federally Funded	Instructions and Execution Documents

Bid Package No.: 1.4

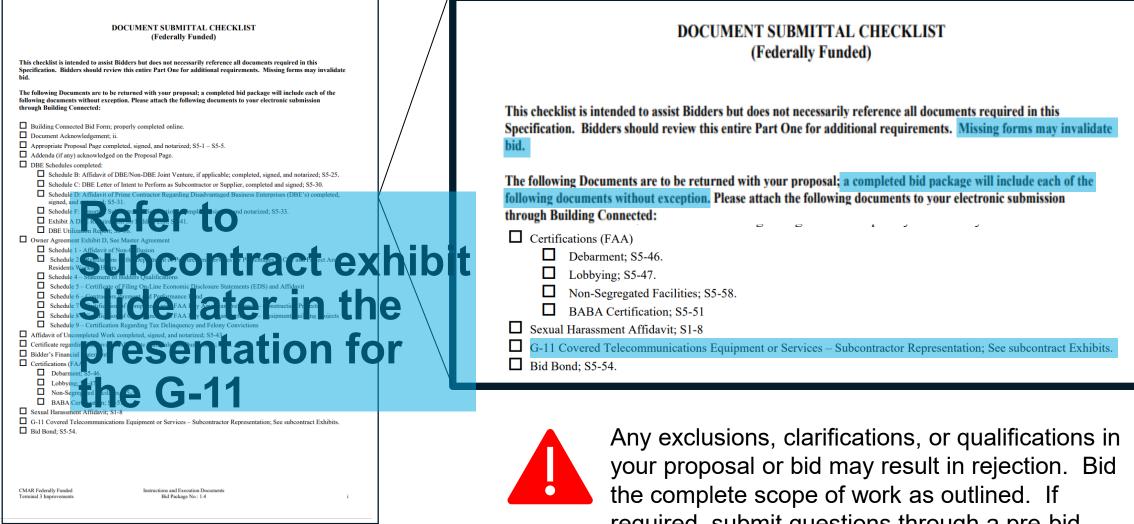

required, submit questions through a pre-bid Request for Information (RFI).

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Building Connected Bid Form; properly completed online. Decoment Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledgement; ii. DBE Schedules completed. Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule D: Affidavit of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement Schedule 1- Affidavit of Non-Collusion Schedule 4- Statement of Bidders Qualifications Schedule 4- Centification of Compliance with FAA Buy American Preference – Construction Projects Schedule 6- Centrification of Compliance with FAA Buy American Preference – Equipment/Building Projects	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51
Schedule 9 - Certification Regarding Tax Delinquency and Felony Convictions Affidavit of Uncompleted Work completed, signed, and notarized; \$5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; \$5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; \$5-46. Lobbying; \$5-47.	 Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54.
Non-Segregated Facilities; S5-58. BABA Certification; S5-51 Sexual Harassment Affdavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54. CMAR Federally Funded Terminal 3 Improvements Bid Package No: 1.4	Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If

required, submit questions through a pre-bid Request for Information (RFI).

PROCUREMENT – BID BOND

Bid Bonds are Required. Follow all instructions.

Include as an attachment on Building Connected.

	INSTRUC	S FOR BID BOND FOR	4						
	Bidders/Proposer	e these instructions to you	r surety.						
1.	The Bond must be on the CMAR's for	substitutions will be accept	ible.						
2.	Copies of the form are acceptable. How the paper, and page 2 on the opposite sid	DPS Version 04/25/2017		ł					
3.	The amount of the Bond must be that st the bond should be expressed as a percer	KNOW ALL MEN BY THESE F	BID BOND RESENTS, that we						
4.	All blank spaces to be filled in must be indicated. Determinations of legibility be accepted, nor will any Bond form on	Principal, hereinafter called the P under the laws of the laws of the !	incipal, and	iress or legal title of Subcontractor) as itle of Surety) a corporation duly organized after called the Surety, are held and firmly					
5.	Insert the full legal name and business a form. If the Bidder/ Proposer is biddin stated in the same space as the full legal	bound unto CLARK - W.E. O'N bid for the payment of which sum	EIL JV, hereinafter called the Obligee, in the well and truly to be made, the said Principal a accessors and assigns, jointly and severally, fi	sum of Ten percent (10%) of the amount and the said Surety, bind ourselves, our					
6.	The address of the Principal must be cor as well, as bonds to be returned will be n	WHEREAS, the Principal has submitted a Terminal 3 Improvements, Chicago, IL	bid in accordance with the Bid Package for Specification	Section(s), for					
7.	The Bond must include the Surety's name	NOW. THEREFORE, if the Obli	ee shall accept the bid of the Principal and the	e Principal shall, within the specified					
8.	The Bid Package number must appear or	period of time, one hundred twen	y (120) days, enter into a formal contract and	furnish a surety guaranteeing the full and					
9.	The Surety executing the bond must app act within the limitations listed therein.			vided in the Instructions to Bidders, Plans and Specifications and other said Obligee, then this obligation shall become void; otherwise it shall remain					
10	. The names and titles of the people signing	In the event the Obligge determin	es the Principal has failed to comply with any						
11	Corporations executing the bond shall at "seal not required" in the space where the	paragraph, then the Principal shal	pay to the Obligee the difference, not to exce he Principal's bid and such larger amount for y	eed the full penal sum set forth above,					
12	. A person authorized to bind the Bidder/F	another party to perform the work expense of recovery.	covered by said bid, together with all court co	osts, all attorney's fees and any other					
13	. The Bond must be signed by an atton identifies the surety company's signatory		e said Principal and said Surety have caused th	his instrument to be signed by their					
14	 The date on which the Surety's Power o the bond was signed by the Surety. 	respective officers and their corpo	rate seals to be hereunto affixed thisd	lay ofA.D. 20					
15	. In its application to negotiated contracts,			(Principal) (Seal)					
		Witness:		ausiness Address)					
		Or Secretary's Atte	t By(Signature)	(Title)					
				(Surety) (Seal)					
		Witness:		iusiness Address)					
		Or Secretary's Atte	By	(Title)					

PROCUREMENT – PAYMENT & PERFORMANCE BOND

See P&P bond forms in Exhibit C of the Subcontract Agreement in Part Two B and also Owner Agreement Exhibit D, see Master Agreement Schedule 6.

Include as an attachment on Building Connected.

*At COT3 option, you may be enrolled into the Subcontractor Default Insurance (SDI) program DPS Version 04/25/2017 ***RIDER ATTACHED CONTRACTORS PERFORMANCE & PAYMENT BOND** See P&P bond forms in Exhibit C of the Subcontract Agreement in Part Two B.

PROCUREMENT – BID SUBMISSION CHECKLIST


BOOK 1 is not required to be submitted with the bid in its entirety

All required forms must be included with the bid. Upload as an attachment with your submission on Building Connected.

Check all forms for signature, initials, notarizations, etc. requirements.

Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).



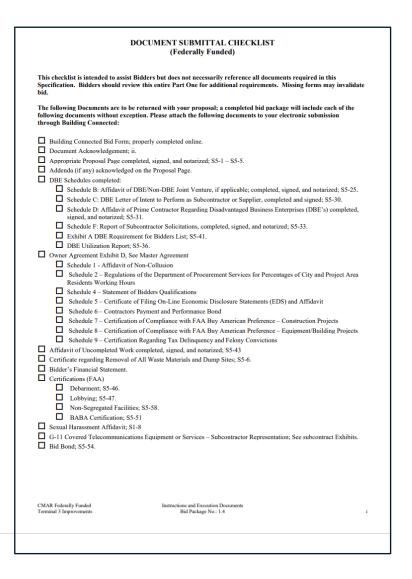

PROCUREMENT – BID DOCUMENTS

BID DOCUMENTS Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Contains various requirements impacting the work and its administration

Supplemental Documents

PROCUREMENT – BID DOCUMENTS

BID DOCUMENTS Part One of Three – Instructions and Execution Documents


Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings


Supplemental Documents

PROCUREMENT – SUBCONTRACT EXHIBITS A, B & C

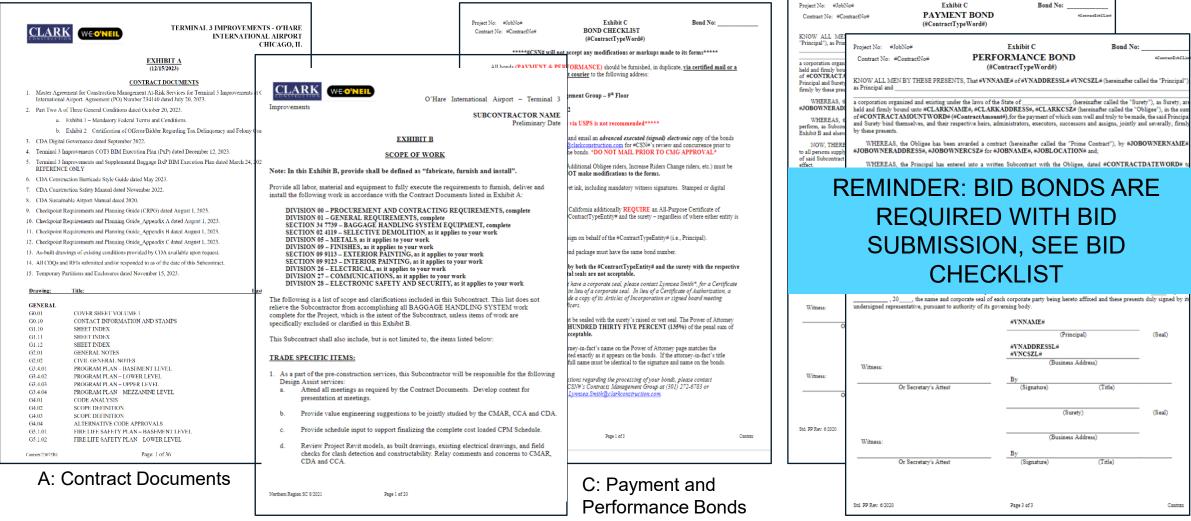

B: Scope of Work

PROCUREMENT – SUBCONTRACT EXHIBITS D, D-1, D-3, D-4

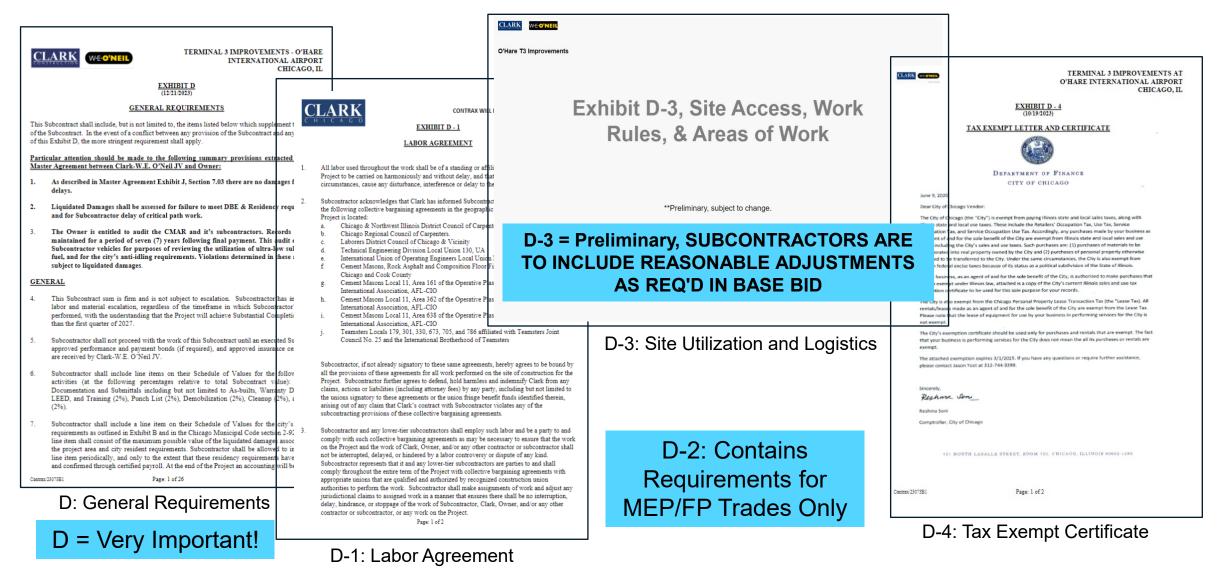

PROCUREMENT – SUBCONTRACT EXHIBIT E

Insurance Requirements

CLARK WECHIN	TERMINAL 3 IMPROVEMENTS AT O'HARE INTERNATIONAL AIRPORT CHICAGO, IL
	EXHIBIT E (10/20/2023)
INSUR	ANCE REQUIREMENTS
Clark Project No.: 23073B1	
OWNER CONTROLLED INSURANCE PROG	RAM
OVERVIEW:	
(OCIP). The OCIP is more fully described in t that is incorporated in this Exhibit E by this refer to read the OCIP Manual and the OCIP Insuranc to Enrolled Parties (as defined below) worke liability insurance, and excess liability insuran	ain insurance coverages under an Owner Controlled Insurance Program he Sponsor's OCIP Insurance Manual (hereinafter "Insurance Manual") ence and made a part hereof. All Enrolled Parties are strongly encouraged e Policies in detail prior to enrolling in the OCIP. The OCIP will provide rs' compensation, employer's liability insurance, commercial general ce ("OCIP Coverage's"), as summarily described below, in connection in the event that there are any discrepancies between this Exhibit and the
2) ENROLLED PARTIES AND THEIR INSU	RANCE OBLIGATIONS:
subcontractors at any tier, who enroll in the OC may designate (each such party who is insured) performing labor or services at the Project site a unless designated by Sponsor as an Excluded P.	nrolled Parties are: Sponsor, eligible Subcontractors and all of their IP, and such other persons or entities as Sponsor in its sole discretion under OCIP is collectively referred to as an "Enrolled Party"). Parties is defined in the Insurance Manual, are eligible to enroll in the OCIP arty (as defined below). Enrolled Parties (Subcontractors) shall obtain, at any tier to obtain and maintain, the insurance coverages specified
3) EXCLUDED PARTIES AND THEIR INSU	RANCE REQUIREMENTS:
 b) Architects, surveyors, engineers, soil testin c) Vendors, suppliers, fabricators, material de up, deliver, or carry materials, personnel, p site; d) Any entity who does not perform any actua 	and/or transport companies and their consultants; g engineers, and their consultants; alers, truckers, haulers, drivers and others who merely transport, pick arts or equipment or any other items or persons to or from the Project
4) OCIP COVERAGES:	
complete, or to alter or amend any provision of	ges in this Exhibit E or the Insurance Manual are not intended to be the actual OCIP Coverages. In the event any provision of this Exhibit its, or the summary below conflicts with the OCIP insurance policies, icies shall govern.

OCIP Coverages shall apply only to those operations of each Enrolled Party performed at the Project site in connection with the subcontract work and only to Enrolled Parties that are eligible for the OCIP, even if erroneously enrolled in the OCIP. The OCIP shall provide only the following insurance to eligible and Enrolled Parties:

Contrax/23073B1

Page: 1 of 7

PROCUREMENT – SUBCONTRACT EXHIBITS G2, G3, G4, G8, G11

					#JobName# #VNNAME#	
				#Contrac	tTypeWord# Dated: #ContractDateWord#	
	#JobName: #VNNAME:		#JobName#	EXHIBIT G - 8 PREVAILING WAGE AND LABOR STANDAR	DS ACKNOWLEDGEMENT	
#ContractType	Word# Dated: #ContractDateWord	÷	#VNNAME# #ContractTypeWord# Dated: #ContractDateWord#	By the signature below, it is hereby expressly agreed and acknowledge	1	
EXHIBIT G - 2		-	EXHIBIT G - 4	agreement to perform work on the <u>#JobName#</u> , which is subject to Requirements for labor standards and covered by Prevailing Wage requ	4	#JobName# #VNNAME#
DEBARMENT CERTIFICAT	<u>ON</u>	EXHIBIT G - 3		Subcontractor expressly agrees and acknowledges that Subcontract Subcontractor's price for the performance of work on the above reference	c #Con	atractTypeWord#Dated: #ContractDateWord#
#ContractTypeEntity#, hereby certifies that at the time of the aw #ContractTypeEntity#, or its Principals, is not debarred, suspended or Government.	ard of this #ContracTj CERTIFI proposed for debarment	CATION REGARDING INFLUENCING OR ATTEMPTIN FEDERAL CONTRACTING AND FINANCIAL T	G STATEMENT AND ACKNOWLEDGMENT CAN Development of the second seco	of the requirements established therein: • Subcontractor has received as part of Subcontractor's #Contra	EXHIBIT G	
THIS CERTIFICATION CONCERNS A MATTER WITHIN TH	JURISDICTION OF	igned certifies, to the best of his or her knowledge and belief, th	PART L- STATEMENT OF PRIME CONTRACTOR	by reference, the Davis-Bacon and Construction Wage Kate Key C.F.R. §§ 5.5(a)(1) through 5.5(a)(10).	REPRESENTA	
OF THE UNITED STATES AND THE MAKING OF A FALSE CERTIFICATION MAY RENDER THE MAKER SUBJECT TO 1001, TITLE 18, UNITED STATES CODE.	PROSECUTION UNDI (1) No person for	Federal appropriated funds have been paid or will be paid, by o influencing or attempting to influence an officer or employee of	In 4. FYEME CONTRACTOR 5. EUROCONTRACTOR	 Subcontractor has received as part of Subcontractor's #Contrat by reference, the Contract Work Hours and Safety Standards A 29 C.F. §§ 5.5(b)(1) through 5.5(b)(4). Subcontractor has received as part of Subcontractor's #Contractor's #Contracto	Pursuant to 48 CFR § 52.204-25, the undersigned provid applicable, disclosure(s):	les the following representation(s) and, if
Company Name: <u>#VNName#</u>	any Federa cooperativ	employee of Congress, or an employee of a Member of Congre Il contract; the making of any Federal grant; the making of any e agreement; or the extension, continuation, renewal, amend	CI & STREET ADDRESS, ADV. STREET ADDRESS	by reference, the labor standards clauses and the applicable we that the Wage Determination applicable to the Project reference General Decision Number: <u>IL2023009</u> Dated: 07/14/20 Except for potential jurisdictional disputes. Subcontractor will	 Definitions: As used in this provision, the terms arrangements," "Covered telecommunications eq and "substantial or essential component" have th 	uipment or services", "critical technology",
#ES-Signature1# #ES-Title1# Authorized Signature Title	#ES-Sig Date (2) If	rant, loan, or cooperative agreement. any funds other than Federal appropriated funds have been p	6. The prime contract does, does not contain the clause entitied "Contract Work Hours and Saltery Standards Act Overtime Compensation"	prevailing area practice for Subcontractor's work, and the ap contract price. • Without limiting any other obligations, Subcontractor agrees to	Prohibition on Contracting for Certain Telecomn Equipment	
	employee loan or coo	g or attempting to influence an officer or employee of any agency of Congress, or an employee of a Member of Congress in come perative agreement, the undersigned shall complete and submit S _obbving", in accordance with its instructions (as amended by	7 The prime contractor states that under the contract shown in Nem 1, a subcontract was awarded on the date shown in Nem 2 to the subcontract or same states and the shown in Nem 2 to the subcontract or same states and	 a) Comply with all applicable laws, including but not lim Construction Wage Rate Requirements, and the Wage Dee b) Flow down to all of Subcontractor's lower-tier subcontracto Requirements as well as provisions and Federal Acquising 	2019 (Pub. L. 115-232) prohibits the Government	t, on or after August 13, 2019, from procuring
**************************************	to Report	coopying, in accordance with its instructions (as amended by	D0 As provided within this =ContractTypeWord= = =ContractNo= dated =ContractDateWord= attached hereto.	Subcontractor's #ContractTyneWord#	or obtaining, or extending or renewing a contract	to procure or obtain, any equipment, system,

REMINDER: SOME FORMS ARE REQUIRED WITH CONTRACT AWARD, SOME WITH BID SUBMISSION, SEE

BID	CHECKLIS	Т

For the period perio	ations	Telecommunication Equipment or Servi	gement	Acknowled Form	orm	edgment F	_	ving Activities	re of Lobby	isclosu	G3: Di			
probabile expension or fails to file or anneal a required certification or define in the file or anneal a required certification	Page 1 o			0				Contrax	Page 1 of 1			ent Certification	Debarr	G2: C
prohibited expenditure or fails to file or amend a required certification or fails to file or amend a required certification or fails to file or amend a required certification or fails to file or amend a required certification or fails to file or amend a required certification or fails to file or amend a required certification or and solution or a	nanufacturer part number, or	offered provided to the Prime Contractor (include brand; model num original equipment manufacturer (OEM) number; manufacturer part wholesaler number; and item description, as applicable);	U I		Contrax		Page 1 of 2	SF1413 Rev. 8/2023 ES				Page 1 of 1	114	DEBARMENT Rev. 2/201
prohibited expenditure or fails to file or amend a required certification or departed to refine comma term blek (6) Appendice and Training prompty provide standard or refine comma term blek (6) Subcontract (1400 H)			Page 1 of 1	& Labor Acknowledgement 2/2021 ES	222(e)	STANDARD FORM 1413 (REV Prescribed by GSA/FAR (48 CFR								
prohibited expenditure or fails to file or amend a required certification or data civil penditure or fails to file or amend a required certification or data civil pendity for of less than \$10,000 and not more than \$10,000 for each such civil pendity of not less than \$10,000 and not more than \$10,000 for each such civil pendity of not less than \$10,000 and not more than \$10,000 for each such disclosure. In addition, the undersigned understands and agrees that the provide apply to this certification and disclosure, if any.	in two (2) business days. By signi it will only provide cover	equipment or services" to the Prime Contractor, the Subcontractor shall pr information to the Prime Contractor on the next page within two (2) busin this Representation, the Subcontractor represents it will only		orized Signature	_	17. DATE SIGN	10. BY (Signature)	10. NAME OF PERSON SIGNING #ES-Namel#	#FS_Title1#					
Image: contract of a list of file or amend a required certification or data civil penalty of not less than \$10,000 and not more than \$100,000 and not more than \$100 and \$		 Subcontractor Disclosures. If the Subcontractor cannot make the represe (3), and/or if the Subcontractor "will" or currently "does" provide "covered 	- 4		#ES-	₽.	o #STX	A #\$TX3#	re, if any.	dition, the undersigne tification and disclosu	apply to this certi			
	nce of this Subcontract. The at of excluded parties in the System rentities excluded from receiving at or services," and none of	er services, and it will not provide any equipment, system, or service that uses or telecommunications equipment or services in the performance of this Subocc Subcontractor further represents that it has reviewed the list of excluded parts for Award Management (SAM) (https://www.sam.gov) for entities exclude federal awards for "covered telecommunications equipment or services," an Subcontractor's lower-ter subcontractors or suppliers under this Subcontractor is Subcontractor's lower-ters uncontractor so uppliers under this Subcontractor	uired information related ther grams prior to apprentices ex- nentation upon request. and acknowledged that Subco- comply with all of the above r- ier subcontractors working for : ontractor will be responsible to	reasonably requested or requ approved apprenticeship prog promptly provide such docum ly, it is hereby expressly agreed an ontractor's lower-tier subcontractors c bove listed information to all lower-tie ons of the work on this Project. Subco	Subc the a porti	em 1 are included in this subcontract: struction Wage Rate Requirements rentices and Trainees npliance with Copeland Act Requirement contracts (Labor Standards) tract Termination - Debarment	offowing clauses of the contract shown in rds Act - Overtime Compensation C At 6) Act - Overtime Compensation C Si C	CICL 13. The subscritterator acknowledges that the fo D/µ Contrast Work Hours and Safety Standar (If included in prime contract see Bioc Payrolls and Basic Records Utypels and Casic Records Utypelse Concerning Labor Standards Compliance with Construction Wage Rate and Related Regulations.	Pursuant to 31 U.S.C. § 1352(c)(1)- or amend a required certification or d and not more than \$100,000 for each the truthfulness and accuracy of each	S.C. § 1601, et seq.)). I aditure or fails to file o not less than \$10,000 a l certifies and affirms	codified at 2 U.S. prohibited expend civil penalty of n The undersigned			

IMAGE IS FOR REFERENCE ONLY – USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

PROCUREMENT – SUBCONTRACT EXHIBIT J & J-1

J: Owner Required Flowdowns

J-1: Self Certification Form

	WE-O'NEIL
--	-----------

TERMINAL 3 IMPROVEMENTS - O'HARE INTERNATIONAL AIRPORT CHICAGO, IL

Addre

UEI #

EXHIBIT J (08/31/2023)

OWNER REQUIRED FLOWDOWNS

Preliminary Exhibit J - Subject to Change Upon Execution of the Fina

[Subcontractor/Supplier/Consultant/Designer/Provider/Lessor] (hereinal "Subcontractor") shall comply with all terms, conditions, and provisions that are or set forth in full text in, or otherwise comprise a part of or are applicable to the Construction Management At-Risk Services for Terminal 3 Improvements at (hereinafter referred to collectively as the "Prime Contract"). All such terms, con hereby incorporated by reference and shall have the same force and effect as if th forth in full text in this [Subcontract/Order/Agreement/Lease Order] (hereina "Subcontract"). In the event of a conflict between the terms and conditions inclu any other terms and conditions included in the Subcontract, this Exhibit J shall g City, S

Subcontractor hereby agrees to include all clauses included herein in all of its Subcontractor enters into a lower tier subcontract at any time during the perform copy of those lower tier subcontracts must also be provided to Clark/O'Neil. Thi to any and all lower tier subcontractors related to the performance of this Subcor

Exhibit D - Required Subcontract Provisions

II. Standard of Performance, Construction Manager will require that its Trade (minimum, meet the standard of performance set forth herein.

In addition to performing the Work in full compliance with the Contract Documents, perform, or cause to be performed, all Work required of it under the terms and condit that degree of skill, care, and diligence normally exercised by qualified and experien performing work in projects of a scope and magnitude comparable to the Project. Un materials and equipment will be new, and of such quality as required to comply with The Trade Contractor will, when required, furnish satisfactory evidence as to kind an and equipment. All labor will be performed by workers skilled in their respective rabe of good quality so that first class work in accordance with the standards of constru-Contract Documents will result.

III. Permits, Licenses and Regulations. Subcontracts must contain the following permits, licenses and regulations.

A. Permits

Contrax/23073B1

1. The Trade Contractor will not be responsible for the building permit cost. How specific permits, applicable licenses and associated fees will be the responsibility of

2. The nature of the foundation systems required on portions of this Project may 1 permits, and coordination will be required with the City of Chicago Bureau of Under required by the Contract, the Trade Contractor, representing its familiarity with these processes, is responsible for any and all submittals, fees, coordination, and any other approvals required by the authorities having jurisdiction for the installation of these

Page: 1 of 66

EXHIBIT J - 1 SELF CERTIFICATION FORM

#ContractTypeWord# Dated: #ContractDateWord#

any Name:	#VNNAME#
55:	#VNADDRESSL#
State, Zip:	#VNCSZL#
	#\$T0#

Business Concern Self Certification [SELECT AT LEAST ONE (1) BOX THAT APPLIES TO YOUR ORGANIZATION]:):

- #\$0# Large Business (LB)
- #\$1# Small Business Enterprise (SBE)
- #\$12# Certified Disadvantaged Business Enterprise (DBE)
- #\$13# Minority Business Enterprise (MBE)
- #\$14# Woman Business Enterprise (WBE)
- #\$11# Other: #\$TX2#

II. Commercially Useful Function:

Attention is directed to Exhibit B of your #ContractTypeWord#, in which you agree that each Disadvantaged Business Enterprise ("DBE"), if any, with which you subcontract for work within the scope of your #ContractTypeWord# will perform a <u>Commercially Useful Function</u> as defined in Department of Transportation Regulations, 49 C.F.R. § 26.55. See pages 3-5 of this Exhibit J-1 for information concerning regulatory and #ClarkName# (hereinafter "#CSN#") requirements regarding "Commercially Useful Function." #ContractTypeEntity# further agrees to assure that each DBE lower tier subcontractors, if applicable, possesses a sufficient DBE certification for all within the scope of such lower tier subcontract.

III. In Section I above, Business Concern Self Certification:

Select here #\$RD0E# and skip the rest of Section III if you are <u>NOT</u> a Certified Disadvantaged Business Enterprise (DBE).

If you checked the box for "Certified Disadvantaged Business Enterprise (DBE)", complete the below items that apply to your organization:

The Illinois Unified Certification Program (ILUCP): (check the subset that applies to this Project)

#\$18# CERTIFIED U/DBE b	y the Illinois Department of Transport	ation (IDOT)-
Certification #: #\$TX	10#	
Date of Certification:	#\$TX11#	
* Attach a copy of the	Certification	


(this space left intentionally blank)

Page 1 of 6

IL DRE CERTIFICATION 10/2017 ES

#JobName# #VNNAME#

PROCUREMENT – SUBCONTRACT EXHIBIT R

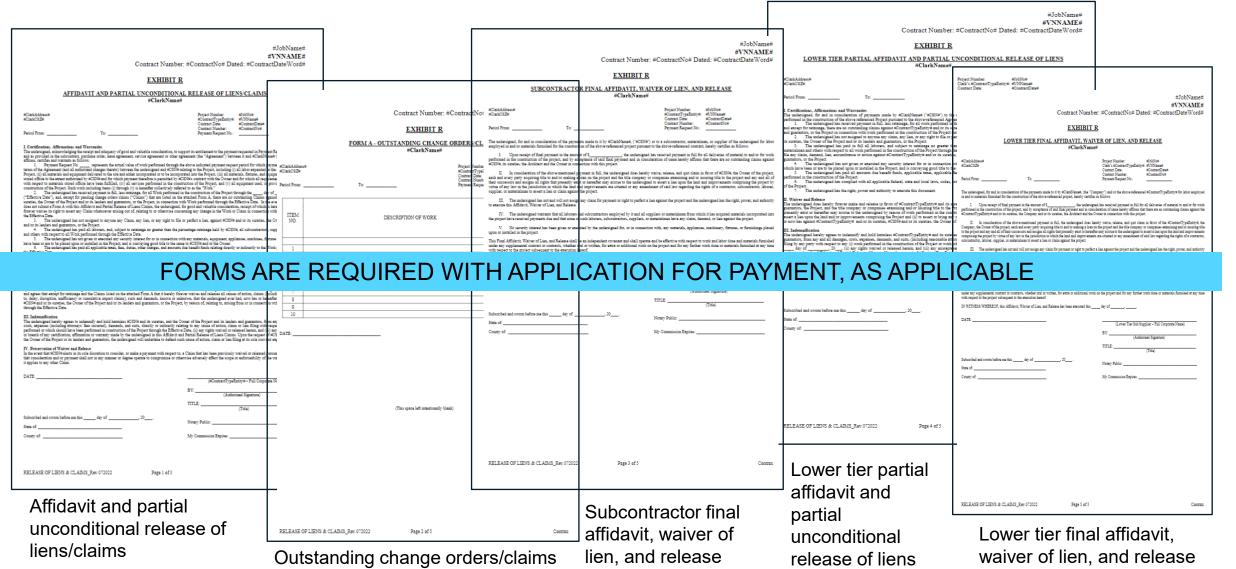

PROCUREMENT – SUBCONTRACT EXHIBIT V

V: Building Information Modeling

Applies only to trades with a BIM requirement

CON	O'Hare International Airpor Terminal 3 Improvement
	EXHIBIT V (12/12/2023)
Defin	itions: (Definitions included below are specific for this Exhibit)
1.	"2D" means two dimensional.
2.	"3D" means three dimensional.
3.	"BIM Detailer" means person(s) responsible for the detailing of each Subcontractor's BI content.
4.	"Construction Team" means Clark-W.E. O'Neil JV and all of its subcontractors and supplier
4.	of any tier.
5.	"Contract Drawing" means a two-dimensional document derived from the three-dimension
	model produced by a designer.
6.	"Coordinated Model" means a Federated Building Information Model (BIM) which has bee
	coordinated with the Construction Team and Design Team to eliminate virtual clashes an
	installation constraints and is sufficient to create Contract Drawings/Shop Drawings for
	installation of the Work.
7.	"Coordination Model Schedule" means the schedule that dictates the time by which differe
	areas, trades, and/or floors are to be coordinated, signed off, and submitted necessary to achiev
	the ultimate project schedule with input from the Construction Team and approved b
	Clark-W.E. O'Neil JV.
8. 9.	"Data Hosting Site" means the web site(s) used to transfer, store, and share electronic data. "Deliverables" means 2D drawings in PDF and DWG format, 3D models in native authoring
9.	format, models in NWC/NWD format (to be coordinated in Revisto), Shop Drawings, of
	submittals.
10.	"Design Team" means the Architect and all of its consultants at any tier.
11.	"Electronic Information" means 2D and 3D digital data.
12.	"Lead Coordinator" means the responsible party for creating a Coordinated Model for the
	coordination scope, performing clash detection, analyzing clashes and coordinating solution
	grouping and logging clashes, importing and assigning clashes in the tracking syste
	designated by Clark-W.E. O'Neil JV. The Lead Coordinator will prioritize clashes according
	priority system and assign issues to the responsible party during coordination meetings using
	the designated issue tracker. Clark-W.E. O'Neil JV will be the final authority on model issues.
13.	"Model" means a digital representation of the physical and functional characteristics of the
	project and is referred to in this Exhibit as the "Model(s)", which may be used to describe
• 4	Model Element, a single Model, or multiple Models used in aggregate.
14.	"Model Element" means a portion of a Model representing a component, system, or assemb within a building or building site
15.	within a building or building site. "Shop Drawing" means a two-dimensional document derived from the three-dimension
15.	"Stop Drawing" means a two-dimensional document derived from the three-dimension model produced by a Subcontractor.
	Page: 1 of 15

PROCUREMENT – SUBCONTRACT EXHIBIT W, W-1

W: Certification of Compliance with Wage Laws

W-1: Authorized Individual for Signing Certification of Compliance with Wage Laws

#C	#JooName# #VNNAME# Joed# Dated: #Contro tDateWord#	
#Contract1ypew	/ord# Dated: #ContractDateWord# Contract No.: #ContractNo#	
EXHIBIT W		#JobName#
Certification of Compliance with Wage The undersigned certifies and affirms that #VNNAME# and all of its tie been, at all times through the date written below, and will remain, in com wage laws applicable to #VNNAME# work on the Project with respect to payment of wages, (3) payment of overtime, (4) federal, state, and local wit payroll and other taxes as applicable, worker's compensation contribution required by law. #VNNAME# shall defend, indemnify, and hold harmless #CSN#, the O respective directors, officers, members, managers, employees, sureties, an	rei lii (I) hh if Authorized Individual Only required (I) our behalf shall have the same effect a set Authorized Individual(s): Name (Printed): #\$T5# Name (Printed): #\$TX3# This authorization is valid until further Sincerely, #VNNAME# (Subcontractor) By: #ES-Signature1# (Authorized Representative's signature	#UNAME# #ContractTypeWord# Dated: #ContractDateWord# Contract No.: #ContractNo# Mainter Contract No.: #ContractNo# In the Initial submission of Compliance with Wage Laws with initial submission or when updates are made to individual(s) listed below to sign on our behalf in all manners relating to ance with Wage Laws. Any and all acts carried out by the individual(s) on s acts of our own.
Cattification of Compliance with Wige Lenv 09 2022 Page 1 of 1	Print name: #ES-Name1# Title: #ES-Title1#	
	Certification of Compliance with Wage Laws 03/2023	Page 1 of 1 Constant

PROCUREMENT – SUBCONTRACT ATTACHMENT, PRELIMARY PROJECT SCHEDULE- DRAFT



O'HARE INTERNATIONAL AIRPORT – TERMINAL 3 IMPROVEMENTS CHICAGO, IL

ATTACHMENT (12/22/2023)

PRELIMINARY PROJECT SCHEDULE - DRAFT

This attachment contains a preliminary project schedule titled "O'Hare T3I Preliminary Schedule DD 12.21.23" (77 pages).

Subcontractor acknowledges that the preliminary project construction schedule may require further development, including, but not limited to logic revisions, resequencing, resource-stacking, etc., as the work progresses; and has included all provisions necessary to maintain the Project Schedule.

The dates in the following schedule are Early Start and Finish Dates.

Contrax/23073B1

Page: 1 of 77

Date Printed: 22-Dec	c-23 10:35	Layou	t: T3I - (1)	Detailed Sch	edule				Data Date: 21-Dec-
tivity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Total Float			2025 2028 2027 JFMAMJJASONDJFMAMJJASONDJFMAMJ
T3 Improvemen	nts - Preliminary Schedule - Data Date: 12/21/2023	946	841	21-Dec-23	13-Apr-27	0			
MILESTONES		946	753	3 21-Dec-23	13-Apr-27	0			
PROJECT MILEST	TONES	1360	1082	2 21-Dec-23	13-Apr-27	0			
MILE-130	PRE-CON NTP (7/24/2023)	0		21-Dec-23			E-CO	N NTP (7/24/2023)	
MILE-010	CONSTRUCTION NTP (ANTICIPATED 4/26/2024)	0	0)	26-Apr-24	2		♦ CONSTRUCTIO	N NTP (ANTICIPATED 4/26/2024)
MILE-110	SUBSTANTIAL COMPLETION	0	()	10-Feb-27	0	1		♦ SUBST/
MILE-120	FINAL COMPLETION	0	()	13-Apr-27	0			♦ FÍN
LD MILESTONES		492	492	2 04-Mar-25	10-Feb-27	0			
LD-1000	LD - AA CLUB SHELL READY FOR TENANT FIT OUT BY OTHERS	0	()	04-Mar-25	492			LD - AA CLUB SHELL READY FOR TENANT FIT OUT BY OT
LD-1010	LD - GATE K1 INCLUDING PARTIAL HOLD-ROOM FIT OUT	0	()	22-Aug-25	371			LD - GATE K1 INCLUDING PARTIAL HOLD-ROOM
LD-1020	LD - GATE L2A INCLUDDING PARTIAL HOLD ROOM FIT OUT	0	()	22-Aug-25	371	1		LD - GATE L2A INCLUDDING PARTIAL HOLD F
LD-1030	LD - CONCESSION SHELL READY FOR TENANT FIT OUT	0	()	17-Sep-25	354			LD CONCESSION SHELL READY FOR TEN
LD-1040	LD - SUBSTANTIAL COMPLETION	0	()	10-Feb-27	0			♦ LD - SU
INTERIM MILESTO	ONES	1150	1022	2 21-Dec-23	10-Feb-27	62			
MILE-150	DESIGN COMPLETE	0	()	21-Dec-23			DESIGN COMPLETE	
MILE-140	PERMITTING COMPLETE	0	()	24-Apr-24	1084		PERMITTING CO	DMPLETE
MILE-160	PURCHASING COMPLETE	0	()	24-May-24	1054		PURCHASING	COMPLETE
MILE-170	LONG LEAD MATERIAL PROCUREMENT COMPLETE	0	()	02-Jun-25	680			LONG LEAD MATERIAL PROCUREMENT COMPLET
MILE-230	CONSTRUCTION - MECHANICAL COMPLETE	0	()	13-Nov-25	516			 CONSTRUCTION - MECHANICAL COMP
MILE-180	CONSTRUCTION - CORE & SHELL COMPLETE	0	()	07-May-26	341			 CONSTRUCTION - CORE &
MILE-190	CONSTRUCTION - STRUCTURAL/ENCLOSURE INFILL/OPENING COMPLETE	0	()	19-Oct-26	176			CONSTRUCTIO
MILE-210	CONSTRUCTION - RESTROOM ALTERATIONS COMPLETE	0	()	01-Feb-27	71			 CONST
MILE-220	CONSTRUCTION - BAGGAGE HANDLING SYSTEM COMPLETE	0	0)	03-Feb-27	69			 CONST
MILE-200	CONSTRUCTION - INTERIOR ALTERATIONS COMPLETE	0	()	10-Feb-27	62			 CONST
AAMILESTONES		451	451	29-Apr-24	06-Feb-26	300			
AA FLAG SHP CH	HECK-IN	189	189	0 13-May-24	10-Feb-25	552			••••
AA-1000	AA FLAGSHIP CHECK-IN SUMMARY (CALENDAR DAYS)	267	267	7 13-May-24	03-Feb-25	730			AA FLAGSHIP CHECK-IN SUMMARY (CALENDAR DAYS)
AA-1030	AA FLAGSHIP CHECK-IN START	0	(13-May-24		683		♦ AA FLAGSHIP (CHECK-IN \$TART
AA-1040	AA FLAGSHIP CHECK-IN COMPLETE	0	0)	03-Feb-25	469			AA FLAGSHIP CHECK-IN COMPLETE
CDA-1000	UL - AA FLAGSHIP - FF&E MOVE IN PERIOD	5	5	6 04-Feb-25	10-Feb-25	469			UL - AA FLAGSHIP - FF&E MOVE IN PERIOD
AAPPS		120	120) 29-Apr-24	16-Oct-24	631			
AA-1010	AA PPS SUMMARY (CALENDAR DAYS)	171	171	1 29-Apr-24	16-Oct-24	7		AAI	PPS SUMMARY (CALENDAR DAYS)
AA-1050	AAPPS START	0	(29-Apr-24		693		AAPPS START	
AA-1060	AAPPS COMPLETE	0	()	16-Oct-24	573		♦ AAI	PPSCOMPLETE
AACLUB TI		236	236	6 05-Mar-25	06-Feb-26	0			
CDA-1010	UL - AA CLUB TI START	0	(05-Mar-25		69			• UL-AACLUBTISTART
AA-1020	UL - AA CLUB TI SUMMARY (CALENDAR DAYS)	339	339	05-Mar-25	06-Feb-26	0			UL - AA CLUB TI SUMMARY (CALE
CDA-1050	UL- AA CLUB TI COMPLETE	0	()	06-Feb-26	0			UL - AA CLUB TI COMPLETE
GATE CLOSURE	ESIOPENINGS	320	320) 21-May-24	25-Aug-25	415			
GATE K1 CLOSU	JRE/OPENING	320	320	21-May-24	22-Aug-25	415			
GATE-K1-1000	GATE K1 CLOSURE WINDOW (CALENDAR DAYS)	459	459	21-May-24	22-Aug-25	537			GATE K1 CLOSURE WINDOW (CALENDAR D
CDA-1100	UL- GATE K1 CLOSURE START	0	(21-May-24		677		UL- GATEK1	CLOSURE START

T3I-231221-ForMarket | T3 Improvements - Preliminary Schedule - Data Date: 12/21/2023 Terminal 3 Improvements at O'Hare International Airport City of Chicago: Chicago Department of Aviation



Page 1 of 76



PROCUREMENT – BID DOCUMENTS

BID DOCUMENTS Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT – BID DOCUMENTS, Part Three of Three

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Available on BuildingConnected:

← C ŵ https://app.buildingconnected.com/projects/652048e2cf223100f951a4c7/files A ☆ ☆ ↓										
	DDESK Construction Cloud BuildingConnected ▼ Q Search for p	eople or companies		3 (2)	SP •					
	Projects / O'Hare Terminal 3 Improvements O'Hare Terminal 3 Imp	provements			~					
:=		formation Bid Forms Team Reports								
41	 All Bidders Construction Documents (Vpload files	Size	Link with Autodesi	k Docs					
2	Supplemental Documents	Construction Documents (Part 3)	1.09 GB	12/21/2023 at 3:06 PM CST	:					
- =		Supplemental Documents	122.8 MB	12/22/2023 at 2:32 PM CST	:					
C										
ıtıl										

PROCUREMENT – BID DOCUMENTS

BID DOCUMENTS Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT – BID DOCUMENTS, Supplemental Documents


Available on BuildingConnected:

- CDA Construction Barricade Style Guide_May 2023
- CDA Construction Safety Manual FINAL
 110922
- CDA Digital Governance_Sept 2022
- CDA Smartsheet Standard Operating
 Procedure
- CDA Sustainable Airport Manual_v4.0
- CDA-RFI Response Log_2023.12.22
- COT3 Temporary Partitions and Enclosures
 Plan Rev1 202312120
- Exhibit 1- Mandatory Federal Terms and Conditions 20231020
- Exhibit 2 Tax Delinquency and Felony Convictions 20231020
- Master Agreement Exhibit E Bond Forms
- O'Hare T3I Preliminary Schedule DD 12.21.23 2
- ORD T3_Geotechnical Report
- Terminal 3 Public Owner Contract
- Terminal 3 Improvements and Supplemental Baggage BIM Execution Plan_3-24-23
- TSA checkpoint-requirements-and-planningguide appendix-a
- TSA checkpoint-requirements-and-planningguide_appendix-b
- TSA checkpoint-requirements-and-planningguide_appendix-c

\leftarrow		om/proje	cts/652048e2cf223100f951a4c7/files	A" 🗘	\$ □ ۮ @ %	
	DESK Construction Cloud BuildingConnected	eople or	companies		3 (3) SP	•
0	Projects / O'Hare Terminal 3 Improvements O'Hare Terminal 3 Imp	orov	ements		\checkmark	
:=	Bid Packages Messages Files In	formatio	on Bid Forms Team Reports			
Ê	✓ ☐ All Bidders	(↑.) Upload files		Link with Autodesk Docs	
	> Construction Documents (Name	Size	Last updated 🔹	
Ë	Supplemental Documents		Construction Documents (Part 3)	1.09 GB	12/21/2023 at 3:06 PM CST	
ন্দ্র						
Ē			Supplemental Documents	122.8 MB	12/22/2023 at 2:32 PM CST	
C						
ш						
_						


To begin, find the project in your Bid Board.

• From the "Accepted" tab on your Bid Board, click "Send or Log" on the right-hand side of the bid.

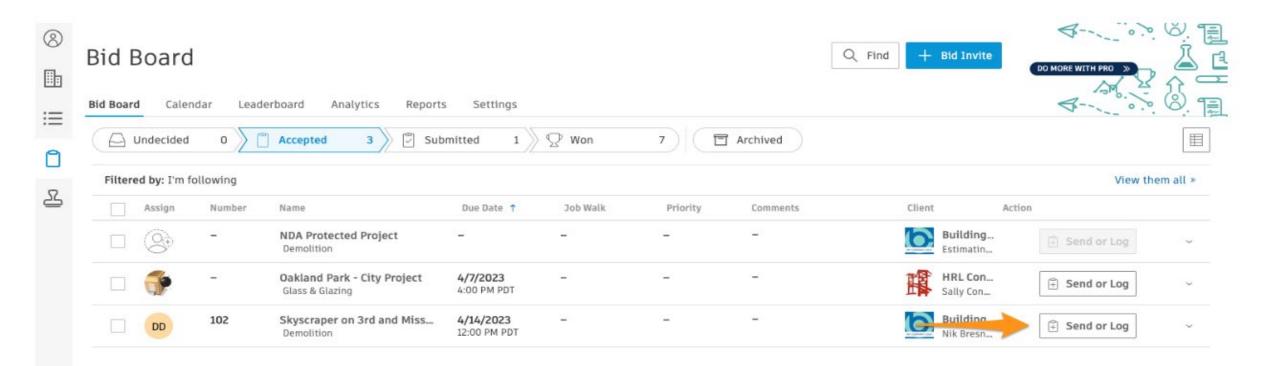

If you are already inside the project, click on the "Bid Form" tab or click "Bid Form" next to "Opportunity Summary"

Note: "Bid Form" appears next to the Opportunity Summary after you have indicated you are bidding. Select "Bidding" first see the "Bid Form" button.

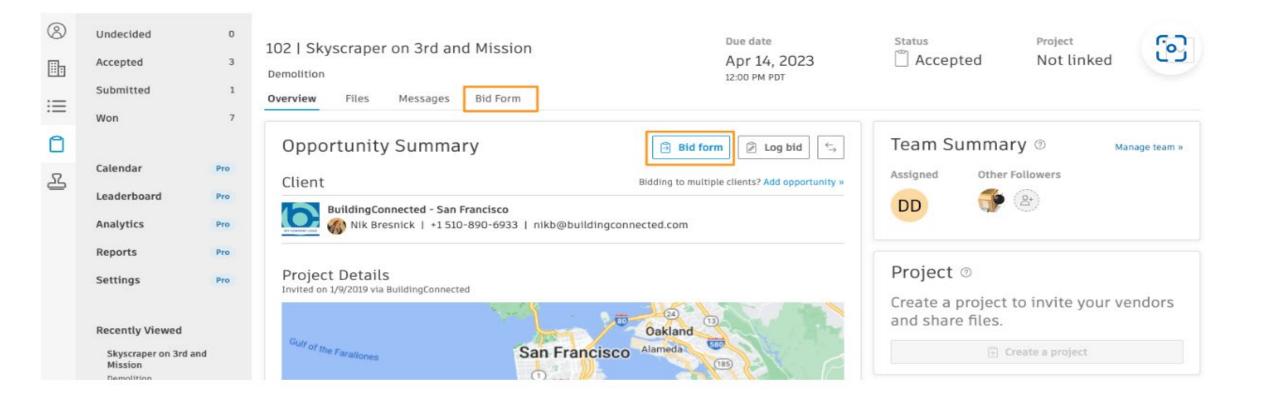

Enter all of the information requested in the form.

To attach the required documents, click "Attach your proposal" and select files from your computer. The files will immediately start uploading until they reach 100%. Upload more by clicking "Attach more".

Click "Print" to download or print a PDF copy of the bid form. The proposal will open in a new tab where there are options to download and print.


Once the bid form is complete, click "Preview & send".

⊗ ⊡	Undecided Accepted Submitted	0 3 1	102 Skyscraper o Demolition Overview Files	n 3rd and Mission	Due date Apr 14, 2023 12:00 РМ РФТ	Status	Project Not linked	~
0	Won	7	[Draft] Send prop	osal: \$250,000 Saved		Already submitted your bid outside of BuildingConnected?		
L	Calendar	Pro	Line Items			Log your bid instead »		
-	Leaderboard	Pro	Description	Quantity Unit Cost	Total Cost			
	Analytics	Pro	Your base bid value is the	sum of these line items.				
	Reports	Pro	*Demolition		\$ 250,000.00			
	Settings	Pro	Base Bid		\$250,000			
	Recently Viewed		Additional Info	rmation				
	Skyscraper on 3rd and Mission Demolition		Message	Add a message				
	[NDA-Protected Invite Demolition]						
	Katz & Robert Test Concrete			B / <u>U</u> ≟≡ !≡				
	Oakland Park - City Project Glass & Glazing		Attachments	😵 📙 Sam's Demo - Skyscra	per Proposal (221 KB)			
	Energize Coffee Shop Renovation Demolition			⊕ Attac	ch more			
				[🕒 Print 🛛 Preview & send 🧹			

Please note that if you do not fill in all of the required questions, you will see any required items highlighted with a red flag. Fill them in accordingly and click "Preview & send" again.

Line Items


Sant proposal: \$250,000



Confirm all information on the bid form is correct and then click "Submit." Once you click "Submit," Clark-W.E. O'Neil JV will receive your proposal as well as an email notification.

Sent proposal: \$250,000		Subm
Sam's Demolition San Francisco, CA, USA Sam Samuels Estimator +1 333-333-3333 +1 222-222-222	sam@samsdemo.com)4
Line Items		
Description	Quantity Unit Cost	Total Co:
Demolition		\$250,00
Base Bid		\$250,00
Attachments		
🚡 Sam's Demo - Skyscraper Proposal.p (221 KB)		
		Back to Edit Subm

You will receive a confirmation.




+ Add tracking data

Go to Bid Board

You can ensure your bid was submitted successfully by checking that the "Status" has changed to "Submitted" and the bid form now says "Sent proposal" with the date and time the proposal was sent.

2 Skyscraper o	on 3rd and	Mission	Bid amount \$250,000 Mar 3, 2023 at 1:14 PM	Status Submitted	
erview Files	Messages	Bid Form			
Skyscraper BuildingConnect					
Sent proposal:	\$250,000	Sent on Mar 3, 2023 at 1:14 PM PST		Already submi outside of Buil	
Sam's Demolition				Log your bid in	
San Francisco, CA, US		4 000 000 0000 L 4 000 000 000			
Sam Samuels	Estimator 4	1 333-333-3333 +1 222-222-222	22 sam@samsdemo.com		
Line Items		Quantity Unit Cost	Total Cost		
Demolition			\$250,000		
Base Bid			\$250,000		
Attachments					
Sam's Demo - Sk	syscraper Prop	osal.p (221 KB)			

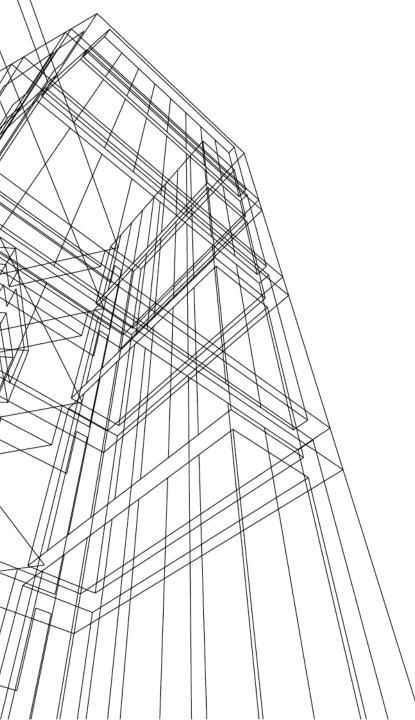

PROCUREMENT – BID OPENING

Submit Bids on BuildingConnected prior to the bid opening date/time

Late bids will not be accepted

Hard copy bids accepted if needed prior to the bid opening date/time

Bid bonds required with your proposal

PROCUREMENT – STEPS AFTER THE BID OPENING

Lowest responsive and responsible bidder to be brought in for post-bid meeting. BID THE SCOPE OF WORK, WITHOUT EXCLUSIONS/CLARIFICATIONS AND MEET OR EXCEED COMPLIANCE REQUIREMENTS.

If required, second or third responsive and responsible bidder to be brought in for a post-bid meeting

Upon completion of post-bid meeting, request for approval sent to CCA/CDA

Subcontract agreements issued upon approval by CDA. For long lead items, subcontractors may receive a Letter of Intent to commence with shop drawing preparations and potentially material/equipment procurement.

OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

CONCLUSION – NEXT STEPS

- Meet the Primes
- Site Walk Through
- RFI'S are due no later than the Question Cut-Off Date / Time posted on <u>www.cot3.com</u> and <u>www.ord21.com</u>
- Review and acknowledge all Clarifications & Addenda
- Submit Bid(s) through Building Connected no later than the Bid Opening Date / Time posted on <u>www.cot3.com</u> and <u>www.ord21.com</u>

Bid Package Schedule_v1 : Sheet1

CLA CONSTRU	RK	W·E	O'NEIL					
TERMINAL 3		NTO						
BID PACKAGE			SCHEDULE					
Updated:	1/5/2024							
•			to change at COT3's discretion. Updates will be poste	ed on COT3's web	osite and notices o	distributed via Building	gConner	
Bid Package Description	Bid Pkg	Trade Pacakg e	Trade Package Description	Notice of Bid Opportunity Date	Invitation to Bid Date	Pre-Bid Conference Date / Time	Question Cut-Off Date / Time	Bid Opening Date / Time
		2.1	Cast-in-Place Concrete	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.2	Masonry	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.4	Spray Fireproofing	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.5	Millwork - including wall paneling & countertops	10/26/2023	01/12/2024	01/19/24 10:00 AM	01/26/24 5:00pm	02/13/2024 2:00pm
		2.6	Civil/Sitework - Paving, Excavation, Site Demo,	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/17/2024 2:00pm
		2.7	Excavation Support & Shoring Systems	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/17/2024 2:00pm
		2.9	Fall Protection/Building Maintenance Equipment	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/17/2024 2:00pm
		2.10	Waterproofing/Air Barriers	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/17/2024 2:00pm
		2.19	Ornamental Metals	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/17/2024 2:00pm
		2.8	New Roofing Systems & Roof Patching	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.11	Ceilings	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.13	Terrazzo	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Remaining	2	2.15	Painting & Intumescent Fireproofing	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Trades	2	2.16	Metal Wall Panels	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm

CONCLUSION – QUESTIONS

Key takeaways:

- Return all documents needed with bid (reference the checklist)
- Be on the lookout for Addendums
- Complete the bid form in its entirety
- Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection
- Account for all Logisitics, DBE and Workforce requirements

SUBMIT ALL QUESTIONS

TO: ProjectCOT3.inquiries@clarkconstruction.com

NOTICE: NOTHING DISCUSSED TODAY IS INTENDED TO ALTER THE BID DOCUMENTS. ALL CLARIFICATIONS MUST BE SUBMITTED THROUGH THE REQUEST FOR INFORMATION (RFI) PROCESS FOR PROPER REVIEW AND RESPONSE.

IN CASE OF CONFLICTS BETWEEN TODAY'S DISCUSSIONS AND THE BID INFORMATION, BIDDERS SHOULD SUBMIT A PRE-BID RFI FOR CLARIFICATION AND GUIDANCE

Site Tour

1 PM TODAY

TERMINAL 3

LOWER LEVEL

NEAR BAGGAGE CLAIMS CAROUSEL 6

BRING YOUR DRIVERS LICENSE IF YOU ARE NOT BADGED

Meet the Primes/ Potential Bidders

Civil/Sitework - Paving, Excavation, Site Demo	Excavation Support & Shoring Systems	Fall Protection/ Building Maintenance Equipment	Waterproofing/ Air Barriers	Ornamental Metals	
 Berger Excavation Contractors, Inc. John Keno & Company, Inc. K-Five Construction Corp. Lima Excavating Lindahl Brothers, Inc. Norman Mechanical, Inc. Plote Construction Quality Excavation Reyes Group Ltd. Rossi Contractors Inc. 	Keller North America, Inc. Michel's Construction, Inc. Stalworth Underground, LLC Thatcher Foundations, Inc.	Bryker Enterprises, LLC Pro-Bel USA, Inc. Sky Climber Access Solutions, LLC Tractel Ltd. Swingstage Division	Barrier Corp BOFO Waterproofing Systems JP Larsen Inc. Kedmont Waterproofing Co. Superl Inc.	Chicago Ornamental Iron Meccor MTH Industries Specialty Construction Sturdi Iron	
