O'Hare Terminal 3 Improvements

COT3 Non-Mandatory Pre-Bid Conference Meeting & Meet The Primes Event







This presentation and a copy of the sign-in sheet will be published to www.cot3.com

If you are attending virtually, please type your name, company name, email address and phone # in the chat

NOTICE: NOTHING DISCUSSED TODAY IS INTENDED TO ALTER THE BID DOCUMENTS. ALL CLARIFICATIONS MUST BE SUBMITTED THROUGH THE REQUEST FOR INFORMATION (RFI) PROCESS FOR PROPER REVIEW AND RESPONSE.

IN CASE OF CONFLICTS BETWEEN TODAY'S DISCUSSIONS AND THE BID INFORMATION, BIDDERS SHOULD SUBMIT A PRE-BID RFI FOR CLARIFICATION AND GUIDANCE.

Agenda

- Introductions
- II. Project Overview
- III. Trade Packages
- IV. Compliance
- V. Contract Administration
- VI. Safety
- VII. Quality
- VIII. Procurement
- IX. Conclusion & Next Steps
- X. Meet the Primes / Potential Prime Contractors

Main points:

- Return all documents needed with bid (reference the checklist)
- Be on the lookout for Addendums
- Complete the bid form in its entirety
- Bid the full scope of work, without exception
- Account for all Logisitics, DBE and Workforce requirements





INTRODUCTIONS

- OWNER: Chicago Department of Aviation (CDA)
- PROGRAM MANAGER: Connect Chicago Alliance (CCA)
- CONSTRUCTION MANAGER AT RISK (CMAR): Clark-W.E. O'Neil JV (COT3)
 - Partner Firms
 - Cotter Consulting, Inc.
 - McKissack & McKissack Midwest, Inc.







PROJECT OVERVIEW - SCOPE OF WORK

- Expansion of the Departures and Arrivals levels to create room for a new outbound baggage makeup area, additional hold-room space and a new American Airlines Club space
- Demolition of an existing bag claim area and construction of a new inbound bag claim area
- Reconfiguration of the TSA checkpoints
- Reconfiguration of vertical transportation (elevators and escalators)
- Renovation of the existing restrooms
- ➤ Demolition and reconfiguration of existing airport/airline support spaces
- Roof replacement of Terminal 3



PROJECT OVERVIEW – T3 IMPROVEMENTS & SUPPLEMENTAL BAGROOM – SCHEDULE & LIQUIDATED DAMAGES

NOTICE TO PROCEED:

ANTICIPATED 4/26/24

SUBSTANTIAL COMPLETION:

2/10/27

REFER TO PUBLISHED SCHEDULE FOR MORE DETAIL

SECTION 4 TIME OF COMPLETION/LIQUIDATED DAMAGES/WEATHER AND MORATORIUM DAYS TABLE

NO.	MILESTONE	MILESTONE DATE	AMOUNT OF LIQUIDATED DAMAGES	
1.	AA Club Shell ready for tenant fit out by others (Schedule activity CDA-1010, UL - AA Club TI Start)	4-Mar-25	\$5,000 per calendar day	
2.	Gate K1 including partial hold-room fit out (Schedule activity CS-AA-1990, Complete Gate Opening Checklist for K1 – Hold Rooms & AA Club)	22-Aug-25	\$5,000 per calendar day	
3.	Gate L2A including partial hold-room fit out (Schedule activity CS-AA-2010, Complete Gate Opening Checklist for L2A- Hold Rooms & AA club)	22-Aug-25	\$5,000 per calendar day	
4.	Concession shell ready for tenant fit out (Schedule activity IA-UL-2G.A1360, Final Acceptance and Turnover – Airline Ops & Commercial)	17-Sep-25	\$5,000 per calendar day	
5.	Substantial Completion (Schedule activity Mile-110, Substantial Completion)	10-Feb-27	\$3,000 per calendar day	

PROJECT OVERVIEW – T3 IMPROVEMENTS & SUPPLEMENTAL BAGROOM – PRELIMINARY AIRSIDE LOGISTICS





O'Hare T3 Improvements

Airside Access - Trucking, Equipment Mobilization, & Deliveries

- 1. T3 Area of Work
- 2. Construction Vehicle Inspection Area #5 (CVIA 5) - Gate Access to Airside

Legend

- ... Airside
- Landside
- Active Taxiway



PROJECT OVERVIEW - PRELIMINARY AIRSIDE LOGISTICS


Airside Access – Trucking, Equipment Mobilization, & Deliveries

Keynotes

- Primary Vehicular Access via Construction Vehicle Inspection Area #5 (CVIA 5) – Gate Access to Airside.
- During full duration of expansion work: Stabilized construction entrance w/ trackout control (synthetic/movable). Full-time tire wash by trades. Full-time sweeper by trades.
- During full duration of expansion work: Full time dedicated flaggers required by trades

Legend

- Construction Vehicular Traffic
- Construction Foot Traffic
- Guard Post

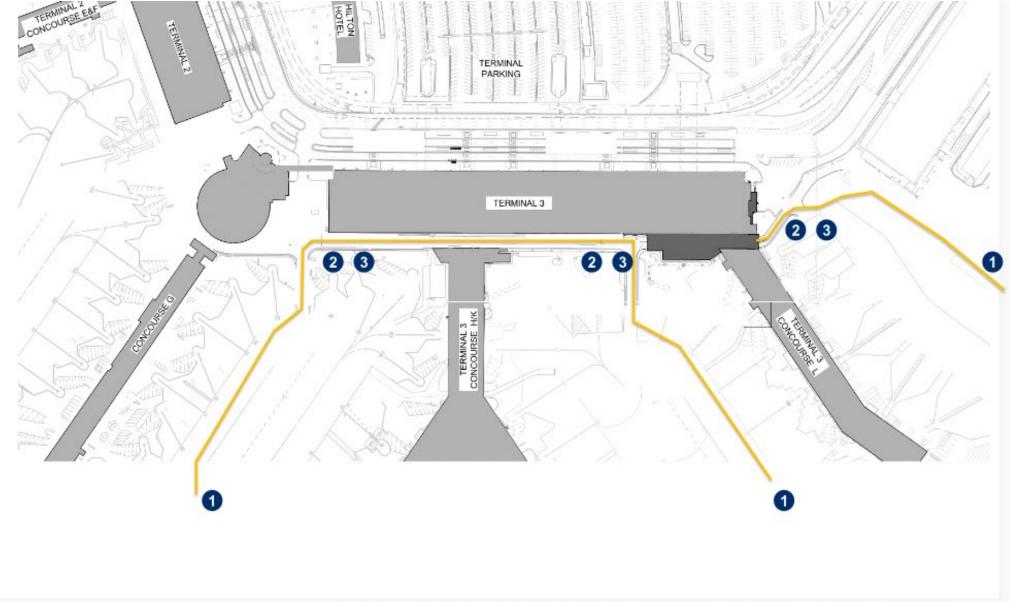

^{**}Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."

PROJECT OVERVIEW – PRELIMINARY AIRSIDE LOGISTICS


Airside Access – Trade Access On Foot

Keynotes

- Airside trade access on foot through existing Guard Post #8 & #10
- 2. Guard Post #8
- 3. Guard Post #10

Legend

- Construction Vehicular Traffic
- Construction Foot Traffic
- Guard Post

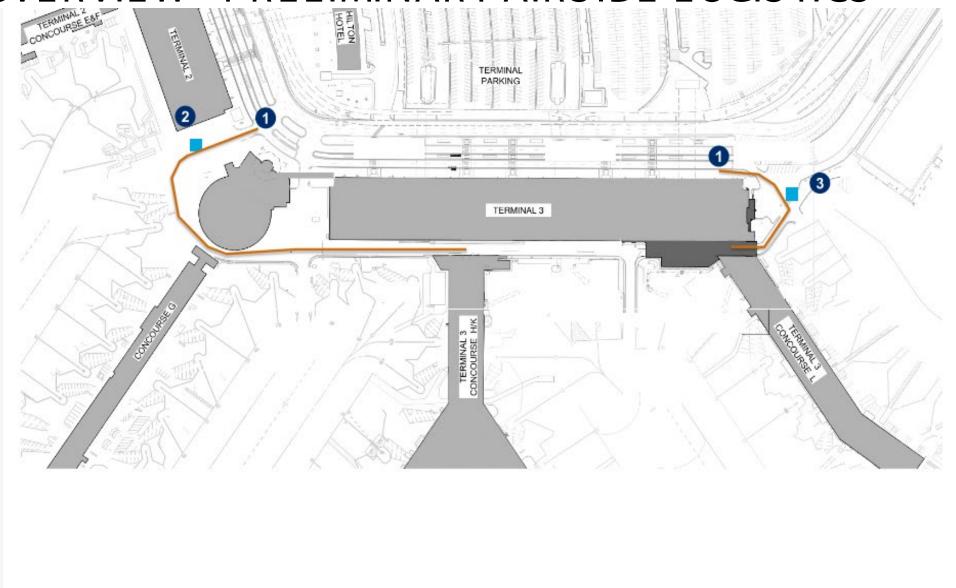


PROJECT OVERVIEW – PRELIMINARY LANDS IDE LOGISTICS

Landside Access – Trucking, Equipment Mobilization, & Deliveries (NIGHT WORK)

Keynotes

- Primary Vehicular Access for Landside Construction
- Landside Construction Deliveries As Req'd to Service Work Areas. Schedule According to Area "Work Rules"
- Full-time sweeper required by trades during expansion area construction at VSR & haul routes
- Full time dedicated flaggers required by trades during expansion construction at VSR & haul routes.

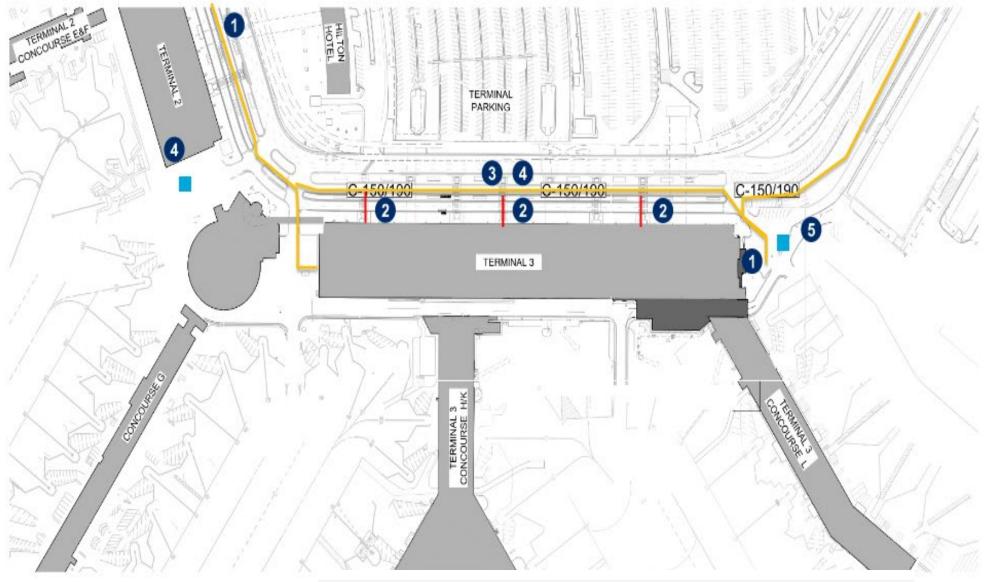

^{**}Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."

PROJECT OVERVIEW - PRELIMINARY APRON WORK LOGISTICS


Apron – Work Rules

General Notes

- Subcontractor is responsible for maintaining tug traffic access to OH to all baggage areas including through the overhead doors at all times during operations.
- Gate K2 will remain operational. Work adjacent K2 must be scheduled & coordinated in advance with Owner and Clark-WE O'Neil JV
- During full duration of expansion work: Stabilized construction entrance w/ trackout control (synthetic/movable). Full-time tire wash by trades. Full-time sweeper by trades, by trades performing work on the VSR as required
- Full-time sweeper required by trades during expansion area construction at VSR & haul routes

Legend

- Jersey Barricade Construction Area
- Jersey Barricade Temp Scheduled outing w/ Gate K2
- OH Protection
- Flagger
- Tire-Wash/Track-out Control
- OH Door
- Stair Tower Landing at Apron, Upper Level, Roof Level

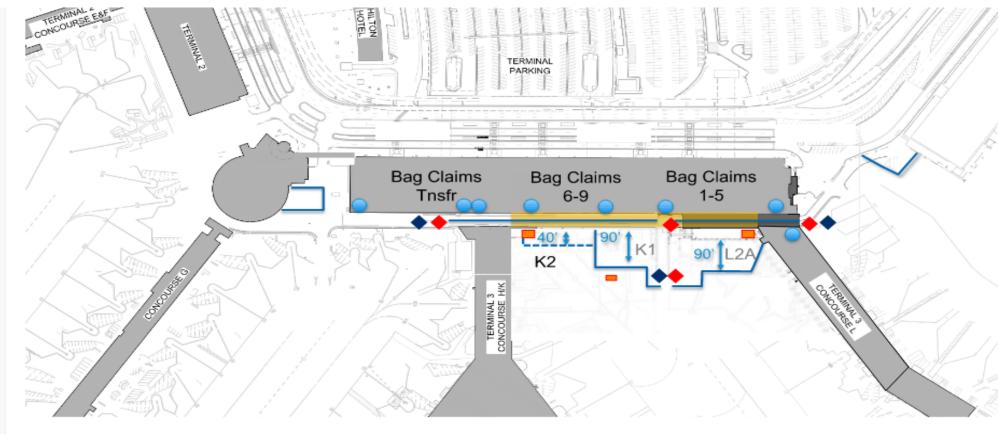

INCL. IN YOUR BID AS NEEDED FOR YOUR WORK

^{**}Preliminary, subject to change. Due to field conditions the subcontractor includes reasonable adjustments as required."

NOTICE:

BIDDERS MUST CONDUCT A SITE INSPECTION TO UNDERSTAND THE CONDITIONS, FACILITIES, AND SITE LOGISTICS RELEVANT TO THE WORK OUTLINED IN THE CONTRACT.

THE FAILURE TO VISIT THE SITE DOES NOT EXEMPT OR CHANGE THE BIDDER'S RESPONSIBILITY TO COMPLETE THE WORK IN ACCORDANCE WITH THE CONTRACT DOCUMENTS.

TRADE PACKAGES: BID PACKAGE 1, TRADE PACKAGES 2.6, 2.7, 2.8, 2.11, 2.13, 2.15, 2.16

Bid Package Schedule_v1 : Sheet1

Dia i donago c								
CLA	RK	W·E	O'NEIL					
TERMINAL 3 II	MPROVEME	NTS						
BID PACKAGE	/ TRADE P	ACKAGE	SCHEDULE					
Updated:	1/5/2024							
Note: Below da	tes / times a	ire subject	to change at COT3's discretion. Updates will be poster	d on COT3's web	site and notices	distributed via Building	gConnected	
Bid Package Description	Bid Pkg	Trade Pacakg e	Trade Package Description	Notice of Bid Opportunity Date	Invitation to Bid Date	Pre-Bid Conference Date / Time	Question Cut-Off Date / Time	Bid Opening Date / Time
		2.19	Ornamental Metals	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.6	Civil/Sitework - Paving, Excavation, Site Demo,	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.7	Excavation Support & Shoring Systems	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.8	New Roofing Systems & Roof Patching	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
	Remaining 2	2.11	Ceilings	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.13	Terrazzo	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Remaining		2.15	Painting & Intumescent Fireproofing	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Trades	2.16	Metal Wall Panels	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm	
		2.14	Doors, Frames and Hardware	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.17	Interior Glass	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.20	TSA Systems Integrator	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.22	Pedestrian Security Equipment - Breach control	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.24	Overhead doors	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
	2.25	Signage	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm	
		1	 	I	1	 		

COMPLIANCE- REQUIREMENT SUMMARY

DBE Requirements

- Participation at any level
- Trade specific range: 24% 30%+ depending on trade

City Resident & Project Area Resident Requirements

- 50% City Residents
- 7.5% Project Area Residents
- Norwood Park
- Edison Park
- Jefferson Park
- Dunning
- Forest Glen
- Portage Park

Affirmative Action Requirements

- Minority participation: 19.6%
- Female participation: 6.9%

Buy America Build America (BABA) Project

 See specifications for complete requirements

Workforce Commitments

COMPLIANCE- DBE PARTICIPATION

- DBE Certification must be from the Illinois Unified Certification Program ("IL UCP") for the participation to apply towards the project requirements
- The DBE Contract Specific Goals set during the contract bid are applicable to any adjustments made to the contract after award.
- The contribution towards meeting the Contract Specific Goals only include the dollars paid to the DBE firm for the work performed within its certified Area of Specialty.
- All Subcontractors are required to use the B2Gnow system to track compliance and payments, including:
 - Entering all certified and non-certified Sub tier Subcontractors, including contract values.
 - Confirming payment(s) received and reporting sub tier Subcontractor payments made.
 - Ensure all sub tier Subcontractor commitments are current and all payments are confirmed.



COMPLIANCE- DBE PARTICIPATION



CITY OF CHICAGO

Department of Procurement Services Aileen Velazquez, Chief Procurement Officer

121 North LaSalle Street, Room 806 Chicago, Illinois 60602-1284 Fax: 312-744-3281

DBE SPECIAL CONDITIONS FOR FAA/FTA/FHWA (IDOT) FUNDED CONTRACTS
CONSTRUCTION, SERVICES, TASK ORDER SERVICES, AND SUPPLY

ARTICLE 1. SPECIAL CONDITIONS REGARDING DISADVANTAGED BUSINESS ENTERPRISE COMMITMENT Contractor must comply with the following terms and conditions where Work or Services are funded in whole or in part by any federal flueds including but not limited to FHWA. FTA and FAA.

1.1. Policy and Terms

In the event of a conflict between these Special Conditions and 49 CFR Part 26, the provisions of 49 CFR Part 26 shall control.

It is the policy of the City that Disadvantaged Business Enterprises (DBEs) as defined in 49 CFR Part 26, have the maximum opportunity to participate fully in the performance of contracts subject to 49 CFR Part 26. Contractor must not discriminate against any person or business on the basis of race, color, national origin or sex in the performance of this Contract. Contractor must carry out applicable requirements of 49 CFR Part 26 in the award and administration of United States Department of Transportation (DOT)-assisted contracts and take affirmative action to ensure that businesses owned by socially and economically disadvantaged individuals have full opportunity to participate.

The CMAR has set an overall DBE Program Goal of 30%.

Failure to carry out the commitments and policies set forth in this Article constitutes a material breach of the Contract and may result in the termination of the Contract or such remedy as the CMAR deems appropriate.

1.1.1. Contract-Specific DBE Participation Goal

The CMAR sets contract-specific goals for participation in furtherance of reaching its overall DBE Program Goal.

For purposes of this contract, the CMAR has set the following contract goal:

Contract DBE Participation Goal: 24%

Note: if this contract is task-order based, goals will be set for the individual task orders; in the context of each task order, these provisions will apply to those task order goals as if they were an overall contract goal.

A bid or proposal may be rejected as non-responsive if the bidder/proposer fails to submit one or more of the following with its bid demonstrating sits good faith efforts to meet the Contract DBE Participation Goal by reaching out to DBEs to perform work on the contract:

- A DBE compliance plan demonstrating how the bidder/proposer plans to meet the Contract DBE Participation Goal (Schedule D, D-1 or D-3 and Schedule(s) C, C-1 or C-3); and/or
- B. Documentation of Good Faith Efforts to obtain DBE participation in this contract.

Note: Schedules D and C are used for contracts for construction work. Schedules D-1 and D-3 are used for contracts for services, and Schedules D-3 and C-3 are used for task order based contracts.

The bidder/proposer must make good faith efforts to obtain DBE participation in this contract. The commitment will be reflected in Schedule D, D-1 or D-3. The bidder/proposer must document that it has obtained enough DBE participation to meet the Contract DBE Participation Good set forth above or, if unsuccessful in doing so, has made aducte Good Faith Efforts to meet the goal (see Section 1.7 "Good Faith Efforts"). If awarded the Contract, Contractor must expend not less than the committed percentage of the total Contract Price (including any amendments and modifications) for contract participation by DBEs.

For purposes of evaluating bidder/proposer's responsiveness, the Contract DBE Participation Goal will be a percentage of the total contract value. The Contract DBE Participation Goal applies to the total value of the contract, inclusive of all amendments and modifications. The Chief Procurement Officer also has the authority to review each proposed contract modification and amendment that by itself or aggregated with previous modification/amendment requests, increases the contract value by 10 percent of the initial award or \$50,000, whichever is greater, for opportunities to increase participation of DBEs already involved in the contract.

CMAR Federally Funded Instructions and Execution Documents
Technical 3 Innovancements

Bid Package No. 1 1

Tennisal 3 Improvements Bi6 Package No.: 1.1



interest

CITY OF CHICAGO ASSIST AGENCY LIST

	ATTACHMENT (On Bidder/Proposer's Let	
RETURN RECEIPT REQUES	TED	(Date)
(Assist Agency Name and Addre	Descr	Specification
Dear: (Bidder/Proposer)	intends to submit a bid/proposal in response	e to the above referenced specification with the CMAR.
Bids are due on The following areas have been id	entified for subcontracting opportunities on b	both a direct and indirect basis:
Our efforts to identify potential	subcontractors have not been successful in	n order to meet the Disadvantaged Business Enterpri
("DBE") contract goal. If you are please contact:	aware of any DBE firms that would be cap	pable of performing in any of the above-identified area
Name of Com	pany Representative	atAddress/phone
within (10) ten working days of r	eceipt of this letter.	
submitted. Written comments receipt of this letter to: Program Manager Comnect Chicago Allian 10510 West Zemike Roa Chicago, IL 60666 (Timely Information Op	on (Bidder/Proposer's) waiver request may ce d	, a request for the wairer of the contract goals will ly be directed within fifteen (15) working days of yo
	please contact the undersigned at	·
Sincerely,		
CMAR Federally Funded	Instructions and Execution Document	3

Street Business Asso	Chatham Business Association Small Business Dev.* 800 E. 78th Street			Chicago Minority Supplier Development Council Inc. * 105 W. Adams, Suite 2300 Chicago, IL 8009.3-6233				
. 51st Street	Chicago, IL 604	10		Cilicago, iz o	0000-0200			
go, IL 60615	773-994-5006							
85-3401	773-855-8908	Greater Southwest Development Corpora		ation		rican Construction Industry		
285-3407	admin@cbaw	2601 W. 63rd Str			Association (
Iststreetbusinessass	www.cbawork	Chicago, IL 6062	29		650 W. Lake S			
	Maintains list	773-362-3373			Chicago, IL 60	661		
.51stStreetChicago.c	Provides train	c.james@grea						
tains list of certified		www.greatersc						
des training for busir	Chicago Urb	list of certified	South Shore Chamber,	nc *		Sustainable Options for Urban Living, Inc. (SOUI		
	4510 S. Michi	training for bus	1750 E. 71st Street			11603 S. Throop		
of God Resource C	Chicago, IL 6		Chicago, IL 60649-2000			Street Chicago, IL		
S. Halsted	773-285-580(773-955- 9508			60643		
lale, IL 60827	iiohnson@chi		773-955-9554			773-250-1770 Ext 702 773 250-1770		
2-9323	Maintains list	HIRE360	Tonya Trice, Executive D	irector				
80-0121	Provides train	2301 S Lake S	info@southshorechambe			Cyndi@soul- program.com www.soul-		
ogrc@gmaiil.com	Provides train	Chicago, IL 60	www.southshorechamber			program.com		
angelofgodresource		312 575-2500	Maintains list of certified t			Maintains list of certified firms: Yes		
ains list of certified		info@HIRE360	Provides training for busing			Provides training for businesses: Yes		
les training for busir		www.HIRE360						
co deming for bulli	Contractor A	list of certified	The Monroe Foundation			Turn 2 Growth		
African American	1507 E. 53rd S	training for bus	1547 South Wolf Road			15475 S. Park		
/. Chicago Ave.	Chicago, IL. 6		Hillside, Illinois 60162			South Holland, IL 60473		
	312-436-0301		773-315-9720			708-913-4700		
jo, IL 60651	info@contrac	Illinois Hispar	omonroe@themonroefou			info@turn2growth.org		
26-4497	www.contract	222 Merchand	www.themonroefoundatio	n.org		www.turn2growth.org		
aaabna.org	list of certified	Chicago, IL 60	Maintains list of certified t	irms: No		Maintains list of certified firms: Yes		
aabna.org	training for bu	312-425-9500	Provides training for busing	resses: Yes		Provides training for businesses: Yes		
ns list of certified		info@ihccbusir www.ihccbusir						
s training for busir	Council of B	Maintains list c						
Contractors Owners	Engineering	Provides traini	US Minority Contractors		c. ^	Women's Business Development Center *		
	1 South Wack	Flovides trainii	1250 S. Grove Ave. Suite	200		8 S. Michigan Ave., Suite 400		
S. Stony Island Ave.	Chicago, IL 6		Barrington, IL 60010			Chicago, IL 60603		
go, IL 60649	312-960-1238		847-352-5010			312-853-3477×220		
46-5658	msutton@infr	JLM Business	847-382-1787			312-853-0145		
46-5659	Maintains list	Center* 2622	larry.bullock@usminority			edimenco@wbdc.org		
@bcoechicago.org	Provides train	Chicago, IL 60	www.USMinorityContract			www.wbdc.org		
coechicago.org		773-826-3064	Maintains list of certified f			Maintains list of certified firms: Yes		
ins list of certified:		773-359-4021	Provides training for busing	nesses: Yes		Provides training for businesses: Yes		
s training for busir	Elite Service	lady930@prod						
-	420 Lake Cod	www.jlmcenter	Women Construction O	wners & Executi	ves (WCOE)*			
ject 5000 NFP	Deerfield, IL (Maintains list c	Chicago Caucus 308 Circle Avenue					
9th Street	847-453-8890	Provides traini	Forest Park, IL 60130					
IL 60619	jscifers@scig		708-386-1250					
5939	www.elitesdv		mkm@mkmservices.com					
1903	Maintains list	Native Americ	www.wcoeusa.org					
	Provides train	100 N. Riversii	Maintains list of certified t	irms: Yes				
ter@gmail.com		Chicago, IL 60	Provides training for busing					
fied firms: Yes		630-926-1700						
aining for busir	Federation o	info@nacc-il.o				1		
	4210 W. Irvin	www.nacc-il.or						
	Chicago, IL 6	Maintains list c						
	312-360-1122	Provides trainii						
	info@fwcchic							
	www.fwcchica							
	Maintains list	Rainbow/PUS						
	Provides train	930 E. 50th Stn						
		Chicago, IL 60						
		773-255-9087						
		773-256-2768						
		imitchell@rain						
*Prime Contract		www.rainbowp						
		Maintains list s						

Provides traini

*Prime Contractors should contact agency with subcontracting opportunities to connect certified firms

Rev. July 2020 – Information subject to change – visit www.chicago.gov/dos for the most recent list



OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

COMPLIANCE- WORKFORCE COMMITMENTS

Federal Requirements

Minority Worker Requirement – 19.6%

Female Worker Requirement – 6.9%

Chicago Requirements

City of Chicago Residency Requirement – 50%

Project Area Worker Requirement – 7.5%

The Contract requires compliance with Chicago Residency Ordinance, Section 2 92 330 of the Chicago Municipal Code.

Failure to meet these requirements will result in assessment of penalties in the form of liquidated damages

1/20 of 1% (0.05%), 0.0005, of the approved contract value shall be assessed to the prime Subcontractor for each percentage of shortfall toward the stipulated residency requirement.

CONTRACT ADMINISTRATION- SOFTWARE

Administrative

- B2Gnow
- DocuSign
- LCP Tracker
- Oracle Textura
- Wrap X

Project Management

- Revisto
- E-Builder
- Primavera P6
- Procore

CONTRACT ADMINISTRATION- SCHEDULE OF VALUES REQUIREMENTS

Subcontract shall include line items on their Schedule of Values for the following work activities (at the following percentages relative to total Subcontract value):

- Close-out Documentation and Submittals including but not limited to As-builts, Warranty Documents, LEED and Training (2%)
- Punch List (2%)
- Demobilization (2%)
- Cleanup (2%)
- Safety (2%)

Subcontractor shall include a line item on their Schedule of Values for the city's residency requirements as outlined in Exhibit B and in the Chicago Municipal Code section 2-92-330. The line item shall consist of the maximum possible of the liquidated damages associated with the project area and city resident requirements. Subcontractor shall be allowed to invoice this line item periodically, and only to the extent that these residency requirements have been met and confirmed through certified payroll. At the end of the Project an accounting will be tabulated to determine any liquidated damages owed by Subcontractor related to unmet residency requirements, and these damages will be funded from this line item in the Subcontractor Schedule of Values.

CONTRACT ADMINISTRATION- SCHEDULE

Schedule Resource Loading will be required by each Subcontractor:

- Manpower (Crew Size and Hours)
- Equipment (Type, Quantity and Equipment Hours)

CONTRACT ADMINISTRATION- PAYMENT APPLICATIONS

MANDATORY WITH EACH PAYMENT REQUEST:

- G702 AND G703
- STATEMENT OF SUBCONTRACTOR TO COT3
- CONDITIONAL WAIVER AND RELEASES ON PROGRESS PAYMENTS
- WAIVER OF LIEN TO DATE
- CHANGE ORDER REQUEST LOG
- IF APPLICABLE, CITY OF CHICAGO C&D DEBRIS RECYCLING COMPLIANCE FORMS
- IF APPLICABLE, DIESEL EMISSIONS COMPLIANCE FORM
- IF APPLICABLE, STORED MATERIAL DOCUMENTATION
- OTHER SAM DOCUMENTATION, AS APPLICABLE

CONTRACT ADMINISTRATION-INSURANCE

Owner Controlled Insurance Program (OCIP)

Insurance Administrator – Alliant

Each Subcontractor, along with all lower-tier subcontractors, including professional services and suppliers, must undergo the enrollment process. Alliant will assess and notify if any firm is ineligible for participation in the program.

The Subcontractor must input all lower-tier subcontractors into WrapX. The actual labor, categorized by classification, needs to be documented through monthly payroll entries in the WrapX portal.

Review and approval of insurance will be handled directly between the Subcontractor and Alliant.

Additional insurance requirements outside of OCIP. See Sample Subcontract – Exhibit E

CONTRACT ADMINISTRATION- OCIP

Enrolled Parties

- All Eligible Prime Subs
- All Eligible
 Subcontractor Tiers
 performing labor or
 services at the Project
 Site
- Other Parties Enrolled at Owners Discretion

Excluded Parties

- Demolition
- Hazardous Materials Contractors/Transporters
- Vendors, Suppliers, Fabricators, Material Haulers, Truckers, Cranes
- Subcontractors of any tier not eligible for and are excluded from the OCIP

CONTRACT ADMINISTRATION- OCIP ENROLLMENT

Contract signed with Subcontractor

The Awarding Contractor Notifies Alliant through a Notice of Award (NOA) Letter

Enrollment in project

- Alliant works directly with the subcontractor for enrollment
- Enrollment must be completed online and be accepted before commencing work onsite
- If a subcontractor is onsite prior to enrollment, Carrier is not obligated to cover any accidents- there is no coverage.

Enrollment – requires the following information:

- Onsite Enrollment Form
- Insurance Cost Worksheet with WC/GL/XS Rate & Declaration Pages
- Offsite proof of insurance COI & Policy Endorsements (All Tiers)

Ongoing Subcontractor Responsibilities:

- Submit monthly payroll to Alliant through online entry
- Provide renewal offsite COI & Endorsements (All Tiers)

CONTRACT ADMINISTRATION- PROFESSIONAL LIABILITY INSURANCE



CDA'S PPL INSURANCE PROGRAM IS A
REQUIREMENT FOR ALL SUBCONTRACTORS
THAT HAVE A SCOPE OF WORK THAT
INCLUDES DESIGN AND ENGINEERING



THE COST OF PARTICIPATING INTO THE PROGRAM IS 3/4% AND WILL BE DEDUCTED FROM THE CONTRACT AMOUNT



NO CHANGE ORDERS WILL BE ISSUED IF THIS FEE IS NOT RETURNED IT APPEARS THIS COST HAS NOT BEEN RETURNED TO ANY CONTRACTOR TO DATE (YET)

SAFETY

- Chicago Department of Aviation Construction Safety Manual November 2022
- Clark-W.E. O'Neil JV Safety Manual
- Subcontractor is required to: (i) develop a sitespecific safety plan, and (ii) reference subcontract for additional safety requirements and dedicated on-site Safety representation



CONSTRUCTION SAFETY MANUAL NOVEMBER 2022



QUALITY ASSURANCE / QUALITY CONTROL

Technical Specification 01 4000 – Quality Requirements

Prior to commencing work:

- The Subcontractor must submit a Quality Control Plan for approval by COT3
- The Subcontractor is responsible to conduct a Pre-activity meeting

Each Subcontractor is required to provide a dedicated Quality Control representative onsite at all times

PROCUREMENT - QUESTIONS, PRE-BID RFI'S & ADDENDUMS

Bid Package Schedule_v1 : Sheet1



TERMINAL 3 IMPROVEMENTS

BID PACKAGE / TRADE PACKAGE SCHEDULE

Updated: 1/5/2024

Note: Below dates / times are subject to change at COT3's discretion. Updates will be posted on COT3's website and notices distributed via BuildingConnec

Bid Package Description	Bid Pkg	Trade Pacakg e	Trade Package Description	Notice of Bid Opportunity Date	Invitation to Bid Date	Pre-Bid Conference Date / Time	Question Cut-Off Date / Time	Bid Opening Date / Time
		2.19	Ornamental Metals	10/26/2023	01/16/2024	01/23/24 10:00 AM	01/30/24 5:00pm	02/16/2024 2:00pm
		2.6	Civil/Sitework - Paving, Excavation, Site Demo,	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.7	Excavation Support & Shoring Systems	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.8	New Roofing Systems & Roof Patching	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.11	Ceilings	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.13	Terrazzo	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
Remaining 2	2.15	Painting & Intumescent Fireproofing	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm	
Trades	2	2.16	Metal Wall Panels	10/26/2023	01/23/2024	01/30/24 10:00 AM	02/06/24 5:00pm	02/23/2024 2:00pm
		2.14	Doors, Frames and Hardware	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.17	Interior Glass	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.20	TSA Systems Integrator	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
		2.22	Pedestrian Security Equipment - Breach control	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm
	2.24	Overhead doors	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm	
		2.25	Signage	10/26/2023	01/31/2024	02/07/24 10:00 AM	02/14/24 5:00pm	03/01/2024 2:00pm

PROCUREMENT - REQUEST FOR INFORMATION



SUBMIT ALL PROJECT RFI'S VIA EMAIL OR THROUGH BUILDING CONNECTED





Email:

ProjectCOT3.inquiries@clarkconstruction.com



Subject: RFI T3 Improvements "Trade Package" – "Company Name"

NOTES:

- MAKE SURE TO SUBMIT ALL QUESTIONS VIA RFI BY THE QUESTION CUT-OFF DATE & TIME INDICATED. LATE QUESTIONS WILL NOT BE RESPONDED TO!
- ALL RESPONSES WILL BE PROVIDED VIA BID ADDENDUM.

PRE-BID ADDENDUM TIMELINE

ADDENDUMS, IF ANY, ARE PLANNED TO BE ISSUED FOR ISSUANCE NO LATER THAN ONE WEEK BEFORE THE BID OPENING

LIST OF ANTICIPATED ADDENDUMS:

- UPDATED PROJECT SCHEDULE
- UPDATED EXHIBIT B'S
- ADDENDUM #01 DESIGN UPDATES/CLARIFICATIONS
- ADDENDUM #02 DESIGN UPDATES/CLARIFICATIONS
- ADDENDUM #XXX PRE-BID RFI RESPONSES

PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT - CHECKLIST

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submissi through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. □ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funder Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ■ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Base Bid Line Items - Pricing

Alternates

Inclusions

*Scope included per Exhibit B

Scope-Specific Information and Unit Costs



PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

Scope-Specific Information and Unit Costs (continued from above)

General Acknowledgements

202141 : O'Hare Terminal 3 Improvements 2000 West Baimoral Avenue, Terminal 3, Chicago, IL 60666, United States of America				
"Asbestos Abatement of 4" LTWR Fittings (\$ per Each)	per each	\$		
"Lead Based Paint Abatement of door frames (\$ per Each)	per each	\$		
*Lead Based Paint Abatement of wide flange beams (\$ per SF)	per square foot	\$		
"Lead Based Paint Abatement of pipe hangars (\$ per Each)	per each	s		
*Lead Based Paint Abatement of valve wheels (\$ per Each)	per each	\$		
*Lead Based Paint Abatement of electrical boxes (\$ per Each)	per each	s		
Lead Based Paint Abatement of pipe - assume 4 OD (\$ per Linear Foot)	per linear foot			
*Lead Based Paint Abatement of bollards or pipe quards (\$ per Each)	per each			
"Lead Based Paint Abatement of handrall/guard rail (\$ per Linear Foot)	per linear foot			
General Acknowledgments	Mark "yes" to all	yes/no	guest	io
"Have you prepared your proposal in accordance with the Plans and Specifications?) Yes	s (
*Have you reviewed all Division 0 and 1 of the Specifications?			5 C	
"Have you reviewed the requirements for shift work and included premium cost as applicable?			s C	
*Does your scope require design services or engineering?	C) Yes	s C)
"If Yes to Design Services and Engineering, have you included 3/4% of your Bid total in you Bid for Project Professional Liability Insurance that may not be refunded at the end of the Job?	C) Yes	s C)
Subcontractor acknowledges their responsibility for all liquidated damages as a result of their performance and Work, as defined in the Owner Master Agreement, No. 234140.	C) Yes	s C)
Subcontractor acknowledges that they shall be responsible for any Builders Risk and General Liability deductibles associated with a claim resulting from your Work, as outlined in Exhibit D or E of the Subcontract Agreement.	C	Yes	s C)
*The Bidder agrees to submit its bid without limitations or exceptions, except as permitted by the Contract Documents.	C) Yes	s C)
*The Bidder further agrees that if awarded the Contract, the Bidder shall perform the Contract with no limitations or exceptions.	C) Yes	s C)
*The Contract Base Bid shall include the entire scope of Work and requirements of Part One, Part Two, Part Three and the Contract Drawings of the Contract Documents.	C) Yes	s C)
* The Contract will be awarded to the responsive and responsible Bidder offering the lowest Contract Base Bid, as determined by the Chief Procurement Officer.	C) Yes	s C)
"The contractor acknowledges that they may be asked to proceed with a Letter of Intent.	C) Yes	s C)
"Bids will be compared based on the Bid Amount(s) and any combination of Alternates of each Trade Package, correctly computed, and a contract, if awarded, will be to the lowest response and responsible bidder, as determined by the CMAR.	С) Yes	s C)


PROCUREMENT – BID FORM (SUBMIT ONLINE)

BUILDING CONNECTED BID FORM SECTIONS

General Acknowledgements (continued from above)

Checklist of Required
Documents to attached to
your electronic bid submission
through building connected

DBE Schedules (as applies)

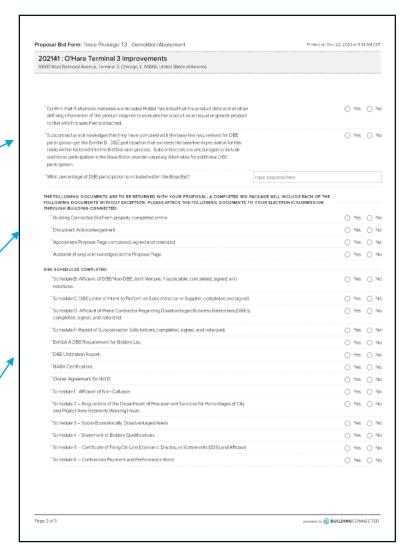

PROCUREMENT – BID FORM (SUBMIT ONLINE)


BUILDING CONNECTED BID FORM SECTIONS

Checklist of Required Documents to attached to your electronic bid submission through building connected

FAA Certifications

Other Requirements

Subcontract Exhibits

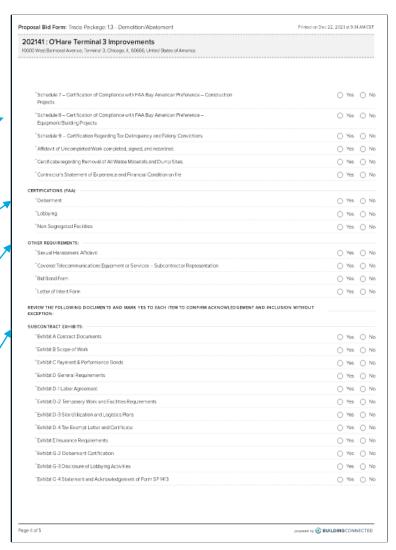

PROCUREMENT – BID FORM (SUBMIT ONLINE)


BUILDING CONNECTED BID FORM SECTIONS

Subcontract Exhibits (continued)

Subcontract Attachments

Certifications

Attachments

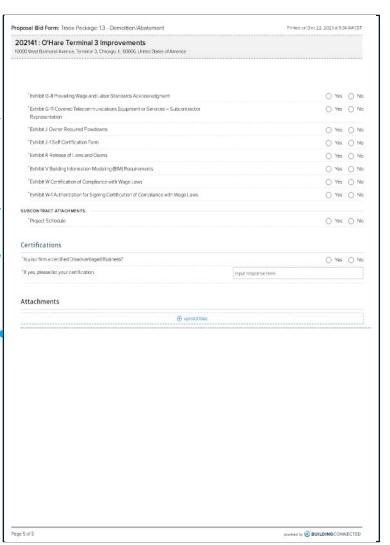

PROCUREMENT – CHECKLIST (list of items to be returned with bid)

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funder Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Building Connected Bid Form; properly completed online. Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



PROCUREMENT - DOCUMENT ACKNOWLEDGEMENT

Complete and return with your bid.

	(Federally Funded)
This ch	ecklist is intended to assist Bidders but does not necessarily reference all documents required in this particul
Specific a bid.	cation. Bidders should review this entire Part One for additional requirements. Missing forms may invalida
Review	the following Documents and <u>initial each item</u> to confirm acknowledgement and inclusion without exception
Subcon	tract Exhibits:
1.	Exhibit A Contract Documents
2.	Exhibit B Scope of Work
3.	Exhibit C Payment & Performance Bonds
4.	Exhibit D General Requirements
5.	Exhibit D-1 Labor Agreement
6.	Not Used
7.	Exhibit D-3 Site Utilization and Logistics Plans
8.	Exhibit D-4 Tax Exempt Letter and Certificate
9.	Exhibit E Insurance Requirements
10.	Exhibit G-2 Debarment Certification
11.	Exhibit G-3 Disclosure of Lobbying Activities
12.	Exhibit G-4 Statement and Acknowledgement of Form SF 1413
13.	Exhibit G-8 Prevailing Wage and Labor Standards Acknowledgment
14.	Exhibit G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation
15.	Exhibit J Owner Required Flowdowns
16.	Exhibit J-1 Self Certification Form
17.	Exhibit R Release of Liens and Claims
18.	Exhibit V Building Information Modeling (BIM) Requirements
19.	Exhibit W Certification of Compliance with Wage Laws
20.	Exhibit W-1 Authorization for Signing Certification of Compliance with Wage Laws
Subcon	tract Attachments:
1.	Project Schedule
	Letter of Intent
2.	
2	
	rized Signature
	rized Signature
Autho	
Autho	Date
Autho Title I hereby	Date

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



PROCUREMENT – PROPOSAL PAGES S5-1 - S5-5 (as applies)

SECTION 5 PROPOSAL TO BE EXECUTED BY A CORPORATION

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Conferious of Section (In Proposal Pages, 7) Certifications and 8) Addends Nos. (none unless than 1) of the Conference of the Confe

and affirms that the corporation shall be bound by all the terms and condition.

Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only
the corporation has taken express written exception thereto in the sections of this specification designated by

Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an EDS Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are a complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted any certification in the EDS false, macourate or incomplete.

Further, the undersigned being duly sworm deposes and says on oath that no disclosures of ownership withheld and the information provided therein to the best of its knowledge is current and the undersigned line any agreement with any other bidder (proposer) or prospective bidder (proposer) or with any other corporation relating to the price named in this proposal or any other proposal, nor any agreement or armag any act or omission in restraining of free competition among bidders (proposers) and has not disclosed to corporation the terms of this bid (proposal) or the price named herein.

Proposals must be submitted with original signatures in the space provided. Proposals not properly signed

NAME OF CORROBATION

PROPOSAL TO BE EXECUTED BY A SOLE PROPRIETOR

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Palas or Drawings (if applicable). 5) Leptialed Specifications or Scope of Services, Evaluation/Selection Critegia and Submittal.

PROPOSAL TO BE EXECUTED BY A PARTNERSHIP

The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation Selection Criteria and Submittal Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless indicated here) and affirms that the partnership shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the nattracribin has taken excess writtine exception thereto in the sections of this specification desimated for that turnose.

Under penalty of perjury, the undersigned. (1) warrants that he/she was authorized to submit an EDS on behalf of the Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are true, accurate and complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of this proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted that would render any certification in the EDS false, inaccurate or incomplete.

Further, the undersigned being duly swom deposes and says on oath that no disclosures of ownership interests have been withheld and the information provided therein to the best of its knowledge is current and the undersigned has not entered into any agreement with any other bidder (proposer) or prospective bidder (proposer) or with any other person, firm or corporation relating to the price named in this proposal or any other proposal, nor any agreement or arrangement under which

Daminomante (IF DEDDEN) & Doos sal Pages, 7) Certifications and 8) Addenda Nos. (none unless indithe sole proprietor shall be bound by all the terms and conditions c there a complete set thereof is attached to this proposal, except only ritten exceptions therefor in the sections of this sencitization designs

ned: (1) warrants that he/she was authorized to submit an EDS on b that all certifications and statements contained in the EDS are true, bmitted on-line; and (3) further warrants that, as of the date of subnges in Circumstances since the date that the EDS was submitted to curate or incomplete.

om deposes and says on oath that no disclosures of ownership interior to the best of its knowledge is current and the undersigned proposer) or propective bidder (proposer) or with any other person in this proposal or any other proposal, nor any agreement or arrange ee competition among bidders (proposers) and has not disclosed to basl) or the price named herein.

nal signatures in the space provided. Proposals not properly signed

PROPOSAL TO BE EXECUTED BY A JOINT VENTURE

The undersigned hereby acknowledges having received Bid Package No. 14 containing a full set of Contract Documents, including, but not insulined a, 1 harstanchus no Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation-Selection Criteria and Submittal Requirements (if RPFRPQ), 6) Proposal Pages, 7) Certifications and 8) Addental Nos. (none unless indicated here) and affirms that the Joint Venture allule be bound by all the terms and conditions contained in the

and affirms that the Joint Venture shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the Joint Venture has taken express written exception thereto in the sections of this specification designated for that purpose.

Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an EDS on behalf of the Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are true, accurate and complete as of the date the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of this proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted that would render any certification in the EDS false, inaccurate or incomplete.

Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership interests have been without the information provided therein to the best of its knowledge is current and the undersigned has not entered into any agreement with any other bidder (reconsort) or prospective bidder (persons) or with any other person. Imm or

SUBMIT ONE (1) OF THE APPLICABLE PROPOSAL EXECUTION FORMS WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED, SIGNED AND NOTARIZED

Note: In the event that this out (proposal) is signed by other than the resolution and interest a copy that section of Corporate By-Laws or other authorization, such as a resolution by the Board of Dirk permits the person to sign the offer for the Corporation. ATTEST: (Corporate Secretary Signature) (Affix Corporate Seal)		b 1903 Chapter 90 Sec. 4 et seq. (Print or Type)	JOINT VENTURE ADDRESS: (Print or Type) If you are operating under an assumed name, provide County registration number herein under as provided in the Illinois Revised Statutes 1965 Chapter 96 Sec. 4 et seq. Registration Number.
State of County of This instrument was acknowledged before me on this day of, 20 by as President (or other authorized officer) and	Outer authorizing occurrent): Partner Signature: Address: (Print or Type) Partner Signature: (Signature) Address: (Print or Type)	edged before me on this day of, 20 by as President (or other authorized officer) and(Corporation Name).	SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE JOINT VENTURE (If all members of the Joint Venture do not sign, indicate authority of signatories by attaching copy of Joint Venture agreement or other authorizing document): SIGNATURE OF Authorized Party: (Signature) TITLE OF SIGNATORY:
Secretary of(Corporation Name). (Seal) Notary Public Signature Commission Expires: CMAR Federally Funded	Partner Signature: (Signature)	prop	(Print or Type) BUSINESS ADDRESS: (Print or Type) (Affex Foirt Venture Secretary Signature) (Affex Foirt Venture Secretary Signature) (Affex Foirt Venture Secretary Signature)
Terminal 3 Improvements Bid Package No.: 1.4	Secretary of(Corporation Name). (Scal) Notary Public Signature Commission Expires:	Instructions and Execution Documents Bid Puckage No.: 1,4	Signature: (Signature) Address: (Print or Type)
	CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4 85-2		CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Biol Package No.: 1.4 SS-4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. □ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. Appropriate Proposal Page completed, signed, and notarized; S5-1 - S5-5. Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed:



PROCUREMENT – ADDENDA (if any) ACKNOWLEDGED ON PROPOSAL EXECUTION FORM

FILL IN THE BLANK ON YOUR APPLICABLE PROPOSAL EXECUTION FORM (S5-1 – S5-5)



The undersigned hereby acknowledges having received **Bid Package No.** 1.4 containing a full set of Contract Documents, including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Conditions, 4) Contract Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Criteria and Submittal Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (none unless indicated here)

and affirms that the Joint Venture shall be bound by all the terms and conditions contained in the Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except only to the extent that the Joint Venture has taken express written exception thereto in the sections of this specification designated for that purpose.

SECTION 5 PROPOSAL TO BE EXECUTED BY A CORPORATION		PROPOS	AL TO BE EXECUTED BY A SOLE PROPRIETOR		
The undersigned hereby acknowledges having received Bid Package No. 1.4 containing a full set of C including, but not limited to, 1) Instructions to Bidders (Proposers), 2) General Conditions, 3) Special Core	entract Documents,	including, but not limited to, 1) last	ges having received Bid Package No. 1.4 containing a full set of Contra- ructions to Bidders (Proposers), 2) General Conditions, 3) Special Condit Detailed Specifications or Scope of Services, Evaluation/Selection Crites	tions, 4) Contract	
Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Services, Evaluation/Selection Cr Requirements (If RFP/RFO). 6) Proposal Pages, 7) Certifications and 8) Addenda Nos. (some unle	ggis and Submitted	Department of DEP DECK - C. Per	vial Pages, 7) Certifications and 8) Addenda Nos. (none unless indicate sole preprietor shall be bound by all the terms and conditions or	d boom	
and affirms that the corporation shall be bound by all the terms and condition Contract Documents, regardless of whether a complete set thereof is attached to this proposal, except on the corporation has taken express written exception thereto in the sections of this specification designated	The undersigned hereby acknowledges having received Bid Package No. 1.4 including, but not limited to. 1) Instructions to Bidders (Procosers). 2) General	containing a full set of Contract Documents, Conditions, 3) Special Conditions, 4) Contract	ther a complete set thereof is attached to this proposal, except only ritten exception thereto in the sections of this specification designat		PROPOSAL TO BE EXECUTED BY A JOINT VENTURE
Under penalty of perjury, the undersigned: (1) warrants that he/she was authorized to submit an ED	Plans or Drawings (if applicable) 5) Detailed Specifications or Scope of Service Requirements (If RFP/RFQ), 6) Proposal Pages, 7) Certifications and 8) /	(ddenda Nos. (none unless indicated here)	ted: (1) warrants that he/she was authorized to submit an EDS on b hat all certifications and statements contained in the EDS are true,	including, but not limits	y acknowledges having received Bid Package No. 14 containing a full set of Contract Document do., 1) Instruction to Bidders (Proposens), 2) General Conditions, 3) Special Conditions, 4) Contra- phylicable) 5) Detailed Specifications or Scope of Services, Evaluation-Selection Criteria and Submitt
Disclosing Party on-line; (2) warrants that all certifications and statements contained in the EDS are complete as of the date the EDS was submitted con-line; and (3) further warrants that, as of the date of proposal or bid, there have been no changes in Circumstances since the date that the EDS was submitted	Contract Documents, regardless of whether a complete set thereof is attached	to this proposal, except only to the extent that	bmitted on-line; and (3) further warrants that, as of the date of subt neges in Circumstances since the date that the EDS was submitted the parate or incomplete.	Requirements (If RFP	REQ), 6) Proposal Pages, 7) Certifications and 8) Addends Nos. (none unless indicated here and affirms that the Joint Venture shall be bound by all the terms and conditions contained in the
any certification in the EDS false, inaccurate or incomplete.	Under penalty of periury, the undersigned: (1) warrants that he/she was au	thorized to submit an EDS on behalf of the	orn deposes and says on eath that no disclosures of ownership into	Contract Documents, re the Joint Venture has ta	quadiess of whether a complete set thereof is attached to this proposal, except only to the extent the ten express written exception thereto in the sections of this specification designated for that purpose
Further, the undersigned being duly sworn deposes and says on oath that no disclosures of ownership withheld and the information provided therein to the best of its knowledge is current and the undersigned any agreement with any other bidder (proposer) or prospective bidder (proposer) or with any oft	Disclosing Party on-line; (2) warrants that all certifications and statements complete as of the date the EDS was submitted on-line; and (5) father warr proposal or bid, there have been no changes in Circumstances since the date to	ants that, as of the date of submission of this	therein to the best of its knowledge is current and the undersigned eoposer) or prospective bidder (proposer) or with any other person, in this proposal or any other proposal, nor any agreement or arrang	Disclosing Party on-lin	ry, the undersigned: (1) warrants that he/she was authorized to submit an EDS on behalf of th sc; (2) warrants that all certifications and statements contained in the EDS are true, accurate an
corporation relating to the price named in this proposal or any other proposal, nor any agreement or arrang any act or omission in restraining of free competition among bidders (proposers) and has not disclosed to	any certification in the EDS false, inaccurate or incomplete.		ee competition among bidders (proposers) and has not disclosed to sal) or the price named herein.	proposal or bid, there h	r the EDS was submitted on-line; and (3) further warrants that, as of the date of submission of the ave been no changes in Circumstances since the date that the EDS was submitted that would rend- EDS false: inaccurate or incomplete.
corporation the terms of this bid (proposal) or the price named herein. Proposals must be submitted with original signatures in the space provided. Proposals not properly signed	Further, the undersigned being duly sworn deposes and says on oath that no withheld and the information provided therein to the best of its knowledge is co- arry agreement with any other bidder (reconser) or prospective bidder (re	arrent and the undersigned has not entered into	nal signatures in the space provided. Proposals not properly signer	Further, the undersigne	d being duly sworn deposes and says on oath that no disclosures of ownership interests have be
NAME OF CORPORATION:	any agreement with any other budger (prospectry) or prospective budger (procedure relating to the price named in this proposal or any other proposal, n any act or omission in restraining of free competition among budders (proposer	or any agreement or arrangement under which		withheld and the inform any agreement with a	ation provided therein to the best of its knowledge is current and the undersigned has not entered in ny other bidder (proposer) or prospective bidder (proposer) or with any other person, firm
SIGNATURE OF PRESIDENT*: (Or Authorized Officer)	corporation the terms of this bid (proposal) or the price named herein.		(Signature)	any act or omission in r	he price named in this proposal or any other proposal, nor any agreement or arrangement under whi- cutraining of free composition among bidden (proposers) and has not disclosed to any person, firm (his bid (proposal) or the price named herein.
TITLE OF SIGNATORY: (Signature)	Proposals must be submitted with original signatures in the space provided. Pro BUSINESS NAME: (Print or Type)	oposals not properly signed will be rejected.	(Print or Type)	· ·	itted with original signatures in the space provided. Proposals not properly signed will be rejected.
(Print or Type)	BUSINESS ADDRESS			JOINT VENTURE N	ME:
BUSINESS ADDRESS: (Print or Type) *Note: In the event that this bid (proposal) is signed by other than the President, attach hereto a ce	(Print or Type) If you are operating under an assumed name, provide County registration na	mber herein under as provided in the Illinois	(Print or Type) assumed name, provide County registration number herein under as a 1965 Chapter 96 Sec. 4 et seq.	JOINT VENTURE AT	(Print or Type)
that section of Corporate By-Laws or other authorization, such as a resolution by the Board of Di permits the person to sign the offer for the Corporation.	Revised Statutes 1965 Chapter 96 Sec. 4 et seq. Revistration Number				(Print or Type)
ATTEST: (Corporate Secretary Signature) (Affix Compente Seal)	SIGNATURES AND ADDRESSES OF ALL MEMBERS OF THE PARTNEF (If all General Partners do not sign, indicate authority of partner signatories by	ISHIP by attaching copy of partnership agreement or	(Print or Type)	If you are oper in the Illinois I Registration N	ating under an assumed name, provide County registration number herein under as provided tevised Statutes 1965 Chapter 96 Sec. 4 et seq.
State of	other authorizing document): Partner Signature: (Signature)			SIGNATURE: (If all member	S AND ADDRESSES OF ALL MEMBERS OF THE JOINT VENTURE s of the Joint Venture do not sign, indicate authority of signatories by attaching copy of Joint
County of	(Signature) Address: (Print or Type)		adged before me on thisday of, 20by as President (or other authorized officer) and	Venture agrees	ment or other authorizing document):
This instrument was acknowledged before me on thisday of, 20 by as President (or other authorized officer) and	Partner Signature: (Signature)		(Corporation Name).	SIGNATURE Authorized Pa	
Secretary of (Corporation Name).	Address: (Print or Type) Partner Signature:			TITLE OF SIC	(Print or Type)
(Scal) Notary Public Signature	(Signature) Address:		prop	BUSINESS AI	DDRESS: (Print or Tyne)
Commission Expires:	State of			ATTEST:	(Joint Venture Secretary Signature)
		day of, 20 by		OR	(Affix Joint Venture Scal)
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4	s as President (or other authorized office Secretary of (Corporation Name).	r) and as	Instructions and Execution Documents	Joint Venturer Signature:	(Signature)
	(Seal) Notary Public Signature		Bid Package No.: 1.4	Address:	(Print or Type)
	Commission Expires:				
	CMAR Federally Funded Instructions and Execution Documents			CMAR Federally Funded	Instructions and Execution Documents

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submissi through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. DBE Utilization Report; S5-36.



PROCUREMENT – SCHEDULE B: AFFIDAVIT OF DBE/NON-DBE JOINT VENTURE

Complete and return with your bid.

Include as an attachment on Building Connected.

SCHEDULE B: Affidavit of DBE/Non-DBE Joint Venture (FTA, FHWA and FAA Funded Contracts)

Note: If all joint venturers are DBEs, a written joint venture agreement between the DBE venturers may be submitted in lieu of this form. In all proposed joint ventures, each DBE venturer must submit a copy of its current Letter of Certification.

ALL INFORMATION REQUESTED BY THIS SCHEDULE MUST BE ANSWERED IN THE SPACES PROVIDED. DO NOT REFER TO YOUR JOINT VENTURE AGREEMENT EXCEPT TO EXPAND ON ANSWERS PROVIDED ON THIS FORM. IF ADDITIONAL SPACE IS REQUIRED ADDITIONAL SHEETS MAY BE ATTACHED.

I.	Name of joint vent	ure:	
	Address of joint ve	nture:	
	Phone number of jo	oint venture:	
II.	Identify each non-I	DBE venturer(s):	
	Name of Firm:		
	Address:		
	Phone:		
	Contact person for	matters concerning DBE compliance:	
III.	Identify each non-I	DBE venturer(s):	
	Name of Firm:		
	Address:		
	Phone:		
	Contact person for	matters concerning DBE compliance:	
IV.	Describe the role(s)) of the DBE venturer(s) in the joint venture:	
V.	management respondetails related to: (work items to be p	he joint venture agreement. In order to demonstrate the DBE v nsibilities, risks and profits of the joint venture, the proposed join (1) the contributions of capital and equipment; (2) work items to be erformed under the supervision of the DBE venturer; and (4) the mnel employed by the DBE to be dedicated to the performance of the	at venture agreement must include specific be performed by the DBE's own forces; (3) commitment of management, supervisory
			and projects.
VI.	Ownership of the Jo A. What are the	oint Venture. percentage(s) of DBE ownership of the joint venture?	
		ership percentage(s)	
	Non-DBE	ownership percentage(s)	
	B. Specify DBI	E percentages for each of the following (provide narrative descripti	ions and other details as annlicable).
		nd loss sharing:	iono and outer details as approasso).
		contributions:	
		Dollar amounts of initial contribution:	
	(b)	Dollar amounts of anticipated on-going contributions:	
CMA	R Federally Funded	Instructions and Execution Documents	
	inal 3 Improvements	Bid Package No.: 1.1	\$5-25

PROCUREMENT – SCHEDULE C: DBE LETTER OF INTENT TO PERFORM AS A SUBCONTRACTOR OR SUPPLIER

Complete and return with your bid.

	so	CHEDULE C	
		Letter of Intent to	
	Perform as a	Subcontractor or Supplie	<u>er</u>
Project Name:		Bid Package No.:	
From:			
	(Name of DBE Firm)		
To:	(Name of Prime Contractor)		and the City of Chicago.
The DBE status of the und Certification Letter.	dersigned is confirmed by	the attached City of Chicago or	Illinois Uniform Certification Progra
			the above named project/contract payment schedule, attach addition
		ollowing price and described terr	
Pay Item No	./Description	Quantity/Unit Price	<u>Total</u>
Partial Pay Items		Gra	and Total: \$
Partial Pay Items For any of the above items	s that are partial pay items :		and Total: \$ and subcontract dollar amount(s):
	s that are partial pay items		
	s that are partial pay items :	specifically describe the work an	nd subcontract dollar amount(s):
For any of the above items SUB-SUBCONTRACTING A zero (0) must be shown	G LEVELS	specifically describe the work an	
For any of the above items SUB-SUBCONTRACTING A zero (0) must be shown schedule.	S LEVELS in each blank if the DBE wi	specifically describe the work an	and subcontract dollar amount(s): and Total: \$
SUB-SUBCONTRACTING A zero (0) must be shown schedule. % of the dollar v % of the dollar v	6 LEVELS in each blank if the DBE wi value of the DBE subcontra value of the DBE subcontra	Gra ill not be subcontracted to 1 ct that will be subcontracted to 1 ct that will be subcontracted to 1	and subcontract dollar amount(s): and Total: \$
SUB-SUBCONTRACTING A zero (0) must be shown schedule. % of the dollar v % of the dollar v NOTICE: If any of the DB explanation, description	G LEVELS in each blank if the DBE will walue of the DBE subcontral value of the DBE subcontral E scope of work will be sand pay item number of into a formal written agree	Gra ill not be subcontracting any of the that will be subcontracted to rect that will be subcontracted to rect that will be subcontracted, list the name of the work that will be subcontracted, rect the that will be subcontracted, and the work that will be subcontracted, because of the work that will be subcontracted.	and subcontract dollar amount(s): and Total: \$
SUB-SUBCONTRACTING A zero (0) must be shown schedule. % of the dollar v % of the dollar v NOTICE: If any of the DB explanation, description The undersigned will enter upon your execution of a cithe CMAR.	GLEVELS in each blank if the DBE will also the DBE subcontrate value of the DBE subcontrate. So the DBE subcontrate so the DBE subcontrate of the DBE will be subcontrate of the DBE subcont	Gra ill not be subcontracting any of the that will be subcontracted to rect that will be subcontracted to rect that will be subcontracted, list the name of the work that will be subcontracted, rect the that will be subcontracted, and the work that will be subcontracted, because of the work that will be subcontracted.	and subcontract dollar amount(s): and Total: \$
SUB-SUBCONTRACTING A zero (0) must be shown schedule. % of the dollar v % of the dollar v NOTICE: If any of the DB explanation, description The undersigned will enter upon your execution of a c the CMAR. NOTICE: THIS SCHEDUL	GLEVELS in each blank if the DBE will also the DBE subcontrate value of the DBE subcontrate. So the DBE subcontrate so the DBE subcontrate of the DBE will be subcontrate of the DBE subcont	Gra ill not be subcontracting any of the subcontracted to rect that will be subcontracted to rect that will be subcontracted to rect that will be subcontracted to resubcontracted, list the name the work that will be subcontrament for the above work with you thin three (3) business days of your REQUIRE ORIGINAL SIGNATU	and subcontract dollar amount(s): and Total: \$
SUB-SUBCONTRACTING A zero (0) must be shown schedule. % of the dollar v % of the dollar v NOTICE: If any of the DB explanation, description The undersigned will enter upon your execution of a c the CMAR. NOTICE: THIS SCHEDUL	6 LEVELS in each blank if the DBE will also the DBE subcontral value of the DBE will be subcontract with the CMAR, with the CMAR, with the CMAR value.	Gra ill not be subcontracting any of the subcontracted to rect that will be subcontracted to rect that will be subcontracted to rect that will be subcontracted to resubcontracted, list the name the work that will be subcontrament for the above work with you thin three (3) business days of your REQUIRE ORIGINAL SIGNATU	and subcontract dollar amount(s): and Total: \$
SUB-SUBCONTRACTING A zero (0) must be shown schedule. % of the dollar v % of the dollar v NOTICE: If any of the DB explanation, description The undersigned will enter upon your execution of a c the CMAR. NOTICE: THIS SCHEDUL (Signature of President/Owne	6 LEVELS in each blank if the DBE will also the DBE subcontral value of the DBE will be subcontract with the CMAR, with the CMAR, with the CMAR value.	Gra ill not be subcontracting any of the subcontracted to rect that will be subcontracted to rect that will be subcontracted to rect that will be subcontracted to resubcontracted, list the name the work that will be subcontrament for the above work with you thin three (3) business days of your REQUIRE ORIGINAL SIGNATU	and subcontract dollar amount(s): and Total: \$

PROCUREMENT – SCHEDULE D: AFFIDAVIT OF PRIME CONTRACTOR REGARDING DISADVANTAGED BUSINESS ENTERPRISE (DBEs)

Complete and return with your bid.

DPS Version 04/25/2017		
	SCHEDULE D Affidavit of Prime Contractor g Disadvantaged Business Enterprises (DBEs) FTA/FHWA and FAA Funded Projects)	
Project Name:		
Department Project No.:		
Bid Package No.:		
State of	:SS	
County (City) of)	D AFFIRM det I en d
	captioned contract, I HEREBY DECLARE AN and duly authorized representative of	D AFFIRM that I am th
(Title of Affiant)		
	Name of Prime Contractor)	
and that I have personally reviewed the mate Business Enterprises (DBE), Schedule Cs and	rial and facts set forth in and submitted with the attac Schedule Bs (if applicable), being such information.	hed Schedules of Disadvantage
Names of DBE Firms	Type of Work to be Performed (in accordance with Schedule Cs)	Credit Toward DBE Goal
		s
		s s
		-
		s
		s s
		S S S
		s s s
		s s s s
		s s s s
		s s s s
		\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$
		\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$
		\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$
	Total DBE	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$
	Total DBE	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$

PROCUREMENT – SCHEDULE F: REPORT OF SUBCONTRACTOR SOLICITATIONS

Complete and return with your bid.

	E F: Report of Subcontractor Solicitations
(FHWA, FTA and FAA Funded Contracts)
	Project Name: Specification #:
_	Specification #:
[,(Name of reporter)	on behalf of(Prime contractor)
have either personally solicited, or p	ermitted a duly authorized representative of this firm to solicit, work for ctors which comprise all DBE and non-DBE subcontractors who bid or que
Name of Subcontractor	
Address of Subcontractor	
	□Yes □ No
Type of Work Solicited	
Years in Business (if available)	
Name of Subcontractor	
Address of Subcontractor	
Contact Person	
	□Yes □ No
Type of Work Solicited	
Years in Business (if available)	
Years in Business (if available) Annual Gross Receipts (if available)	
Name of Subcontractor	
Name of SubcontractorAddress of Subcontractor	
Name of Subcontractor	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified?	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available)	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified?	□Yes □ No
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Annual Gross Receipts (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Contact Person	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Contact Person	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Name of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified?	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	
Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available) Annual Gross Receipts (if available) Name of Subcontractor Address of Subcontractor Contact Person Status: DBE Certified? Type of Work Solicited Years in Business (if available)	

PROCUREMENT – EXHIBIT A DBE REQUIREMENT FOR BIDDER/PROPOSER LIST

Complete and return with your bid.

Include as an attachment on Building Connected.

	ersion 04/25/2017	EXHIBIT A
	DBE R	EQUIREMENT FOR BIDDER/PROPOSER LIST
bidd requ on th	ing or proposing on print ested to provide a list of his contract. Failure to co	The CMAR is required to maintain a bidders list, consisting of all me contracts and bidding or quoting subcontracts. The bidder/proposall DBE AND non-DBE subcontractors who bid or quote price inform properate may result in the bidder/proposer being deemed non-responsive roposer is requested to provide the following information:
Prim	ne Contractor (Including	all partners to a Joint Venture, if applicable)
	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	
Subo	contractors (all DBE ANI	D non-DBE subcontractors)
1.	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	Goods or Services:	
2.	Name:	
	Address:	
	Address:	
	City, State, Zip:	
	City, State, Zip.	

Instructions and Execution Documents

\$5-41

CMAR Federally Funded

PROCUREMENT – DBE UTILIZATION REPORT

Complete and return with your bid.

		DBE Utilization R	enort	
NOTICE:	AWARDED A CONTRAC BE REQUIRED TO SUBM	T TO BE COMPLETED AT T T WITH AN APPROVED DBE IIT THIS REPORT IN ACCORDA DITION REGARDING DISADV	HE TIME OF BID OR I /MBE/WBE PLAN, THE NCE WITH THE REPORT	PRIME CONTRACTOR WILI ING REQUIREMENTS STATES
Contract Adm	inistrator:		Bid Package No.	
Phone No			Purchase Order No.	
			Date of Award:	
STATE OF:	(Utilization Report N	o
COUNTY (CI	TY) OF: ()		
In connection	with the above-captioned	contract:		
I HEREBY DI	ECLARE AND AFFIRM	that I am the		
	orized representative of		(Title - Print or Type)	
and that the fo	(Address of Co ollowing Disadvantaged, ire furnishing and prepari	mpany) Minority and Women Busine ng materials for, and rendering	ess Enterprises have bee g services stated in the co	(Phone) en contracted with, and have ontract agreement.
and that the fo furnished, or a The following paid to each to	(Address of Co bllowing Disadvantaged, re furnishing and preparir Schedule accurately refle date.	mpany) Minority and Women Busine	ess Enterprises have bee	(Phone) en contracted with, and have ontract agreement.
and that the fo furnished, or a The following paid to each to	(Address of Co ollowing Disadvantaged, are furnishing and preparing Schedule accurately refle	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M	ess Enterprises have bee services stated in the co (BE/WBE sub-agreemen) (Phone) n contracted with, and have outract agreement. It and the amounts of money
and that the fo furnished, or a The following paid to each to	(Address of Co bllowing Disadvantaged, re furnishing and preparir Schedule accurately refle date.	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee g services stated in the co IBE/WBE sub-agreemen	(Phone) n contracted with, and have ontract agreement. it and the amounts of money Amount Paid
and that the fo furnished, or a The following paid to each to	(Address of Co bllowing Disadvantaged, re furnishing and preparir Schedule accurately refle date.	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee g services stated in the co (BE/WBE sub-agreemen Amount of Contract	(Phone) In contracted with, and have ontract agreement. It and the amounts of money Amount Paid To-Date
and that the fo furnished, or a The following paid to each to	(Address of Co bllowing Disadvantaged, re furnishing and preparir Schedule accurately refle date.	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee g services stated in the co (BE/WBE sub-agreemen Amount of Contract	(Phone) In contracted with, and have ontract agreement. It and the amounts of money Amount Paid To-Date
and that the fo furnished, or a The following paid to each to	(Address of Co bllowing Disadvantaged, re furnishing and preparir Schedule accurately refle date.	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee g services stated in the co (BE/WBE sub-agreemen Amount of Contract	(Phone) In contracted with, and have ontract agreement. It and the amounts of money Amount Paid To-Date
and that the fo furnished, or a The following paid to each to	(Address of Co bllowing Disadvantaged, re furnishing and preparir Schedule accurately refle date.	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee g services stated in the co (BE/WBE sub-agreemen Amount of Contract	(Phone) In contracted with, and have ontract agreement. It and the amounts of money Amount Paid To-Date
and that the fo furnished, or a The following paid to each to DBE/MB	(Address of Co bllowing Disadvantaged, re furnishing and preparii Schedule accurately reflicate. E/WBE Firm Name	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm	ess Enterprises have bee s services stated in the or IBE/WBE sub-agreemen Amount of Contract S	(Phone) In contracted with, and have outract agreement. It and the amounts of money Amount Paid To-Date \$
and that the for furnished, or a The following paid to each to DBE/MB	(Address of Co bllowing Disadvantaged, re furnishing and preparii Schedule accurately reflicate. E/WBE Firm Name	mpany) Minority and Women Busine ag materials for, and rendering ects the value of each DBE/M Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the or BE/WBE sub-agreemen Amount of Contract S	n contracted with, and have outract agreement. It and the amounts of money Amount Paid To-Date S
and that the for furnished, or a The following paid to each to DBE/MB	(Address of Co billowing Disadvantaged, re furnishing and preparir Schedule accurately reflected date. E/WBE Firm Name	Indicate Type of Firm (DBE/MBE/WBE)	ess Enterprises have bee g services stated in the or BE/WBE sub-agreemen Amount of Contract S	n contracted with, and have outract agreement. It and the amounts of money Amount Paid To-Date S

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. CMAR Federally Funder Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit Schedule 6 – Contractors Payment and Performance Bond Schedule 7 - Certification of Compliance with FAA Buy American Preference - Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions



PROCUREMENT – SCHEDULE 1 AFFIDAVIT OF NON-COLLUSION

Complete and return with your bid.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175
Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)
SCHEDULE 1 AFFIDAVIT OF NON-COLLUSION
STATE OF ILLINOIS } SS COUNTY OF COOK }
, being first duly sworn, deposes and says that:
(1) He/She is
(Owner, Partner, Authorized Officer, or Representative or Agent)
(Name of Organization/Firm)
the Bidder that has submitted the attached Bid;
(2) That Bidder is fully informed respecting the preparation and contents of the attached Bid and of all pertinent circumstances respecting such Bid; (3) Such Bid is genuine and is not a collusive or sham bid; (4) Neither Bidder nor any of its officers, partners, owners, agents, representatives, employees, or parties in interest, including this affiant, has in any way colluded, connived, conspired, or agreed, directly or indirectly, with any other Bidder, firm, or person to submit a collusive or sham bid in connection with the Contract for which the attached bid has been submitted or to refrain from bidding in connection with such Contract, or has in any manner, directly or indirectly, sought by agreement or collusion or communication or conference with any other Bidder, firm, or person to fix the price or prices in the attached bid or in that of any other Bidder, or to fix any overhead, profit, or cost element of the bid price of any other Bidder, or to secure through any collusion, conspiracy, connivance or unlawful agreement any advantage against the City of Chicago or any person interested in the proposed Contract; and (5) The price or prices quoted in the attached Bid are fair and proper and are not tainted by any collusion, conspiracy, connivance, or unlawful agreement on the part of the Bidder or any of its agents, representatives, owners, employees, or parties in interest, including this affiant. (6) The Bidder is not barred from bidding as a result of having violated Illinois Criminal Code, 720 ILCS 5/33E-3 (Bid-rigging), 720 ILCS 5/33E-4 (Bid rotating) or the Prevailing Wage Act, 30 ILCS 570/0.01 through 570/7.
(Signed)
(Title)
Exhibit D to the Agreement Required Subcontract Provisions

PROCUREMENT – SCHEDULE 2 regulations of the department of procurement services for percentages of City and Project Area Residents working hours

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

REGULATIONS OF THE DEPARTMENT OF PROCUREMENT SERVICES FOR PERCENTAGES OF CITY AND PROJECT AREA RESIDENTS WORKING HOURS

GENERAL PROVISIONS

1. Statement of Authority

These regulations are issued pursuant to the following Section of the Municipal Code

Section 2-92-330 of Municipal Code of Chicago establishes a minimum number of hours to be performed by City Residents as well as a minimum number of hours to be performed by Project Area residents. Subsection (a) requires the Chief Procurement Officer to "develop standards and procedures for reducing or waiving these minimum percentages level of Chicagoans work hours for eligible residents when a bidder or contractor can demonstrate the impracticality or excessive cost of complying with these percentage levels for particular contracts or classes of employees." Subsection (f) authorizes the Chief Procurement Officer to "adopt, promulgate and enforce reasonable rules and regulations pertaining to the administration and enforcement" of

Subsection (a) provides that, for any construction project advertised, or if not advertised, awarded, by the City that has an estimated contract value of \$100,000 or more, and where not otherwise prohibited by federal, state or local law, the total hours worked by persons on the site of the construction project by employees of the contractor and subcontractors shall be performed (i) at least 50 percent by City Residents; and (ii) at least 7.5 percent by Project Area residents. Work hours performed by Project Area residents shall be considered to be work hours performed by City Residents for purposes of calculating the minimum work hour percentage required to be performed by City Residents.

2. Application and Statement of Purpose

These regulations describe how the ordinance will be administered and enforced, including the right of the Chief Procurement Officer to waive the residency

DEFINITIONS

Unless otherwise specified, whenever used in these regulations, the following terms have the following meanings:

"City Residents" means persons domiciled within the City of Chicago.

Exhibit D to the Agreement Required Subcontract Provisions D-30 | Page

PROCUREMENT – SCHEDULE 4 STATEMENT OF BIDDER'S QUALIFICATIONS

Complete and return with your bid.

SCHEDULE 4 STATEMENT OF BIDDER'S QUALIFICATIONS At the request of the City, the Bidder shall also submit additional information regarding the capability of the Bidder to perform the Contract. Bidder: Submitted By: Title: Permanent Main Office Address: Local Address: Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract			Construction Management		Hare 21 at O'Hare International Airport of Aviation (Specification No.1258275
capability of the Bidder to perform the Contract. Bidder: Submitted By: Title: Permanent Main Office Address: Local Address: Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract Nature of Project	-		e's QUALIFICATIONS		
Submitted By: Title: Permanent Main Office Address: Local Address: Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract Nature of Project				dditional infor	nation regarding the
Title: Permanent Main Office Address: Local Address: Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract Nature of Project	В	idder:			
Permanent Main Office Address: Local Address: Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract	Sı	ubmitted By:			
Local Address: Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract Nature of Project	T	itle:			
Local Telephone No. and Fax Number: How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract	P	ermanent Main Office Add	ress:		
How many years operating as Trade Contractor for work of this nature? List of recently completed contracts of similar dollar value and scope of work: Name/Address Dollar Amount Year of Contract	L	ocal Address:			
Name/Address Dollar Amount Contract Nature of Project 1. 2. 3. 4. 5. 6. 7. 8.	_	ow many years operating as	Trade Contractor for work		
2. 3. 4. 5. 6. 7. 8. The undersigned hereby authorizes any person, firm, or corporation to furnish any information requested by the City of Chicago in verification of this Statement of Bidder's Qualifications. If submitted by a corporation: (a) Corporation Name:	_	ow many years operating as	Trade Contractor for work	lue and scope o	f work:
4. 5. 6. 7. 8. The undersigned hereby authorizes any person, firm, or corporation to furnish any information requested by the City of Chicago in verification of this Statement of Bidder's Qualifications. If submitted by a corporation: (a) Corporation Name:	Lis	ow many years operating as	Trade Contractor for work	lue and scope o	f work:
6.	Lis	ow many years operating as	Trade Contractor for work	lue and scope o	f work:
8. The undersigned hereby authorizes any person, firm, or corporation to furnish any information requested by the City of Chicago in verification of this Statement of Bidder's Qualifications. If submitted by a corporation: (a) Corporation Name:	1. 2. 3. 4.	ow many years operating as	Trade Contractor for work	lue and scope o	f work:
The undersigned hereby authorizes any person, firm, or corporation to furnish any information requested by the City of Chicago in verification of this Statement of Bidder's Qualifications. If submitted by a corporation: (a) Corporation Name:	1. 2. 3. 4.	ow many years operating as	Trade Contractor for work	lue and scope o	f work:
requested by the City of Chicago in verification of this Statement of Bidder's Qualifications. If submitted by a corporation: (a) Corporation Name:	1. 2. 3. 4. 5. 6.	ow many years operating as	Trade Contractor for work	lue and scope o	f work:
(a) Corporation Name:	1. 2. 3. 4. 5. 6. 7. 8.	st of recently completed con Name/Address	Trade Contractor for work	Year of Contract	f work: Nature of Project
	1. 2. 3. 4. 5. 6. 7. 8.	st of recently completed con Name/Address e undersigned hereby author	Trade Contractor for work ntracts of similar dollar val Dollar Amount prizes any person, firm, or	Year of Contract	Nature of Project Furnish any information
(b) State and City in which incorporated:	1. 2. 3. 4. 5. 6. 7. 8. The required	w many years operating as st of recently completed cor Name/Address e undersigned hereby authouested by the City of Chica	Dollar Amount Dollar Amount prizes any person, firm, or ago in verification of this S	Year of Contract	Nature of Project Furnish any information

PROCUREMENT – SCHEDULE 5 CERTIFICATE OF FILING ON-LINE ECONOMIC DISCLOSURE (EDS) STATEMENTS AND AFFIDAVIT

The bidder shall complete an online EDS prior to the bid due date. A bidder who does not file an electronic EDS prior to the bid due date may be found non-responsible and its bid rejected. If you are unable to complete the online EDS and print a Certificate of Filing prior to the bid/proposal due date, the City will accept a paper EDS provided written justification is submitted with the bid/proposal explaining the Bidder's good faith efforts to complete it before the bid/proposal due date and the reasons why on line EDS could not be completed

Hard copy to be submitted with your bid but do NOT need to submit electronically pior to bid. Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 5

INSTRUCTIONS FOR COMPLETING ECONOMIC DISCLOSURE STATEMENT AND AFFIDAVIT (EDS) ON-LINE

The Bidder shall complete an online EDS prior to the bid due date. A Bidder who does not file an electronic EDS prior to the bid due date may be found non-responsive and its bid rejected. If you are unable to complete the online EDS and print a Certificate of Filing prior to the bid/proposal due date, the City will accept a paper EDS provided written justification is submitted with the bid/proposal explaining the Bidder's good faith efforts to complete it before the bid/proposal due date and the reasons why on line EDS could not be completed.

1.1. ONLINE EDS FILING REQUIRED PRIOR TO BID OPENING

The Bidder must complete an online EDS prior to the bid opening date.

A Bidder that does not file an electronic EDS prior to the bid opening will be found nonresponsive and its bid will be rejected, unless a paper EDS and justification is submitted with the bid as described above. Paper EDS forms may be obtained on the City's wesite at: http://www.cityofchicago.org/city/en/depts/dps/provdrs/comp/svcs/economic_disclosurestate mentseds.html

1.2. ONLINE EDS WEB LINK

The web link for the Online EDS is https://webapps.cityofchicago.org/EDSWeb

1.3. ONLINE EDS NUMBER

Upon completion of the online EDS submission process, the Proposer will be provided an EDS number. Bidders should provide this number here:

EDS Number:

1.4. ONLINE EDS CERTIFICATION OF FILING

Upon completion of the online submission process, the Proposer will be able to print a hard copy Certificate of Filing. The Proposer should submit the signed Certificate of Filing with its bid. Please insert your Certification of Filing following this page.

A Proposer that does not include a signed Certificate of Filing with its bid must provide it upon the request of the Chief Procurement Officer.

1.5. PREPARATION CHECKLIST FOR REGISTRATION

To expedite and ease your registration process, we recommend that you collect the following information prior to registering for an Online EDS user account:

Exhibit D to the Agreement Required Subcontract Provisions D-38 | Page

PROCUREMENT – SCHEDULE 6 CONTRACTOR'S PERFORMANCE & PAYMENT BOND RIDER ATTACHED

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 6 CONTRACTOR'S PERFORMANCE AND PAYMENT BOND RIDER ATTACHED

CONTRACTOR'S PERFORMANCE & PAYMENT BOND

Know All Men by these Presents, That we,

COMPANY NAME STREET ADDRESS CITY, STATE ZIP CODE

Principal, hereinafter referred to as Contractor, and of the County of and State of , are held and firmly bound unto the CITY OF CHICAGO in the penal sum of:

--- Dollar Amount in Words and 00/100 Dollars (\$) ---

lawful money of the United States, for the payment of which sum of money, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

Sealed with our seals and dated this

day of

, 20 .

The Condition of the Above Obligation is such, that whereas the above bounden Contractor has entered into a certain contract with the City of Chicago, bearing

Contract (PO) No. XXXXX and Specification No. XXXXXX all in conformity with said contract, for,

Furnishing the City of Chicago, Name of User Department, all labor, tools, material, and equipment required and necessary for the project known as:

PROJECT DESCRIPTION

* The attached rider is incorporated herein by reference.

Now, if the said Contractor shall in all respects well and truly keep and perform the said contract on its part, in accordance with the terms and provisions of all of the Contract Documents comprising said contract, and in the time and manner therein prescribed, and further shall save, indemnify, and keep harmless the City of Chicago against all loss, damages, claims, liabilities, judgments, costs and expenses which may in anywise accrue against said City of Chicago, in consequence of the granting of said contract, or which may in anywise result therefrom, or which may result from strict liability, or which may in anywise result therefrom, or which may result from strict liability, or which may in anywise result from any injuries to, or death of, any person, or damage to any real or personal property, arising directly or indirectly from or in connection with, work performed or to be performed under said contract by said Contractor, its Agents, Employees or Workmen, assignees, subcontractors, or anyone else, in any respect whatever, or which may result on account of any infringement of any patent by reason of the materials, machinery, devices or apparatus used in the performance of said contract, and moreover, shall pay to said City any sum or sums of money determined by the Purchasing Agent, and/or by a court of competent jurisdiction, to be due said City by reason of any failure or neglect in the performance of the requirements of said contract, wherefore the said Purchasing Agent shall have elected to suspend or cancel the same, and shall pay all claims and demands whatsoever, which may accrue to each and every materialman and subcontractor, and to each and every person who shall be employed by the said Contract or by its assigness and subcontractors, in or about the performance of said contract, and with wages paid at prevailing wage rates if so required by said contract, and shall insure its liability to pay the compensation, and shall be employed by them

Exhibit D to the Agreement
Required Subcontract Provisions

D-46 | Page

PROCUREMENT – SCHEDULE 7 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE CONSTRUCTION PROJECTS

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 7 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE CONSTRUCTION PROJECTS

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with its proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101, BABA and other related Made in America Laws, U.S. statutes, guidance, and FAA policies, by selecting one of the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (i.e., not both) by inserting a checkmark (*) or the letter "X".

- ☐ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related U.S. statutes, guidance, and policies of the FAA by:
 - a) Only installing iron, steel and manufactured products produced in the United States;
 - b) Only installing construction materials defined as: an article, material, or supply other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials; aggregates such as stone, sand, or gravel; or aggregate binding agents or additives that are or consist primarily of non-ferrous metals; plastic and polymer-based products (including polyvinylchloride, composite building materials, and polymers used in fiber optic cables); glass (including optic glass); lumber or drywall that have been manufactured in the United States.
 - Installing manufactured products for which the Federal Aviation Administration (FAA)
 has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy
 American Waivers Issued listing; or
 - d) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- To provide to the Airport Sponsor or the FAA evidence that documents the source and origin of the iron, steel, and/or manufactured product.
- b) To faithfully comply with providing U.S. domestic products.
- c) To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.
- d) Certify that all construction materials used in the project are manufactured in the U.S.
- ☐ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:
 - a) To the submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the responsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested.

Exhibit D to the Agreement
Required Subcontract Provisions

D-51 | Page

PROCUREMENT – SCHEDULE 8 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – EQUIPMENT/BUILDING PROJECTS

Complete and return with your bid.

Include as an attachment on Building Connected.

SCHEDULE 8 CERTIFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE – EQUIPMENT/BUILDING PROJECTS

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with their proposal. The bidder or offeror must indicate how they intend to comply with 49 USC § 50101, and other Made in America Laws, U.S. statutes, guidance, and FAA policies by selecting one on the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (not both) by inserting a checkmark (\checkmark) or the letter "X".

- □ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related U.S. statutes, guidance, and policies of the FAA by:
 - a) Only installing steel and manufactured products produced in the United States;
 - b) Only installing construction materials defined as: an article, material, or supply other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials; aggregates such as stone, sand, or gravel; or aggregate binding agents or additives that are or consist primarily of non-ferrous metals; plastic and polymer-based products (including polyvinylchloride, composite building materials, and polymers used in fiber optic cables); glass (including optic glass); lumber or drywall that have been manufactured in the United States.
 - Installing manufactured products for which the Federal Aviation Administration (FAA) has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing; or
 - Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- To provide to the Airport Sponsor or FAA evidence that documents the source and origin of the steel and manufactured product.
- To faithfully comply with providing U.S. domestic product.
- To furnish U.S. domestic product for any waiver request that the FAA rejects.
- d) To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.
- □ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for a Type 3 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:
 - a) To submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the responsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested.

Exhibit D to the Agreement Required Subcontract Provisions D-54 | Page

PROCUREMENT – SCHEDULE 9 CERTIFICATION REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

Complete and return with your bid.

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

SCHEDULE 9 CERTIFICATION REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

The applicant must complete the following two certification statements. The applicant must indicate its current status as it relates to tax delinquency and felony conviction by inserting a checkmark (\mathbf{v}') in the space following the applicable response. The applicant agrees that, if awarded a contract resulting from this solicitation, it will incorporate this provision for certification in all lower tier subcontracts.

Certifications

- 1) The applicant represents that it is () is not () a corporation that has any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.
- The applicant represents that it is () is not () is not a corporation that was convicted of a criminal violation under any Federal law within the preceding 24 months.

Note

If an applicant responds in the affirmative to either of the above representations, the applicant is ineligible to receive an award unless the sponsor has received notification from the agency suspension and debarment official (SDO) that the SDO has considered suspension or debarment and determined that further action is not required to protect the Government's interests. The applicant therefore must provide information to the owner about its tax liability or conviction to the Owner, who will then notify the FAA Airports District Office, which will then notify the agency's SDO to facilitate completion of the required considerations before award decisions are

Term Definitions

Felony conviction: Felony conviction means a conviction within the preceding twentyfour (24) months of a felony criminal violation under any Federal law and includes conviction of an offense defined in a section of the U.S. code that specifically classifies the offense as a felony and conviction of an offense that is classified as a felony under 18 U.S.C. 8 3559.

Tax Delinquency: A tax delinquency is any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted, or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.


Exhibit D to the Agreement Required Subcontract Provisions D-57|Pag

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ■ Building Connected Bid Form; properly completed online. □ Document Acknowledgement; ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5. ■ Addenda (if any) acknowledged on the Proposal Page. ☐ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized; S5-31. ☐ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit; S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54.

/	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded)
	This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid. The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected:
	Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



PROCUREMENT – AFFIDAVIT OF UNCOMPLETED WORK



SUBMIT WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED, SIGNED AND NOTARIZED

(BAM, CAM, PAM)			1	1				THE WORK					SUBCONTRACTOR	1.1		l		T	1
AGGREGATE BASE AND FILL								D				_	TYPE OF WORK	+					
FOUNDATION		+			-			RK				_		\perp					
(CAISSON & PILE)								ST.					SUBCONTRACT PRICE						
HIGHWAY								AL					AMOUNT UNCOMPLETED						
STRUCTURES SEWER & DRAIN								RE CAULKING				_		+				1	
STRUCTURES								CAULKING					I, being duly sworn do hereby	declare	that this affida	vit is a true and corr	rect statement relating	to ALL uncomplet	ed contracts
PAINTING								OUS					of the undersigned for Federal,						
n - 1 m - m - m - c - n - m - c -												_	not yet awarded or rejected, and						
PAVEMENT MARKING								P						- 1	01				
SIGNING													Subscribed and sworn to before thisday of	e me	20 Cor	mpany			
LANDSCAPING													My commission expires		Ade	dress			
DEMOLITION													·						
FENCING												_							
					1						\vdash	_		- 1					
														- 1					
								1			- 1			- 1					
								1			- 1		CMAR Federally Funded	- 1	Instruc	tions and Execution Doc	uments		
CMAR Federally Funded	1	structions and Execut	ion Documents					1			- 1		Terminal 3 Improvements	- 1		Bid Package No.: 1.4		S5-45	
Terminal 3 Improvements		Bid Package N				S5-43		1			- 1			- 1					
								1			- 1			- 1					
								J			l								
														- 1					
							CMAR Fede	coller Free deed	Instructions	and Execution Docu	an ente			- 1					
							Terminal 3 Is	mprovements		Package No.: 1.4	ancina.		S5-44						
														- 1					

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online ☐ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



PROCUREMENT – CERTIFICATE REGARDING REMOVAL OF ALL WASTE MATERIALS AND IDENTIFICATION OF ALL LEGAL DUMP SITES

Complete and return with your bid. If this does not apply to your trade, mark as NA.

AND	IDENTIFICATION OF ALL LEGAL DUMP SITES	
Contractor to show here the name	e and location of the ultimate disposal site he/she is proposing to use for the subject project	t:
SPECIFY THE TYPE OF MATE	ERIALS TO BE DISPOSED OF:	
LEGAL NAME OF LANDFILL	/DISPOSAL SITE:	
(The Contractor must provide t manifests, etc.)	to the Commissioner or his/her designated representative with copies of all dump tick	ets,
LOCATION ADDRESS:		
PHONE:		
CONTACT PERSON:		
	be of sufficient capacity as to insure acceptance of the volume of Construction and the period of this Contract. These disposal sites must meet all zoning and other requirement.	
	arement Officer, the Contractor shall submit copies of all contractual agreements, sanit or these disposal site(s) proposed by the Contractor.	ary
(Revised 6/30/2000)		
CMAR Federally Funded Terminal 3 Improvements	Instructions and Execution Documents Bid Package No.: 1.4	5

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submiss through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits Bid Bond: S5-54. Instructions and Execution Documents

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



PROCUREMENT - BIDDER'S FINANCIAL STATEMENT

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a financial statement dated not earlier then the end of said Bidder's last fiscal year period. This will be kept on file by the Construction Manager as a representative statement for a period of one year only. If a Bidder does not have such statement on file, it must submit a copy with its bid. Failure to have a current financial statement on file at the Construction Manager at time of bid opening may be cause for the rejection of the Trade Contractor's Bid

Include as an attachment on Building Connected.

DocuSign Envelope ID: B23A2248-E048-4404-B038-14363B4EA175

Construction Management At-Risk Services for O'Hare 21 at O'Hare International Airport
Chicago Department of Aviation (Specification No.1258275)

ensure that any contract entered into pursuant to this advertisement, disadvantaged business enterprises will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award."

B. Affidavit of Non-Collusion

Each Bidder shall fully execute an affidavit, in the form provided, to the effect that the Bidder has not colluded with any other person, firm, or corporation in regard to any bid submitted. Such affidavit shall be attached to the bid.

C. DBE Commitments

The goal for DBE participation for this Contract is 21% DBE.* Each Bidder shall submit with its Bid Schedule Cs and Schedule D, affidavits and supporting documents describing the extent to which DBE firms will participate in the Contract in accordance with Schedule 3 "Special Conditions Regarding DBE Participation."

D. Affidavit of Uncompleted Work

The Bidder is required to submit a fully executed Affidavit of Uncompleted Work, which declares, among other things, the value and estimated completion date of all uncompleted contracts to be completed with Bidder's own forces and to be subcontracted to others. Such affidavit shall be attached to the bid on the form provided.

E. Bidder's Financial Statement

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a financial statement dated not earlier then the end of said Bidder's last fiscal year period. This will be kept on file by the Construction Manager as a representative statement for a period of one year only. If a Bidder does not have such statement on file, it must submit a copy with its bid. Failure to have a current financial statement on file at the Construction Manager at time of bid opening may be cause for the rejection of the Trade Contractor's Bid.

F. Disclosure Affidavit

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a fully executed Disclosure Affidavit. If a Bidder does not have such statement on file, it must submit a copy with its bid.

G. Statement of Bidder's Qualifications

Each Bidder shall have on file in the office of the Construction Manager at the time of bid opening a fully executed Statement of Bidder's Qualifications or a Qualification Submittal in response to a Request for Qualifications (RFQ). Construction Manager reserves the right to request additional information regarding the capability of the Bidder to perform the Contract.

H. Economic Disclosure Statements (EDS)

Exhibit D to the Agreement Required Subcontract Provisions D-2|Page

^{*} The overall contract goal for is 21% DBE, with a construction sub-goal of20%. In consultation with the City a given trade bid package may have a different DBE goal specific to that bid package, and individual subcontracts may have different DBE goals.

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreement ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits ☐ Bid Bond: \$5-54. Instructions and Execution Documents

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this. Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: Affidavit of Uncompleted Work completed, signed, and notarized; S5-43 Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6. Bidder's Financial Statement. Certifications (FAA) Debarment; S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51



PROCUREMENT – FAA CERTIFICATIONS

CERTIFICATION REGARDING LOBBYING AND INFLUENCING

The Contractor certifies, to the best of his or her knowledge and belief,

to any person for influencing or attempting to influence an officer or en

of Congress, an officer or employee of Congress, or an employee of a N

connection with the awarding of any Federal contract, the making of any

any Federal loan, the entering into of any cooperative agreement, and th

renewal, amendment, or modification of any Federal contract, grant, loa

for influencing or attempting to influence an officer or employee of any

an officer or employee of Congress, or an employee of a Member of Cong

Federal contract, grant, loan, or cooperative agreement, the undersigned

If any funds other than Federal appropriated funds have been pa

No Federal appropriated funds have been paid or will be paid, by

CERTIFICATE REGARDING DEBARMENT AND SUSPENSION

By submitting a bid/proposal under this solicitation, the bidder or offeror certifies that a the bidder or offeror submits its proposal that neither it nor its principals are presently debar suspended by any Federal department or agency from participation in this transaction.

CERTIFICATION REGARDING DEBARMENT AND SUSPENSION (SUCCESSFU REGARDING LOWER TIER PARTICIPANTS)

The successful bidder, by administering each lower tier subcontract that exceeds \$25,000 transaction", must verify each lower tier participant of a "covered transaction" under the presently debarred or otherwise disqualified from participation in this federally assisted prosuccessful bidder will accomplish this by:

- 1. Checking the System for Award Management at website: http://www.sam.gov
- 2. Collecting a certification statement similar to the Certificate Regarding Debarm Suspension (Bidder or Offeror), above.

CERTIFICATION OF NONSEGREGATED FACILITIES

The federally-assisted construction contractor certifies that she or he does not maintain or provide, for his employees, any segregated facilities at any of his establishments and that she or he does not permit his employees to perform their services at any location, under his control, where segregated facilities are maintained. The federally-assisted construction contractor certifies that she or he will not maintain or provide, for his employees, segregated facilities at any of his establishments and that she or he will not permit his employees to perform their services at any location under his control where segregated facilities are maintained. The federally-assisted construction contractor agrees that a breach of this certification is a violation of the Equal Opportunity Clause in this contract.

As used in this certification, the term "segregated facilities" means any waiting rooms, work areas, restrooms, and washrooms, restaurants and other eating areas, time clocks, locker rooms and other storage or dressing areas, parking lots, drinking fountains, recreation or entertainment areas. transportation, and housing facilities provided for employees which are segregated by explicit directives or are, in fact, segregated on the basis of race, color, religion, or national origin because of habit, local custom, or any other reason. The federally-assisted construction contractor agrees that (except where she or he has obtained identical certifications from proposed subcontractors for specific time periods) she or he will obtain identical certifications from proposed subcontractors prior to the award of subcontracts exceeding \$10,000 which are not exempt from the provisions of the Equal Opportunity

IFICATION OF COMPLIANCE WITH FAA BUY AMERICAN PREFERENCE -CONSTRUCTION PROJECTS

responsiveness, the bidder or offeror must complete, sign, date, and submit this certification proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101, related Made in America Laws, U.S. statutes, guidance, and FAA policies, by selecting one of ification statements. These statements are mutually exclusive. Bidder must select one or the oth) by inserting a checkmark (✓) or the letter "X".

r offeror hereby certifies that it will comply with 49 USC § 50101, BABA and other related tutes, guidance, and policies of the FAA by:

Only installing iron, steel and manufactured products produced in the United States;

Only installing construction materials defined as: an article, material, or supply - other than an item of primarily iron or steel; a manufactured product; cement and cementitious materials;

SUBMIT ONE (1) OF EACH FAA CERTIFICATION WITH YOUR BID AS AN ATTACHMENT ON BUILDING CONNECTED

	1		Date	By		regulation bulgait 25.100.
n .	Business Name			Name and Title of Authorized Representati	ve	ting this certification statement, the bidder or offeror agrees:
ByName and Title of Authorized Representative	Date	ByName and Title		Signature of Authorized Representative		To provide to the Airport Sponsor or the FAA evidence that documents the source and origin of the iron, steel, and/or manufactured product. To faithfully comply with providing U.S. domestic products. To refrain from seeking a waiver request after establishment of the contract, unless extensating streumstances emerge that the FAA determines justified. Certify that all construction materials used in the project are manufactured in the U.S.
Signature of Authorized Representative						der or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences SC § 50101(a) but may qualify for a Type 3 or Type 4 waiver under 49 USC § 50101(b). By g this certification statement, the apparent bidder or offeror with the apparent low bid agrees: To the submit to the Airport Sponsor or FAA within 15 calendar days of being selected as the exponsive bidder, a formal waiver request and required documentation that supports the type of waiver being requested. That failure to submit the required documentation within the specified timeframe is cause for a non-responsive determination that may result in rejection of the proposal. To faithfully comply with providing U.S. domestic products at or above the approved U.S. domestic content percentage as approved by the FAA. To faithfully comply with providing U.S. domestic products that the FAA rejects.
CMAR Federally Funded Instructions and Execution Documents Terminal 3 Improvements Bid Package No.: 1.4	55		CMAR Federally Funded Terminal 3 Improvements	Instructions and Execution Documents Bid Package No.: 1.4	S5-48	To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.
Debarment	CMAR Federally Funded Terminal 3 Improvements	Instructions and Execution Documents Bid Package No.: 1.4	SS-47	Non- Segregated	CMAR Federally Fu Terminal 3 Improven	
		hhyina		Facilities		BABA Certification

Lobbying

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreemen ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits ☐ Bid Bond: \$5-54. Instructions and Execution Documents

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. ☐ Bid Bond; S5-54.



PROCUREMENT – SEXUAL HARASSMENT AFFIDAVIT

Complete and return with your bid.

Include as an attachment on Building Connected.

SEXUAL HARASSMENT POLICY AFFIDAVIT (SECTION 2-92-612)

The policy prohibiting sexual harassment as described in Section 2-92-612 of the Municipal Code of Chicago ("Me	CC") is
applicable to contracts paid from funds belonging to or administered by the City.	

Specification #:

In accordance with requirements set forth in Section 2-92-612 of the MCC, Contractor hereby attests that Contractor has a written policy prohibiting sexual harassment in compliance with Section 6-10-040 of the MCC.

In accordance with Section 6-10-040 of the MCC, Contractor's written policy prohibiting sexual harassment shall include, at a minimum, the following information:

- (i) a statement that sexual harassment is illegal in Chicago;
- (ii) the following definition of sexual harassment: ""Sexual harassment' means any (i) unwelcome sexual advances or unwelcome conduct of a sexual nature; or (ii) requests for sexual favors or conduct of a sexual nature when (1) submission to such conduct is made either explicitly or implicitly a term or condition of an individual's employment, or (2) submission to or rejection of such conduct by an individual is used as the basis for any employment decision affecting the individual, or (3) such conduct has the purpose or effect of substantially interfering with an individual's work performance or creating an intimidating, hostile, or offensive working environment; or (iii) sexual misconduct, which means any behavior of a sexual nature which also involves coercion, abuse of authority, or misuse of an individual's employment position.";
- (iii) a requirement that all employees participate in: (1) sexual harassment prevention training annually, (a) Employees shall participate in a minimum of one hour of sexual harassment prevention training annually, and (b) Anyone who supervises or manages employees shall participate in a minimum of two hours of sexual harassment prevention training annually, and (2) one hour of bystander training annually;
- (iv) Examples of prohibited conduct that constitute sexual harassment;
- (v) Details on: (1) how an individual can report an allegation of sexual harassment, including, as appropriate, instructions on how to make a confidential report, with an internal complaint form, to a manager, employer's corporate headquarters or human resources department, or other internal reporting mechanism; and (2) legal services, including governmental, available to employees who may be victims of sexual harassment; and
- (vi) A statement that retaliation for reporting sexual harassment is illegal in Chicago.

Contractor understands that it may be required to produce records to the CPO to verify the information provided. Under penalty of perjury the person signing below: (1) warrants that he/she is authorized to execute this Affidavit on behalf of Contractor, and (2) warrants that all certifications and statements contained in this Affidavit are true, accurate, and complete as of the date of execution.

Name of Contractor:
(Print or Type)
Signature of Authorized Officer:
(Signature)
Title of Signatory:
(Print or Type)
State of
County of
Signed and swom (or affirmed) to before me on (date) by
(name/s of person/s making statement).
(Signature of Notary Public)
(Seal)

CMAR Federally Funded Terminal 3 Improvements Instructions and Execution Document Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submi through Building Connected: ☐ Building Connected Bid Form; properly completed online Document Acknowledgement: ii ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 Addenda (if any) acknowledged on the Proposal Page. □ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25 ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. Affidavit of Non-Ciliusion Seela in 1th 150 m Company of the Comp is desympted. If Performance and a second se ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits ☐ Bid Bond: \$5-54. CMAR Federally Funded Instructions and Execution Documents Bid Package No.: 1.4

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services - Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54.



DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submis through Building Connected: ☐ Building Connected Bid Form; properly completed online □ Document Acknowledgement: ii. ■ Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5 ☐ Addenda (if any) acknowledged on the Proposal Page. ■ DBE Schedules completed: ☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25. ☐ Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30. ☐ Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed, signed, and notarized: S5-31. □ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33. Exhibit A DBE Requirement for Bidders List; S5-41. ■ DBE Utilization Report; S5-36. Owner Agreement Exhibit D, See Master Agreemen ☐ Schedule 1 - Affidavit of Non-Collusion ☐ Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours ☐ Schedule 4 – Statement of Bidders Qualifications ☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit ☐ Schedule 6 – Contractors Payment and Performance Bond ☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects Schedule 8 - Certification of Compliance with FAA Buy American Preference - Equipment/Building Projects ☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions ☐ Affidavit of Uncompleted Work completed, signed, and notarized: S5-43 ☐ Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6 ☐ Bidder's Financial Statement. ☐ Certifications (FAA) ☐ Debarment; S5-46 Lobbying: S5-47. ■ Non-Segregated Facilities: S5-58 ■ BABA Certification: S5-51 ☐ Sexual Harassment Affidavit: S1-8 ☐ G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits ☐ Bid Bond: \$5-54. Instructions and Execution Documents

DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate The following Documents are to be returned with your proposal; a completed bid package will include each of the following documents without exception. Please attach the following documents to your electronic submission through Building Connected: ☐ Certifications (FAA) Debarment: S5-46. Lobbying; S5-47. Non-Segregated Facilities; S5-58. BABA Certification; S5-51 ☐ Sexual Harassment Affidavit; S1-8 G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits. Bid Bond; S5-54.



PROCUREMENT - BID BOND

Bid Bonds are Required. Follow all instructions.

Include as an attachment on Building Connected.

OPS Version 04/25/2017

INSTRUCTIONS FOR BID BOND FORM

Bidders/Proposers: Give these instructions to your surety.

1.	The Bond must be on the CMAR's for	rm. N	o substitutions will be acceptable.							
2.	Copies of the form are acceptable. How the paper, and page 2 on the opposite sid		DPS Version 04/25/2017							
				BID BOND						
3.	The amount of the Bond must be that so the bond should be expressed as a percent		KNOW ALL MEN BY THESE PRESENTS, that we							
4.	All blank spaces to be filled in must indicated. Determinations of legibility be accepted, nor will any Bond form on	will								
5.	Insert the full legal name and business a form. If the Bidder/ Proposer is biddir stated in the same space as the full legal	ng ur	bound unto CLARK - W.E. O'NEIL JV, hereinafter called the Obligee, in the sum of Ten percent (10%) of the amount bid for the payment of which sum well and truly to be made, the said Principal and the said Surety, bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.							
6.	The address of the Principal must be co as well, as bonds to be returned will be r		WHEREAS, the Principal has submitted a bid in accordance with the Bid Package for Specification Section(s), for Terminal 3 Improvements, Chicago, IL.							
7.	The Bond must include the Surety's nan	ne, th	NOW, THEREFORE, if the Obligee shall accept the	bid of the Principal and the Principal shall,	within the specified					
8.	The Bid Package number must appear or	n the	period of time, one hundred twenty (120) days, enter into a formal contract and furnish a surety guaranteeing the full and							
9.	The Surety executing the bond must appact within the limitations listed therein.	pear	faithful performance of the Work, all as provided in the Instructions to Bidders, Plans and Specifications and other Contract Documents, including addenda, of said Obligee, then this obligation shall become void; otherwise it shall remain in full force and effect.							
10.	The names and titles of the people signing	ng th								
11.	Corporations executing the bond shall a "seal not required" in the space where the		In the event the Obligee determines the Principal has failed to comply with any requirement as set forth in the preceding paragraph, then the Principal shall pay to the Obligee the difference, not to exceed the full penal sum set forth above, between the amount specified in the Principal's bid and such larger amount for which the Obligee may contract with							
12.	A person authorized to bind the Bidder/I	Propo	another party to perform the work covered by said bid, together with all court costs, all attorney's fees and any other							
13.	The Bond must be signed by an attoridentifies the surety company's signator		expense of recovery. IN TESTIMONY WHEREOF, the said Principal and said Surety have caused this instrument to be signed by their							
14.	The date on which the Surety's Power of the bond was signed by the Surety.	of At	respective officers and their corporate seals to be her	reunto affixed thisday of	_A.D. 20					
15.	In its application to negotiated contracts	, the		(Principal)	(Seal)					
			Witness:	(Business Address)						
			By	(Signature)	(Title)					
			Or Secretary's Attest	(Signature)	(Title)					
				(Surety)	(Seal)					
			Witness:	(Business Address)						
				By						
			Or Secretary's Attest	(Signature)	(Title)					
	ederally Funded In	structi		ions and Execution Documents Bid Package No.: 1.4	S5-54					

PROCUREMENT – PAYMENT & PERFORMANCE BOND

See P&P bond forms in Exhibit C of the Subcontract Agreement in Part Two B and also Owner Agreement Exhibit D, see Master Agreement Schedule 6.

Include as an attachment on Building Connected.

*At COT3 option, you may be enrolled into the Subcontractor Default Insurance (SDI) program

DPS Version 04/25/2017

*RIDER ATTACHED CONTRACTORS PERFORMANCE & PAYMENT BOND

See P&P bond forms in Exhibit C of the Subcontract Agreement in Part Two B.

CMAR Federally Funded Terminal 3 Improvement Instructions and Execution Documents

S5-55

PROCUREMENT – BID SUBMISSION CHECKLIST

BOOK 1 is not required to be submitted with the bid in its entirety

All required forms must be included with the bid.

Upload as an attachment with your submission on Building Connected.

Check all forms for signature, initials, notarizations, etc. requirements.



Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection. Bid the complete scope of work as outlined. If required, submit questions through a pre-bid Request for Information (RFI).

SUBMIT ANY QUESTION REGARDING

REQUIRED BID FORMS AS A RFI TO

ProjectCOT3.inquiries@clarkconstruction.com or on BuildingConnected

	DOCUMENT SUBMITTAL CHECKLIST (Federally Funded) This checklist is intended to assist Bidders but does not necessarily reference all documents required in this Specification. Bidders should review this entire Part One for additional requirements. Missing forms may invalidate bid.						
Spe							
foll	following Documents are to be returned with your proposal; a completed bid package will include each of the wing documents without exception. Please attach the following documents to your electronic submission ugh Building Connected:						
	Building Connected Bid Form; properly completed online. Document Acknowledgement; ii.						
	Appropriate Proposal Page completed, signed, and notarized; S5-1 – S5-5.						
	Addenda (if any) acknowledged on the Proposal Page.						
	DBE Schedules completed:						
_	☐ Schedule B: Affidavit of DBE/Non-DBE Joint Venture, if applicable; completed, signed, and notarized; S5-25.						
	Schedule C: DBE Letter of Intent to Perform as Subcontractor or Supplier, completed and signed; S5-30.						
	 Schedule D: Affidavit of Prime Contractor Regarding Disadvantaged Business Enterprises (DBE's) completed signed, and notarized; S5-31. 						
	□ Schedule F: Report of Subcontractor Solicitations, completed, signed, and notarized; S5-33.						
	☐ Exhibit A DBE Requirement for Bidders List; S5-41.						
_	☐ DBE Utilization Report; S5-36.						
ш	Owner Agreement Exhibit D, See Master Agreement						
	Schedule 1 - Affidavit of Non-Collusion						
	Schedule 2 – Regulations of the Department of Procurement Services for Percentages of City and Project Area Residents Working Hours						
	Schedule 4 – Statement of Bidders Qualifications						
	☐ Schedule 5 – Certificate of Filing On-Line Economic Disclosure Statements (EDS) and Affidavit						
	☐ Schedule 6 – Contractors Payment and Performance Bond						
	☐ Schedule 7 – Certification of Compliance with FAA Buy American Preference – Construction Projects						
	☐ Schedule 8 – Certification of Compliance with FAA Buy American Preference – Equipment/Building Projects						
	☐ Schedule 9 – Certification Regarding Tax Delinquency and Felony Convictions						
_	Affidavit of Uncompleted Work completed, signed, and notarized; S5-43						
	Certificate regarding Removal of All Waste Materials and Dump Sites; S5-6.						
	Bidder's Financial Statement.						
ш	Certifications (FAA)						
	Debarment; S5-46.						
	☐ Lobbying; S5-47. ☐ Non-Segregated Facilities; S5-58.						
	Non-Segregated Facilities; 85-58. BABA Certification; S5-51						
	Sexual Harassment Affidavit; S1-8						
	G-11 Covered Telecommunications Equipment or Services – Subcontractor Representation; See subcontract Exhibits.						
	Bid Bond; S5-54.						

PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

Contains various requirements impacting the work and its administration

PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents


Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT - SUBCONTRACT EXHIBITS A, B & C

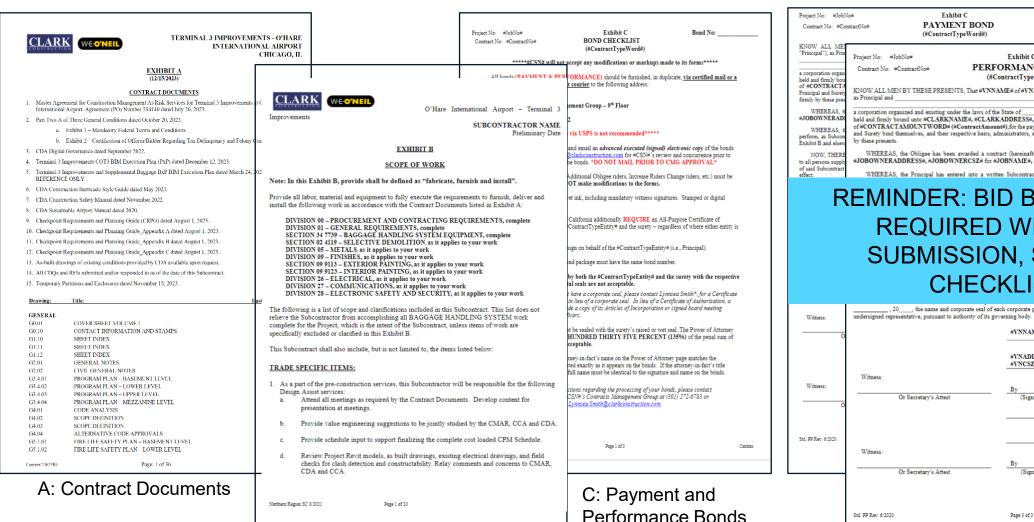


Bond No: #ContractEnhCLi Exhibit C Rond No: PERFORMANCE BOND (#ContractTypeWord#) KNOW ALL MEN BY THESE PRESENTS, That #VNNAME# of #VNADDRESSL# #VNCSZL# (hereinafter called the "Principal a corporation organized and existing under the laws of the State of held and firmly bound unto #CLARKNAME#, #CLARKADDRESS#, #CLARKCSZ# (hereinafter called the "Obligee"), in the su of #CONTRACTAMOUNTWORD# (#ContractAmount#), for the payment of which sum well and truly to be made, the said Princip and Surety bind themselves, and their respective heirs, administrators, executors, successors and assigns, jointly and severally, firm WHEREAS, the Obligee has been awarded a contract (hereinafter called the "Prime Contract"), by #JOBOWNERNAME #JOBOWNERADDRESS#, #JOBOWNERCSZ# for #JOBNAME#, #JOBLOCATION# and: WHEREAS, the Principal has entered into a written Subcontract with the Obligee, dated #CONTRACTDATEWORD# to REMINDER: BID BONDS ARE REQUIRED WITH BID SUBMISSION, SEE BID **CHECKLIST** , 20 , the name and corporate seal of each corporate party being hereto affixed and these presents duly signed by i undersigned representative, pursuant to authority of its governing body #VNNAME# (Seal) #VNADDRESSL# #VNCSZL# (Title) (Signature (Business Address (Title) (Signature

Contra

B: Scope of Work

PROCUREMENT – SUBCONTRACT EXHIBITS D, D-1, D-3, D-4

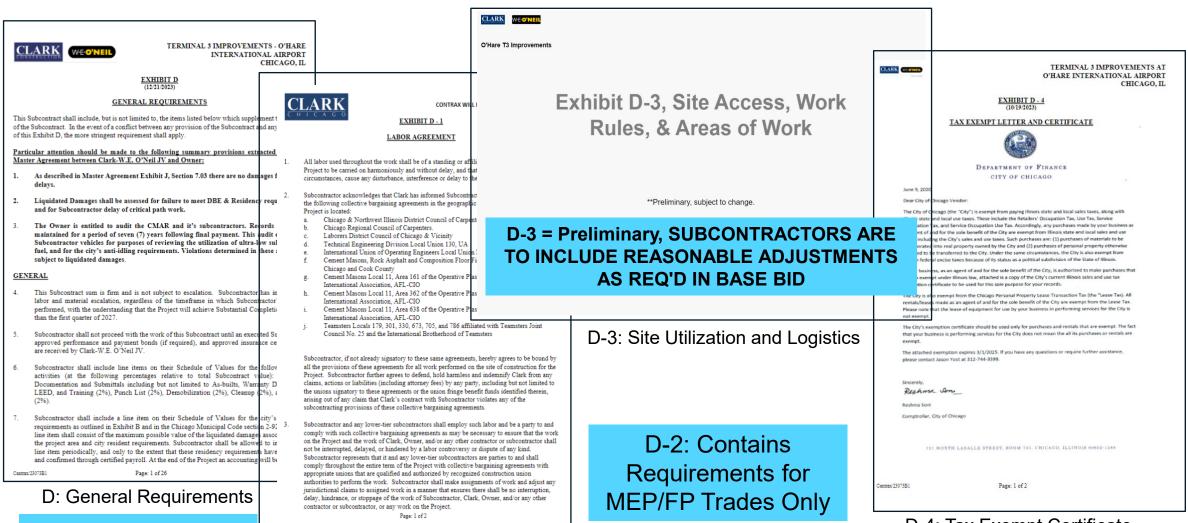

D-1: Labor Agreement

D = Very Important!

PROCUREMENT - SUBCONTRACT EXHIBIT E

Insurance Requirements



TERMINAL 3 IMPROVEMENTS AT O'HARE INTERNATIONAL AIRPORT CHICAGO, IL

EXHIBIT E (10/20/2023)

INSURANCE REQUIREMENTS

Clark Project No.: 23073B1

OWNER CONTROLLED INSURANCE PROGRAM

1) OVERVIEW:

The Owner (Sponsor) may elect to provide certain insurance coverages under an Owner Controlled Insurance Program (OCIP). The OCIP is more fully described in the Sponsor's OCIP Insurance Manual (hereinafter "Insurance Manual") that is incorporated in this Exhibit E by this reference and made a part hereof. All Enrolled Parties are strongly encouraged to read the OCIP Manual and the OCIP Insurance Policies in detail prior to enrolling in the OCIP. The OCIP will provide to Enrolled Parties (as defined below) workers' compensation, employer's liability insurance, commercial general liability insurance, and excess liability insurance ("OCIP Coverage's"), as summarily described below, in connection with the performance of the subcontract work. In the event that there are any discrepancies between this Exhibit and the OCIP Manual the most strict terms shall apply.

2) ENROLLED PARTIES AND THEIR INSURANCE OBLIGATIONS:

OCIP Coverages shall cover Eurolled Parties. Eurolled Parties are: Sponsor, eligible Subcontractors and all of their subcontractors at any tier, who enroll in the OCIP, and such other persons or entities as Sponsor in its sole discretion may designate (each such party who is insured under OCIP is collectively referred to as an "Eurolled Party"). Parties performing labor or services at the Project site as defined in the Insurance Manual, are eligible to enroll in the OCIP unless designated by Sponsor as an Excluded Party (as defined below). Eurolled Parties (Subcontractors all obtain, maintain, and require all of their subcontractors at any tier to obtain and maintain, the insurance coverages specified below and the Insurance Admual.

3) EXCLUDED PARTIES AND THEIR INSURANCE REQUIREMENTS:

OCIP insurance does not cover the following "Excluded Parties":

- a) Hazardous materials remediation, removal and/or transport companies and their consultants;
- b) Architects, surveyors, engineers, soil testing engineers, and their consultants;
- c) Vendors, suppliers, fabricators, material dealers, truckers, haulers, drivers and others who merely transport, pick up, deliver, or carry materials, personnel, parts or equipment or any other items or persons to or from the Project site.
- d) Any entity who does not perform any actual labor on the Project site;
- Any parties or entities not specifically identified in this Exhibit E, or excluded by Sponsor in its sole discretion, even if otherwise eligible.

4) OCIP COVERAGES:

The summary descriptions of the OCIP Coverages in this Exhibit E or the Insurance Manual are not intended to be complete, or to alter or amend any provision of the actual OCIP Coverages. In the event any provision of this Exhibit E, the Insurance Manual, the Contract Documents, or the summary below conflicts with the OCIP insurance policies, the provisions of the actual OCIP insurance policies shall govern.

OCIP Coverages shall apply only to those operations of each Enrolled Party performed at the Project site in connection with the subcontract work and only to Enrolled Parties that are eligible for the OCIP, even if erroneously enrolled in the OCIP. The OCIP shall provide only the following insurance to eligible and Enrolled Parties:


Contrax/23073B1

Page: 1 of 7

Telecommunications

Equipment or Services

PROCUREMENT -SUBCONTRACT EXHIBITS G2, G3, G4, G8, G11

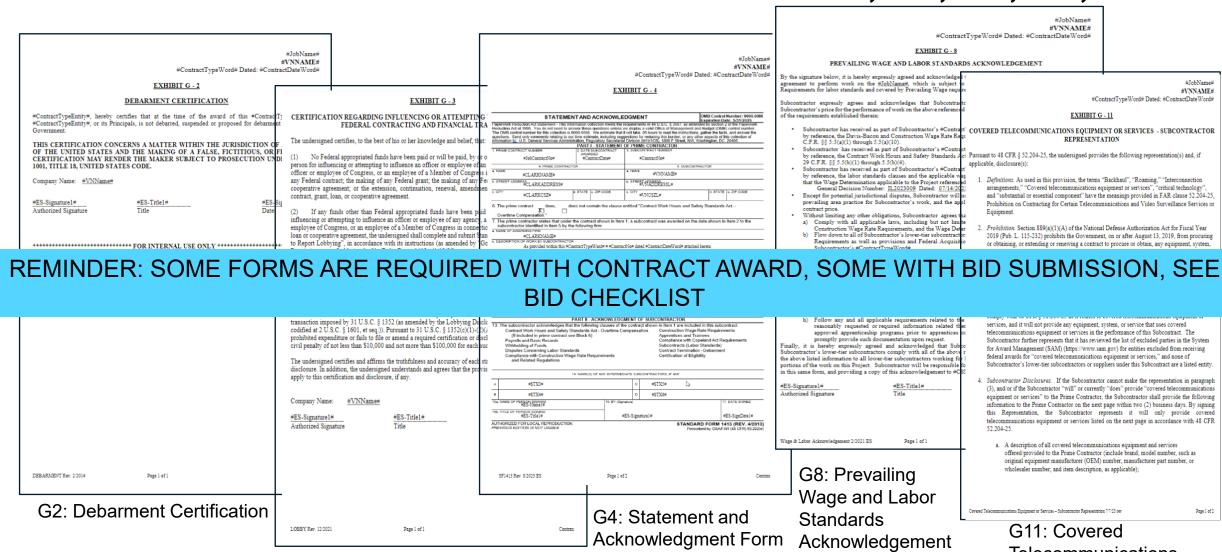

G3: Disclosure of Lobbying Activities

IMAGE IS FOR REFERENCE ONLY – USE THE APPLICABLE FORM(S) FOR EACH TRADE PACKAGE

Form

PROCUREMENT – SUBCONTRACT EXHIBIT J & J-1

J: Owner Required Flowdowns

J-1: Self Certification Form



TERMINAL 3 IMPROVEMENTS - O'HARE INTERNATIONAL AIRPORT CHICAGO, IL

Address

OWNER REQUIRED FLOWDOWNS

Preliminary Exhibit J - Subject to Change Upon Execution of the Fina

- [Subcontractor/Supplier/Consultant/Designer/Provider/Lessor] (hereinated) "Subcontractor") shall comply with all terms, conditions, and provisions that are or set forth in full text in, or otherwise comprise a part of or are applicable to the Construction Management At-Risk Services for Terminal 3 Improvements at (hereinafter referred to collectively as the "Prime Contract"). All such terms, con hereby incorporated by reference and shall have the same force and effect as if the forth in full text in this [Subcontract/Order/Agreement/Lease Order] (hereina "Subcontract"). In the event of a conflict between the terms and conditions inclu any other terms and conditions included in the Subcontract, this Exhibit J shall g
- Subcontractor hereby agrees to include all clauses included herein in all of its Subcontractor enters into a lower tier subcontract at any time during the perform copy of those lower tier subcontracts must also be provided to Clark O'Neil. Thi to any and all lower tier subcontractors related to the performance of this Subcon

Exhibit D - Required Subcontract Provisions

II. Standard of Performance, Construction Manager will require that its Trade (minimum, meet the standard of performance set forth herein.

In addition to performing the Work in full compliance with the Contract Documents, perform, or cause to be performed, all Work required of it under the terms and could that degree of skill, care, and diligence normally exercised by qualified and experien performing work in projects of a scope and magnitude comparable to the Project. Un materials and equipment will be new, and of such quality as required to comply with The Trade Contractor will, when required, furnish satisfactory evidence as to kind an and equipment. All labor will be performed by workers skilled in their respective rabe of good quality so that first class work in accordance with the standards of constru Contract Documents will result.

III. Permits, Licenses and Regulations. Subcontracts must contain the following permits, licenses and regulations.

- 1. The Trade Contractor will not be responsible for the building permit cost. How specific permits, applicable licenses and associated fees will be the responsibility of
- 2. The nature of the foundation systems required on portions of this Project may permits, and coordination will be required with the City of Chicago Bureau of Under required by the Contract, the Trade Contractor, representing its familiarity with these processes, is responsible for any and all submittals, fees, coordination, and any other approvals required by the authorities having jurisdiction for the installation of these

Contrax/23073B1

Page: 1 of 66

#JobName# #VNNAME#

#ContractTypeWord# Dated: #ContractDateWord#

SELF CERTIFICATION FORM

#VNADDRESSL# #VNCSZL#

Business Concern Self Certification [SELECT AT LEAST ONE (1) BOX THAT APPLIES TO YOUR

#\$0# Large Business (LB) #\$1# Small Business Enterprise (SBE) #\$12# Certified Disadvantaged Business Enterprise (DBE) #\$13# Minority Business Enterprise (MBE) #\$14# Woman Business Enterprise (WBE) #\$11# Other: #\$TX2#

II. Commercially Useful Function:

Attention is directed to Exhibit B of your #ContractTypeWord#, in which you agree that each Disadvantaged Business Enterprise ("DBE"), if any, with which you subcontract for work within the scope of your #ContractTypeWord# will perform a Commercially Useful Function as defined in Department of Transportation Regulations, 49 C.F.R. § 26.55. See pages 3-5 of this Exhibit J-1 for information concerning regulatory and #ClarkName# (hereinafter "#CSN#") requirements regarding "Commercially Useful Function." #ContractTypeEntity# further agrees to assure that each DBE lower tier subcontractors, if applicable, possesses a sufficient DBE certification for all within the scope of such lower tier subcontract.

III. In Section I above, Business Concern Self Certification:

Select here #\$RD0E# and skip the rest of Section III if you are NOT a Certified Disadvantaged Business Enterprise (DBE).

If you checked the box for "Certified Disadvantaged Business Enterprise (DBE)", complete the below items that apply to your organization:

The Illinois Unified Certification Program (ILUCP): (check the subset that applies to this Project)

#\$18# CERTIFIED U/DBE by the Illinois Department of Transportation (IDOT) Certification #: #\$TX10# Date of Certification: #\$TX11# * Attach a copy of the Certification

(this space left intentionally blank)

II DRE CERTIFICATION 10/2017 PS

PROCUREMENT -SUBCONTRACT EXHIBIT R

				Contract Numbe	#JobName# #VNNAME# r: #ContractNo# Dated: #ContractDateWord#	
	#JobName#		#JobName# #VNNAME#	EXHIBIT I	R	
Contract Number: #ContractNo# Dated: #Contra	#VNNAME# ctDateWord#		Contract Number: #ContractNo# Dated: #ContractDateWord#	LOWER TIER PARTIAL AFFIDAVIT AND PARTIAL #ClarkName		
EXHIBIT R		SUBCONTRACT	EXHIBIT R OR FINAL AFFIDAVIT, WAIVER OF LIEN, AND RELEASE	ClarkAddresse ClarkCSZ#	Project Number: #footNos Claris's #ContractTypeEntitys: #UNNames ContractDate: #ContractDates	
AFFIDAVIT AND PARTIAL UNCONDITIONAL RELEASE OF LIENS/CLAIMS #ClarkName#	·	SUBCONTRACT	#ClarkName#	Period From: To:	Contact Date:	#JobName# #VNNAME#
#ClanicAddraux# Project Number: #JohNo# #ClanicSZ# #ConnectlypeEntity# #FYNSma#	Contract Number: #Contract	tNo: #ClarkAddress#	Project Number el-chébie d'emmet Type Barbye d'ADNomas Contract Dans Contract Dans Contract Dans Contract Number d'Contract Dans Contract Number d'Contract Dans	 Certification. Affirmation and Warranties The undersigned, for and in consideration of psymeats made by #ClarkName# ("#CSN#") to performed in the construction of the above referenced Project pursuant to the above-referenced A; 		er: #ContractNo# Dated: #ContractDateWord#
Contract Date CommentDate Contract Date ContractDate Paried From: To: Payment Request No: ContractNos	EXHIBIT R	Period From: To:	Payment Request No.:	performed in the construction of the above selection of project procurant to the above-referenced A. The contemptation is received permanent in fail, the ventralings of all works performed and except for retainings, these was no contenting claims against a Contract Type distript and/or its and garantees, or the Project in consection with work performed in the convertient of the Project. The understand has not assigned to revocate any claim, my last, or my right to file or truntient, the Contract Type distript with the file or truntient, the Project.		
1. Certification: Affirmation and Warranties The undersigned, attained plage the recept and indispases of good and valuable consideration, to support in satisfacement to the payment requested in Permitting and the control of the approximation of the approximation of the Appendix of the Cital Section 2018.	FORM A - OUTSTANDING CHANGE ORDER #ClarkName#	1. There exercise of first reservoir in the sec-	ments made to it by #Clark/Danest, (*#CDN**) or to a subcontractor, materialisms, or supplies of the undersigned for labor arts on of the above-referenced project pursuant to the above-referenced contract, hereby certifies as follows: one of \$	 The undersigned has paid in full all laborers, and subject to retainage no greater materialmen and others with respect to all work performed in the construction of the Project through file zero claim, demand, lies, excumplemance or action seniors #ContractTwoExhibit and for its sure 	LOWER TIER FINAL AFFIDAVIT, WAIV this #ClarkName	
 Payment Request No. represents the actual value of work performed through the above indicated payment request period for which terms of the Agreement (and all surfaceigned changes thereto) between the underviewed and #CSN# relating to the Project, including (i) all labor emended. 	ayun arClarkAddresse Project sithe arClarkAddresse Stock	tTypel II. In consideration of the above-mentioned	the gradient of the first property of the third regard for the third property of the first property of the third regard for the r	guarantom, or the Project. 4. The undersigned has not given or executed any security interest for or in connection which have been or are to be placed upon or installed in the Project, and is conveying good title to 5. The undersigned has paid all amounts due benefit funds, applicable taxes, applicable	#ClarkAddress# n not = #ClarkAddress# tips: is Set	Project Number: #fobNo# Clark's #ContractTypeEntitys: #fobNo## Contract Deta: #ContractDeta# Contract Number: #ContractOe#
Project (i) of meterals and approximate followed to the site and other incorporated or to be incorporated and to the project (iii) all meterals, fortunes, and states officials to the better anticorrect or by a "CAUSe and for twink preparat therefore parameted by "CAUSe, contrar variation for the project the project of the project the contract variation for the project that the project think there is the preparation of the project that the contract variation for the project and (v) all appropriate project the project that the value including means (i) the project (iv) and the project (iv) and the value (iii) and in the project (iv) and the value (iii) and in the "Whit".	provi Period From: To: Payment	Numb their successors and assigns all rights that presently a	salican on the project and the title company or companies examining and/or insuring title to the project and any and all of salit or hereafter may accurate to the undersigned to assert a lieu upon the hand and improvements comprising the project by their insurancements are character or any assemblement of said law regarding the nights of a constructor understance. Inhome	performed in the construction of the Project. 6. The undersigned has complied with all applicable federal, state and local laws, codes of the Project. 7. The undersigned has the right, power and authority to execute this document.	period From: To: The undervised, for and in consideration of the permeans analy to it by #ClastOlasse#, (the "Co	Payment Request No.:
2. The undersigned has received prepared in the law retrings, for all Work performed in the construction of the Project through the difference point, and, except of possing changes orient colonium. C'claimes, if the are followed from a facilities to constructing Claimes, and such and the same and form a facilities and parameters, or the Project in connection with Work performed drough the Effective Date. In the case of colonium of Project main a Found and the analysis of the Claimes of Claimes Claimes, the same projects are not as the colonium of the Claimes of Claimes Claimes, the same projects are not projects and the colonium of the Claimes of Claimes Claimes, the same projects are not as the colonium of the Claimes of the Claimes of the Claimes of Claimes Claimes.	ou		ign any claim for payment or right to perfect a lien against the project and the undersigned has the right, power, and authority	II. Waiver and Release The undersigned does hereby freever make and release in favor of #ContractTypeEntity# and its guarantes, the Project, and the totle company or companies examining and or invuring title to the	in and or materials furnished for the construction of the above-referenced project, hereby certifies	as follows:
review varies in right to have my claim variance around out or, making to or conservate concerning my caning in the work of claim in conserva- the Effective Data. 3. The undersigned has not assigned to suppose my Claim, may lies, or any right to file or perfect a lies, against #CENP and/or its survetse, and/or its leading and management or the Poolet.	ITEM DESCRIPTION OF WORK	the project have received payments due and that none	is and subcontractors employed by it and all suppliers or materialmen from which it has acquired materials incorporated into of such aboves, subcontractors, suppliers, or materialmen have any claim, demand, or lien against the project.	presently exist or haveafter may accrue to the unfavaigned by reason of work performed in the or essent a lise upon the land and/or improvements comprising the Project and (2) to sever to bring upon or now has against #CombactTypeEnthy# and/or its sureties, #CSSW# and/or its sureties, the Owne	I Upon secure of final perment in the amount of \$1\$ for performed in the contraction of the performed in the construction of the project, and by necessarian of each final perment and in contract of the performed in the company made in the contract profit and the Contract C	
4. The undersigned has paid all laborate, and, subject to retaining no greater than the percentage retainings held by #CENA; all subconstructor and others with respect to all two performed legislating the Effective Date. The undersigned has not given or executed now security integer for or in connection with any materials, equipment, applicances, machines, fit 	raps	upon or installed in the project. This Final Affidant: Waiver of Lian, and Ralesse that	seated by the underligned for, or in connection with, any materials, appliances, machinery, fittures, or familiangs placed. ———————————————————————————————————	III. Indemnification The undersigned hereby agrees to indemnify and hold harmless #ContractTypeEntity# and its surgamment, from any and all damages, costs, expenses, demands, and suits, (including reasonable alling by any party with respect to any (i) work performed in the construction of the Project or work.	to the project and any and all of their successors and assigns all rights that presently exist or hereaft	on the project and the company to companie watering and to many fitted are not not the sundaring the search account of the sundaring the sundaring the state of a contractor, is are situated or any amendment of said law regarding the rights of a contractor,
have been or me to be planed upon or invatiled in the Project, and in conveying good trids to the same to MCDNs and or the Owner. 6. The underlyinged has paid of applicable seems, does, duties, other charges, and amounts due beautifi facult soluting directly or indirectly to the	Nek 1	with respect to the project subsequent to the execution		day of 20 (ii) may registe wanted or released herein, and (iii) may mixed	The undersigned has not and will not assign any claim for payment or right to perfect	a lien against the project and the undersigned has the right, power, and authority
FORMS A	RE REQUIRED WI	TH APPLI	CATION FOR PAYI	MENT, AS APPL	ICABLE	
and agrees that except for retainings and the Claims listed on the attached Form A that it hereby forever waives and releases all causes of action, claims to date of discussion in afficiency or remodelpha impact (alone), units and decreased, because or undergoes that the understand grow had some but or had	schodi /	_	(Automas agains)	T	under any supplemental contract or contracts, whether oral or written, for extra or additional work with respect to the project subsequent to the execution hereof.	c on the project and for any further work done or materials furnished at any time
and appear that except for reminage and the Chains listed on the stacked Form A that it havely flower values and subsess all clauses of action, chains (in, shale), disreption, auditionary or considering super chains), with and demands, known or unknown, that the undexqueet over hat, now has or he officed and the subsequent over hat, now has or he officed and on a subsequent chain of the subsequent over hat, now has or he officed the subsequent over his order of the Project by seven of relating to, unknown for in connect through the Effective Date. 2. **The Advanced Company of the Service C		Subscribed and sworm before me thisday of	(National Signature) TITLE: (Title)	Bull-scribed and system before me this day of, 20	under any supplemental command or commands, whether and or nothers, for extra or additional work with respect to the project subsequent to the execution harved? IN WITNESS WHEREOF, this Affidient, Wester of Lieu, and Ralesse has been executed this _	t on the project and for any further work done or materials furnished at any timeday of
#CDN and or in severa, the Ornes of the Project and or in leaders and garanters, or the Project, by reason of, relating to, mixing from or in consent through the Effective Date. III. Indemnification: The malercaged hearing agrees to indemnify and held learning with DN and in various, and the Ornes of the Project and in leaders and garanters, the Third and the CDN and the CDN and the CDN and in various, the CDN and the Ornes of the Project and in leaders and garanters, the Third and the CDN and the CDN and the CDN and the CDN and in various, and the Ornes of the Project and in leaders and the CDN and the CDN an	9 10 10 10 10 10 10 10 10 10 10 10 10 10	Subscribed and snoon before me this day of	(National capacities)	Debocribed and evens hefers was files	with respect to the project subsequent to the execution hereof.	to the project and for my further work done or numerical furnished at my time day of
action and on a course, the Ormer of the Project and or in leaders and garanters, or the Project, by rescent of relating to, enthing from or in consent through the Effective Den. III. Intermedication The undersugged abovely gares to indemnify and held harmless of NOS and in various, and the Oreone of the Project and in leaders and garanters, the professional or which about the two performed in connections of the Project to Vigille 1975. Only the Figure 1975, the Connection of the Project to Most of the Project to Most of the Project to Most of the Project to Intermedication and Intermedication and Intermedication and Intermedication and Project in Class Column. Upon the expect the Orace of the Project to Intermedication and Intermedica	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of:	(Namonase organise)	Dubecirbed and overan before and thisday of	with respect to the project subsequent to the execution hereof.	day of
aCDNs and or in severies, the Ormes of the Project and or in landers and garanters, or the Project, by reason of, relating to, mixing from or in consent through the Effective Date. III. Intermedization The undersupped indepely agrees to independ year the hold harmless a CDNs and in venture, and the Ocupe of the Project and in landers and garanters, & cons, appears (including transport Sees increase), destaunts, and with, destroy or indirectly relating us may cross of extent, claim or line filling until particular of which should have been good mode in construction of the Project through the Affective Date, (10) are great sometimes of or interest of the Project or See landers and garanters, the Second of the Contract of the Project or in Section on agaranters, the advanced will understand to defend which care of corner or as follows in on the Contract of the Project or in Section on agaranters, the advanced will understand to defend which care of corner on a Section of an other corner or contract of the Contract of the Project or in Section on a garanters, the advanced will understand to other other through our or a Section of an other corner or contract of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project or in Section of the Contract of the Project of the Section of the Contract of the Project of the Section of the Contract of the Project of the Project of the Section of the Project of the Section of the Contract of the Project of the Section of the Sectio	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of:	(Pataniana capanian)	Bulworshed and evens before me fisisday of, 20 Flore of County of	with respect to the project subsequent to the execution hereof.	day of
a CDN and or in severies, the Ormer of the Project and or in lancine and garanters, or the Project, by season of, relating to, mining from or in consent through the Efficient Den. III. Indemnification: II	10 10 10 10 10 10 10 10 10 10 10 10 10 1	State of:	TITLE:	Subscribed and sween before me finis day of, 20, Blass of Zousty of	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
arCDN and/or in correct, the Cross of the Project and or in landers and garanters, or the Project, by reason of relating in, mixing from or in consent through the Effective Date. III. Intermedication III. Intermedication The undersuper the sharely agrees to industrially and old humilion of CNNs and in various, and the October of the Project and in leaders and garanters, in particular or which shared have been performed are which characters are been preferred as the project through the Effective Date, (a) for region where of reviewed have the configuration of the bank of their configuration. Affirm the configuration of the project through the Effective Date, (a) for region where of reviewed have the configuration of the project through the Effective Date, (a) for region which of reviewed have the configuration of the project through the Effective Date, (a) for region which of reviewed have the configuration of the project through the Effective Date of the Project or in landers and garanters, the underspited into different and Press Effective Classes. Class	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of:	TITLE: (786) Noney Public: N) Commission Engines:	Subscribed and evens before me this day of, 20 State of, 20 Density of	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
arCDN and/or in correct, the Cross of the Project and or in landers and garanters, or the Project, by reason of relating in, mixing from or in consent through the Effective Date. III. Intermedication III. Intermedication The undersuper the sharely agrees to industrially and old humilion of CNNs and in various, and the October of the Project and in leaders and garanters, in particular or which shared have been performed are which characters are been preferred as the project through the Effective Date, (a) for region where of reviewed have the configuration of the bank of their configuration. Affirm the configuration of the project through the Effective Date, (a) for region where of reviewed have the configuration of the project through the Effective Date, (a) for region which of reviewed have the configuration of the project through the Effective Date, (a) for region which of reviewed have the configuration of the project through the Effective Date of the Project or in landers and garanters, the underspited into different and Press Effective Classes. Class	10 10 10 10 10 10 10 10 10 10 10 10 10 1	State of:	TITLE: (Title) Notery Public: My Commission Express:	Steas of County of	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
a CDN and or in course, in a Crosse of the Project and or in leaders and garanters, or the Project, by researc of, relating to, mining from or in consent through the Effective Des. III. Intermedication III. Intermedica	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of:	TITLE:	Deburched and onem before me finis day of	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
a CDN and or in course, in a Crosse of the Project and or in leaders and garanters, or the Project, by researc of, relating to, mining from or in consent through the Effective Des. III. Intermedication III. Intermedica	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of:	TITLE: (Title) Noney Public: No Commission Engines:	Steas of County of	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
a CDN and or in course, in a Crosse of the Project and or in leaders and garanters, or the Project, by researc of, relating to, mining from or in consent through the Effective Des. III. Intermedication III. Intermedica	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of:	New Commission Expires	Release of Liens & CLADAS Pay 072022 Page 4 of 5	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
active and a contract of the c	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of County of	New Commission Expires	RELEASE OF LIENS & CLAIMS Rev 072022 Page 4 of 3 Lower tier partial	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this DATE	day of
art DN and or in courses, and Crome of the Project and or in leaders and guarantee, or the Project, by reason of railing in, mining from or in consent through the Effective Date. III. Laterantification III. Laterantification III. An advantage are to indicate the project of the Project and in the Counce of the Project and in basics and guarantee. The mining with the Project and the Project of the Project and the Counce of the Project o	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of County of	New Commission Expires No Commission Expires 2 Page 3 of 5 Contrax	RELEASE OF LIENS & CLADAS, Rev. 072022 Page 4 of 3 Lower tier partial affidavit and	with respect to the project colsequent the execution keeped. NO WITNESS WESTERSOF, this Affiliant, Writing of Line, and Radons has been executed this	day of
action and recovering the Characteristics and the Characteristics and particular and	a red 9 1 10 1 10 1 10 1 10 1 10 1 10 1 10 1	State of County of	Page 3 of 5 Subcontractor final	RELEASE OF LIENS & CLADAS, Rev. 072022 Page 4 of 5 Lower tier partial affidavit and partial	with report to the proper subsequent the execution hereof. N WINDESS WHENEXOF, does Affilient. Writer of Lies, and Salessa has been executed this	day of
art DN and or in courses, and Crome of the Project and or in leaders and guarantee, or the Project, by reason of railing in, mining from or in consent through the Effective Date. III. Laterantification III. Laterantification III. An advantage are to indicate the project of the Project and in the Counce of the Project and in basics and guarantee. The mining with the Project and the Project of the Project and the Counce of the Project o	9 10 10 10 10 10 10 10 10 10 10 10 10 10	State of County of	New Commission Expires No Commission Expires 2 Page 3 of 5 Contrax	RELEASE OF LIENS & CLADAS, Rev. 072022 Page 4 of 3 Lower tier partial affidavit and	with report to the proper subsequent to the execution hereof. NEXTENDED WESTEROF, does Affilient, Writer of Lies, and Salessa has been executed this	day of

PROCUREMENT – SUBCONTRACT EXHIBIT V

V: Building Information Modeling

Applies only to trades with a BIM requirement



O'Hare International Airport Terminal 3 Improvements

EXHIBIT V (12/12/2023)

Definitions: (Definitions included below are specific for this Exhibit)

- "2D" means two dimensional.
- "3D" means three dimensional.
- "BIM Detailer" means person(s) responsible for the detailing of each Subcontractor's BIM content.
- "Construction Team" means Clark-W.E. O'Neil JV and all of its subcontractors and suppliers
 of any tier.
- "Contract Drawing" means a two-dimensional document derived from the three-dimensional model produced by a designer.
- "Coordinated Model" means a Federated Building Information Model (BIM) which has been coordinated with the Construction Team and Design Team to eliminate virtual clashes and installation constraints and is sufficient to create Contract Drawings/Shop Drawings for installation of the Work.
- 7. "Coordination Model Schedule" means the schedule that dictates the time by which different areas, trades, and/or floors are to be coordinated, signed off, and submitted necessary to achieve the ultimate project schedule with input from the Construction Team and approved by Clark-WE. O'Neil JV.
- 8. "Data Hosting Site" means the web site(s) used to transfer, store, and share electronic data.
- "Deliverables" means 2D drawings in PDF and DWG format, 3D models in native authoring format, models in NWC/NWD format (to be coordinated in Revisto), Shop Drawings, or authorities.
- "Design Team" means the Architect and all of its consultants at any tier.
- 11. "Electronic Information" means 2D and 3D digital data.
- 12. "Lead Coordinator" means the responsible party for creating a Coordinated Model for their coordination scope, performing clash detection, analyzing clashes and coordinating solutions, grouping and logging clashes, importing and assigning clashes in the tracking system designated by Clark-W.E. O'Neil JV. The Lead Coordinator will prioritize clashes according to priority system and assign issues to the responsible party during coordination meetings using the designated issue tracker. Clark-W.E. O'Neil JV will be the final authority on model issues.
- 13. "Model" means a digital representation of the physical and functional characteristics of the project and is referred to in this Exhibit as the "Model(s)", which may be used to describe a Model Element, a single Model, or multiple Models used in aggregate.
- 14. "Model Element" means a portion of a Model representing a component, system, or assembly within a building or building site.
- "Shop Drawing" means a two-dimensional document derived from the three-dimensional model produced by a Subcontractor.


Page: 1 of 15

Contrax/XXXXXXX

PROCUREMENT – SUBCONTRACT EXHIBIT W, W-1

W: Certification of Compliance with Wage Laws

W-1: Authorized Individual for Signing Certification of Compliance with Wage Laws

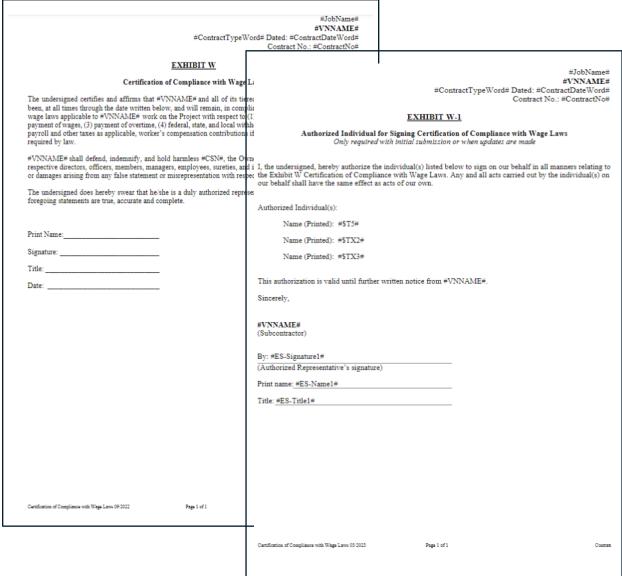

PROCUREMENT – SUBCONTRACT ATTACHMENT, PRELIMARY PROJECT SCHEDULE- DRAFT





O'HARE INTERNATIONAL AIRPORT – TERMINAL 3 IMPROVEMENTS CHICAGO, IL

ATTACHMENT (12/22/2023)

PRELIMINARY PROJECT SCHEDULE - DRAFT

This attachment contains a preliminary project schedule titled "O'Hare T3I Preliminary Schedule DD 12.21.23" (77 pages).

Subcontractor acknowledges that the preliminary project construction schedule may require further development, including, but not limited to logic revisions, resequencing, resource-stacking, etc., as the work progresses; and has included all provisions necessary to maintain the Project Schedule.

The dates in the following schedule are Early Start and Finish Dates.

Contrax/23073B1 Page: 1 of 77

te Printed: 22-Dec-2		Layout	t: T3I - (1) Detailed Sch	edule			Data Date: 21-Dec
y ID	Activity Name	Original Duration	Remaining Early Start Duration	Early Finish	Total Float	2024 2025 ND J F M A M J J A S O ND J F M A M J J A S	2026 2027 SIONID JEMAM I JAS GND JEMAM
3 Improvements	s - Preliminary Schedule - Data Date: 12/21/2023	946	841 21-Dec-23	13-Apr-27	0	MODITIMA MODIFICACION DI LA 1919A	
MILESTONES		946	753 21-Dec-23	13-Apr-27	0		
PROJECT MILESTO	DNES	1360	1082 21-Dec-23	13-Apr-27	0		
MILE-130	PRE-CON NTP (7/24/2023)	0	0 21-Dec-23	10-140-21	E	CON NTP (7/24/2023)	
MILE-010	CONSTRUCTION NTP (ANTICIPATED 4/26/2024)	0	0	26-Apr-24	2	◆ CONSTRUCTION NTP (ANTICIPAT	TED 4/26/2024)
MILE-110	SUBSTANTIAL COMPLETION	0	0	10-Feb-27	0		◆ SUBS
MILE-120	FINAL COMPLETION	0	0	13-Apr-27	0		♦ F
LD MILESTONES	THALOUNI ELTOT	492	492 04-Mar-25	10-Feb-27	0		
LD-1000	LD - AA CLUB SHELL READY FOR TENANT FIT OUT BY OTHERS	0	0	04-Mar-25	492	♦ LD -AA CLU	IB SHELL READY FOR TENANT FIT OUT BY O
LD-1010	LD - GATE K1 INCLUDING PARTIAL HOLD-ROOM FIT OUT	0	0	22-Aug-25	371		LD - GATE K1 INCLUDING PARTIAL HOLD-RO
LD-1010	LD - GATE L2A INCLUDDING PARTIAL HOLD ROOM FIT OUT	0	0	22-Aug-25	371		LD - GATE L'2A INCLUDDING PARTIAL HOLD
LD-1030	LD - CONCESSION SHELL READY FOR TENANT FIT OUT	0	0	17-Sep-25	354		◆ LD - CONCESSION SHELL READY FOR TE
LD-1030 LD-1040	LD - SUBSTANTIAL COMPLETION	0	0	17-Sep-25 10-Feb-27	0		◆LD-S
NTERIM MILESTON		1150	1022 21-Dec-23	10-Feb-27	62		V
	DESIGN COMPLETE				62	DESIGN COMPLETE	
MILE-150		0	0	21-Dec-23		PERMITTING COMPLETE	
MILE-140	PERMITTING COMPLETE	0	0	24-Apr-24	1084	PURCHASING COMPLETE	
MILE-160	PURCHASING COMPLETE	0	0	24-May-24	1054		S LEAD MATERIAL PROCUREMENT COMPLE
MILE-170	LONG LEAD MATERIAL PROCUREMENT COMPLETE	0	0	02-Jun-25	680	♦ LONG	
MILE-230	CONSTRUCTION - MECHANICAL COMPLETE	0	0	13-Nov-25	516		◆ CONSTRUCTION - MECHANICAL CON
MILE-180	CONSTRUCTION - CORE & SHELL COMPLETE	0	0	07-May-26	341		
MILE-190	CONSTRUCTION - STRUCTURAL/ENCLOSURE INFILL/OPENING COMPLETE	0	0	19-Oct-26	176		
MILE-210	CONSTRUCTION - RESTROOMALTERATIONS COMPLETE	0	0	01-Feb-27	71		◆ CONS
MILE-220	CONSTRUCTION - BAGGAGE HANDLING SYSTEM COMPLETE	0	0	03-Feb-27	69		◆ CONS
MILE-200	CONSTRUCTION - INTERIOR ALTERATIONS COMPLETE	0	0	10-Feb-27	62		◆ CONS
AAMILESTONES		451	451 29-Apr-24	06-Feb-26	300		
AA FLAG SHIP CHE	ECK-IN	189	189 13-May-24	10-Feb-25	552		
AA-1000	AA FLAGSHIP CHECK-IN SUMMARY (CALENDAR DAYS)	267	267 13-May-24	03-Feb-25	730		CHECK-IN SUMMARY (CALENDAR DAYS)
AA-1030	AA FLAGSHIP CHECK-IN START	0	0 13-May-24		683		
AA-1040	AA FLAGSHIP CHECK-IN COMPLETE	0	0	03-Feb-25	469	◆ AA FLAGSHIP	CHECK-IN COMPLETE
CDA-1000	UL - AA FLAGSHIP - FF&E MOVE IN PERIOD	5	5 04-Feb-25	10-Feb-25	469	■ UL-AAFLAG	SHIP - FF&E MOVE IN PERIOD
AAPPS		120	120 29-Apr-24	16-Oct-24	631		
AA-1010	AA PPS SUMMARY (CALENDAR DAYS)	171	171 29-Apr-24	16-Oct-24	7	AA PPS SUMMARY (C	ALENDAR DAYS)
AA-1050	AA PPS START	0	0 29-Apr-24		693	♦ AA PPS START	
AA-1060	AAPPS COMPLETE	0	0	16-Oct-24	573		
AACLUB TI		236	236 05-Mar-25	06-Feb-26	0		
CDA-1010	UL - AA CLUB TI START	0	0 05-Mar-25		69	♦ UL-AACLŲ	BTISTART
AA-1020	UL - AA CLUB TI SUMMARY (CALENDAR DAYS)	339	339 05-Mar-25	06-Feb-26	0		UL - AA CLUB TI SUMMARY (CAL
CDA-1050	UL - AA CLUB TI COMPLETE	0	0	06-Feb-26	0		♦ UL-AACLUB TI COMPLETE
GATE CLOSURES		320	320 21-May-24	25-Aug-25	415		
GATE K1 CLOSUR		320	320 21-May-24	22-Aug-25	415		
GATE-K1-1000	GATE K1 CLOSURE WINDOW (CALENDAR DAYS)	459	459 21-May-24	22-Aug-25	537		GATE K1 CLOSURE WINDOW (CALENDAR)
	UL - GATEK1 CLOSURE START	0	0 21-May-24		677		



T3I-231221-ForMarket | T3 Improvements - Preliminary Schedule - Data Date: 12/21/2023
Terminal 3 Improvements at O'Hare International Airport
City of Chicago: Chicago Department of Aviation





PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)


Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT – BID DOCUMENTS, Part Three of Three

Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Available on BuildingConnected:

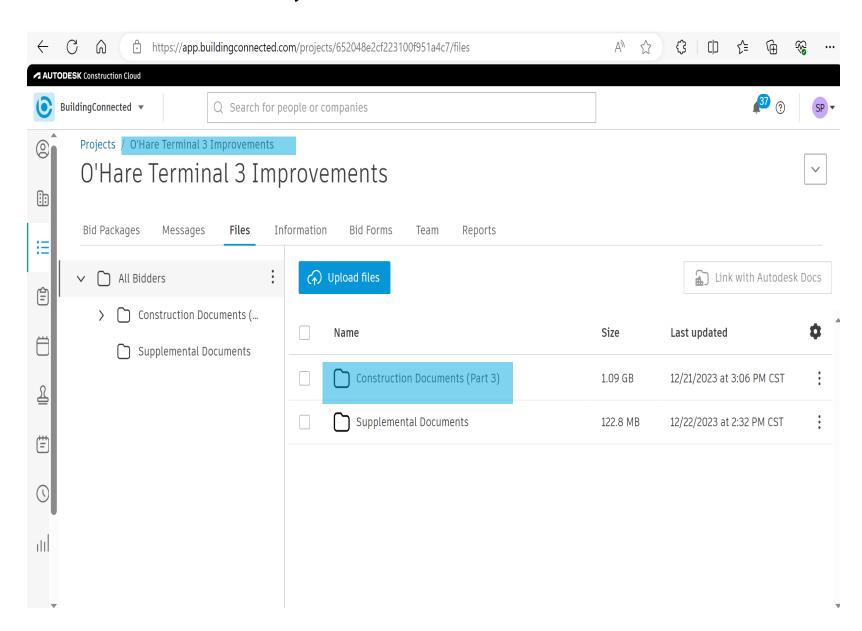

PROCUREMENT - BID DOCUMENTS

BID DOCUMENTS

Part One of Three – Instructions and Execution Documents

Part Two A of Three – CDA General Conditions

Part Two B of Three – Subcontract Agreement (sample)


Part Three of Three – Technical Specifications, CDA Construction Safety Manual, Drawings

Supplemental Documents

PROCUREMENT – BID DOCUMENTS, Supplemental Documents


Available on BuildingConnected:

- CDA Construction Barricade Style Guide_May 2023
- CDA Construction Safety Manual FINAL 110922
- CDA Digital Governance Sept 2022
- CDA Smartsheet Standard Operating Procedure
- CDA Sustainable Airport Manual v4.0
- CDA-RFI Response Log 2023.12.22
- COT3 Temporary Partitions and Enclosures Plan Rev1 – 202312120
- Exhibit 1- Mandatory Federal Terms and Conditions 20231020
- Exhibit 2 Tax Delinquency and Felony Convictions 20231020
- Master Agreement Exhibit E Bond Forms
- O'Hare T3I Preliminary Schedule DD 12.21.23 2
- ORD T3_Geotechnical Report
- Terminal 3 Public Owner Contract
- Terminal 3 Improvements and Supplemental Baggage BIM Execution Plan 3-24-23
- TSA checkpoint-requirements-and-planningguide_appendix-a
- TSA checkpoint-requirements-and-planningguide appendix-b
- TSA checkpoint-requirements-and-planningguide appendix-c

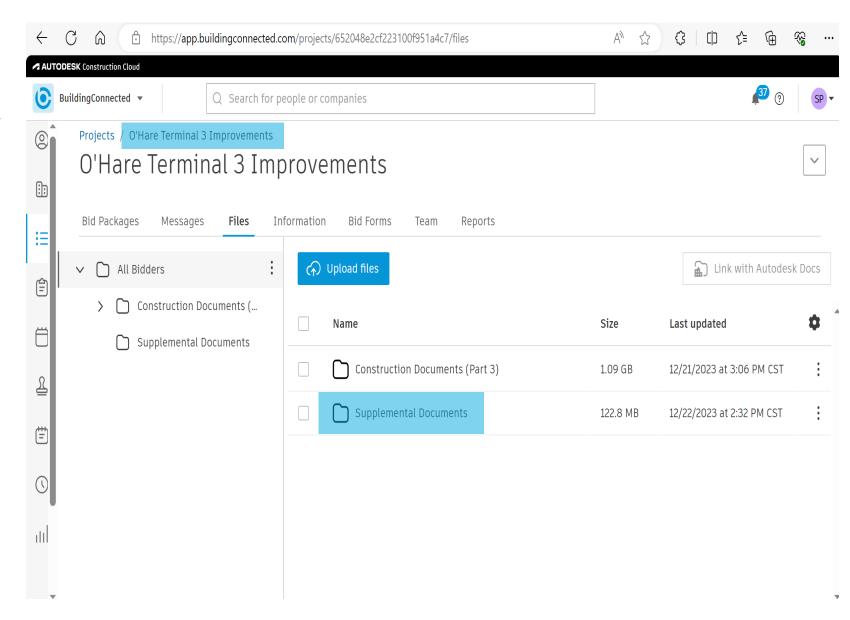


To begin, find the project in your Bid Board.

• From the "Accepted" tab on your Bid Board, click "Send or Log" on the right-hand side of the bid.

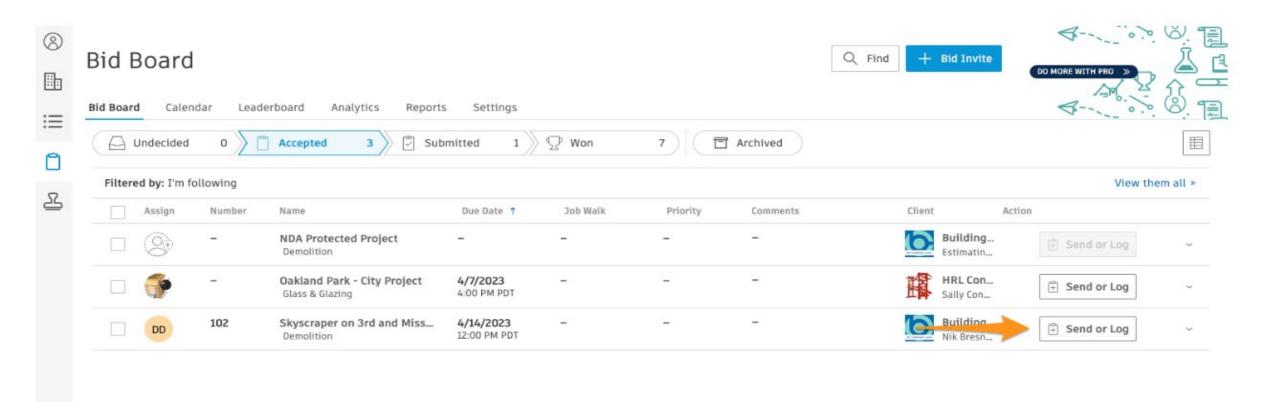

If you are already inside the project, click on the "Bid Form" tab or click "Bid Form" next to "Opportunity Summary"

Note: "Bid Form" appears next to the Opportunity Summary after you have indicated you are bidding. Select "Bidding" first see the "Bid Form" button.

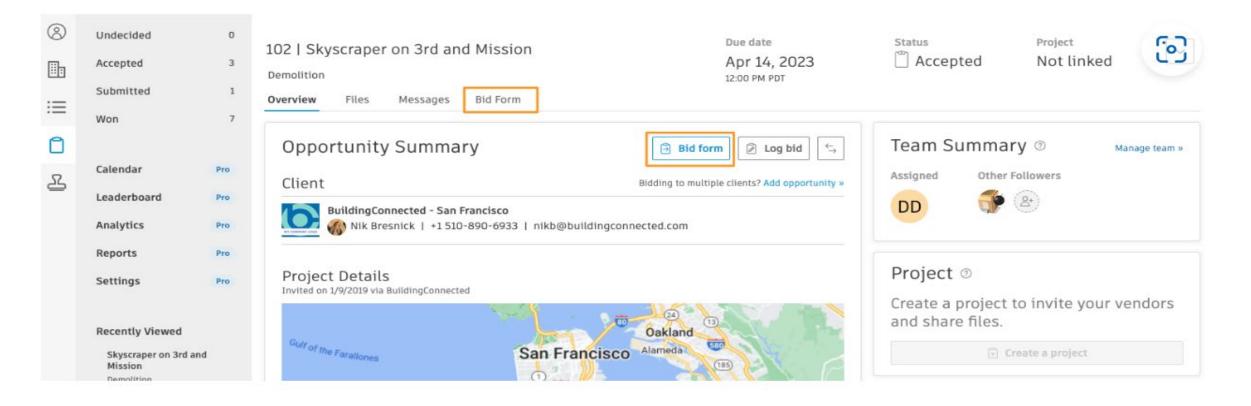


Enter all of the information requested in the form.


To attach the required documents, click "Attach your proposal" and select files from your computer. The files will immediately start uploading until they reach 100%. Upload more by clicking "Attach more".

Click "Print" to download or print a PDF copy of the bid form. The proposal will open in a new tab where there are options to download and print.


Once the bid form is complete, click "Preview & send".

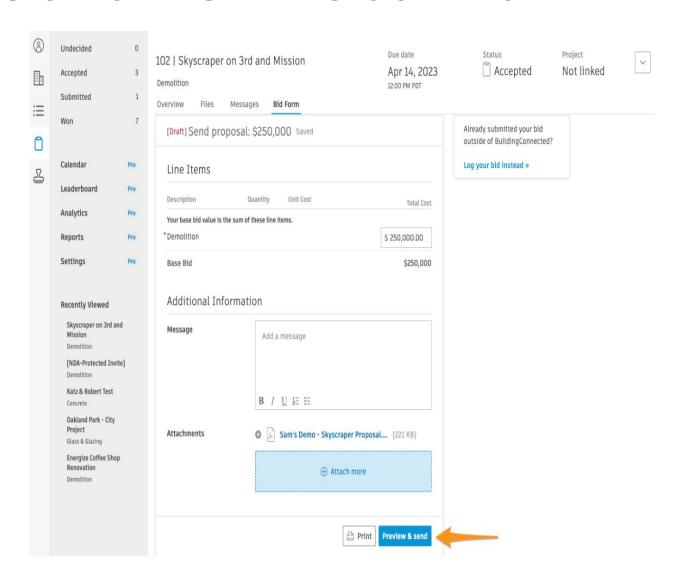


Please note that if you do not fill in all of the required questions, you will see any required items highlighted with a red flag. Fill them in accordingly and click "Preview & send" again.




Confirm all information on the bid form is correct and then click "Submit." Once you click "Submit," Clark-W.E. O'Neil JV will receive your proposal as well as an email notification.

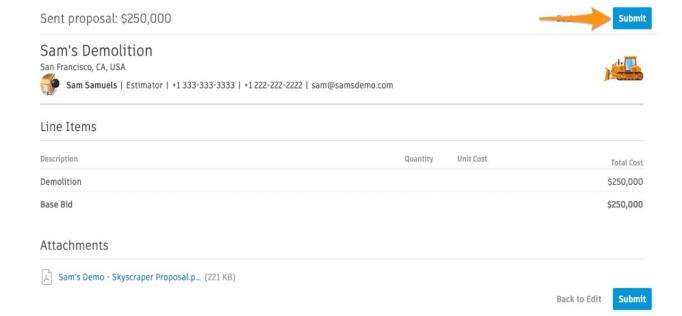


You will receive a confirmation.



You can ensure your bid was submitted successfully by checking that the "Status" has changed to "Submitted" and the bid form now says "Sent proposal" with the date and time the proposal was sent.

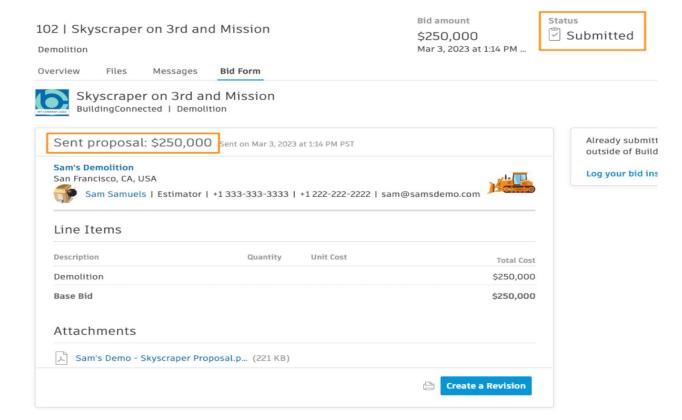

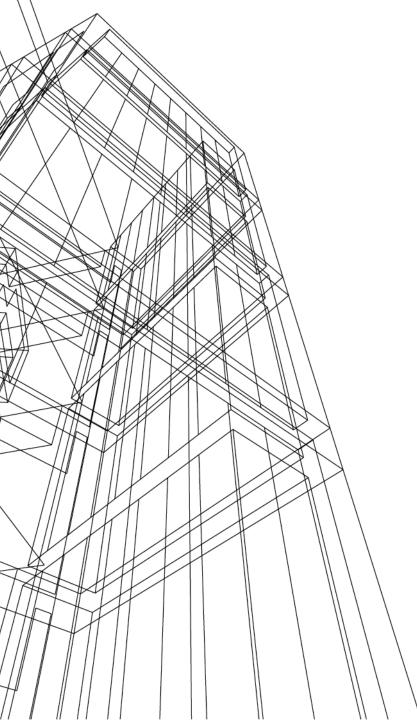


PROCUREMENT - BID OPENING

Submit Bids on BuildingConnected prior to the bid opening date/time

Late bids will not be accepted

Hard copy bids accepted if needed prior to the bid opening date/time

Bid bonds required with your proposal

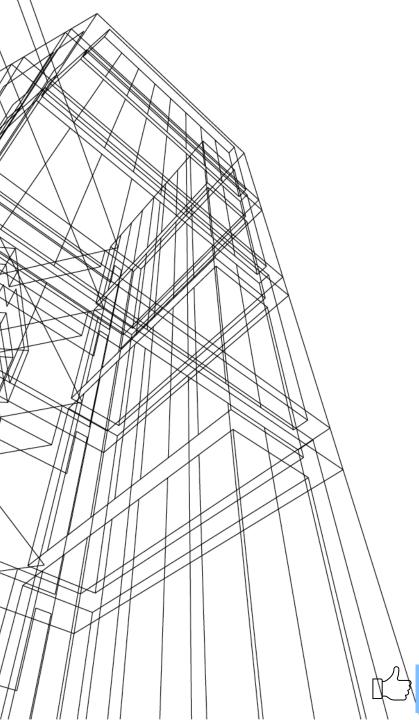

PROCUREMENT – STEPS AFTER THE BID OPENING

Lowest responsive and responsible bidder to be brought in for post-bid meeting. BID THE SCOPE OF WORK, WITHOUT EXCLUSIONS/CLARIFICATIONS AND MEET OR EXCEED COMPLIANCE REQUIREMENTS.

If required, second or third responsive and responsible bidder to be brought in for a post-bid meeting

Upon completion of post-bid meeting, request for approval sent to CCA/CDA

Subcontract agreements issued upon approval by CDA. For long lead items, subcontractors may receive a Letter of Intent to commence with shop drawing preparations and potentially material/equipment procurement.

OFFERING MORE DBE PARTICIPATION WITH YOUR BID THAN THE STATED AMOUNT IS ENCOURAGED AND PART OF THE OVERALL BID EVALUATION

CONCLUSION – NEXT STEPS

- Meet the Primes
- Site Walk Through
- RFI'S are due no later than the Question Cut-Off Date / Time posted on <u>www.cot3.com</u> and <u>www.ord21.com</u>
- Review and acknowledge all Clarifications & Addenda
- Submit Bid(s) through Building Connected no later than the Bid Opening Date / Time posted on www.cot3.com
 and www.ord21.com

Bid Package Schedule_v1 : Sheet1 W·E·O'NEIL **TERMINAL 3 IMPROVEMENTS BID PACKAGE / TRADE PACKAGE SCHEDULE** Updated: 1/5/2024 Note: Below dates / times are subject to change at COT3's discretion. Updates will be posted on COT3's website and notices distributed via BuildingConned Notice of Bid Trade Invitation to Bid Pre-Bid Conference Question Cut-Off Bid Package Bid Opening Date / Bid Pkg Pacakg Trade Package Description Opportunity Description Date Date / Time Date / Time Time Date 01/16/2024 01/23/24 10:00 AM 01/30/24 5:00pm 02/16/2024 2:00pm 2.19 **Ornamental Metals** 10/26/2023 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm Civil/Sitework - Paving, Excavation, Site Demo, 10/26/2023 2.7 **Excavation Support & Shoring Systems** 10/26/2023 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm New Roofing Systems & Roof Patching 10/26/2023 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm 2.11 Ceilings 10/26/2023 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm 2.13 Terrazzo 10/26/2023 2.15 Painting & Intumescent Fireproofing 10/26/2023 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm Remaining 2 Trades 01/23/2024 01/30/24 10:00 AM 02/06/24 5:00pm 02/23/2024 2:00pm 2.16 Metal Wall Panels 10/26/2023 01/31/2024 02/07/24 10:00 AM 02/14/24 5:00pm 03/01/2024 2:00pm 2.14 Doors, Frames and Hardware 10/26/2023 01/31/2024 2.17 Interior Glass 10/26/2023 02/07/24 10:00 AM 02/14/24 5:00pm 03/01/2024 2:00pm 01/31/2024 02/07/24 10:00 AM 02/14/24 5:00pm 03/01/2024 2:00pm 2.20 TSA Systems Integrator 10/26/2023 2.22 Pedestrian Security Equipment - Breach control 10/26/2023 01/31/2024 02/07/24 10:00 AM 02/14/24 5:00pm 03/01/2024 2:00pm 02/07/24 10:00 AM 03/01/2024 2:00pm 2.24 Overhead doors 10/26/2023 01/31/2024 02/14/24 5:00pm 01/31/2024 02/07/24 10:00 AM 02/14/24 5:00pm 03/01/2024 2:00pm 2.25 Signage 10/26/2023

CONCLUSION – QUESTIONS

Key takeaways:

- Return all documents needed with bid (reference the checklist)
- Be on the lookout for Addendums
- Complete the bid form in its entirety
- Any exclusions, clarifications, or qualifications in your proposal or bid may result in rejection
- Account for all Logisitics, DBE and Workforce requirements

SUBMIT ALL QUESTIONS

TO: ProjectCOT3.inquiries@clarkconstruction.com

NOTICE: NOTHING DISCUSSED TODAY IS INTENDED TO ALTER THE BID DOCUMENTS. ALL CLARIFICATIONS MUST BE SUBMITTED THROUGH THE REQUEST FOR INFORMATION (RFI) PROCESS FOR PROPER REVIEW AND RESPONSE.

IN CASE OF CONFLICTS BETWEEN TODAY'S DISCUSSIONS AND THE BID INFORMATION, BIDDERS SHOULD SUBMIT A PRE-BID RFI FOR CLARIFICATION AND GUIDANCE

Site Tour

TERMINAL 3

LOWER LEVEL

NEAR BAGGAGE CLAIMS CAROUSEL 6

BRING YOUR DRIVERS LICENSE IF YOU ARE NOT BADGED

Meet the Primes/ Potential Bidders

Civil/Sitework - Paving, Excavation, Site Demo	Excavation Support & Shoring Systems	Roofing	Ceilings	Terrazzo	Painting & Intumesce nt Fireproofin g	Metal Wall Panels	Building 464 Demo
Berger Excavation Contractors, Inc.	Keller North America, Inc.	A-1 Roofing All American	Alliance Companies Anning-Johnson	Amici Terrazzo CCI Flooring	All-Tech Decorating	All American Exterior Solutions	Break Thru Enterprises
John Keno & Company, Inc.	Michel's Construction, Inc.	Exterior Solutions Bennet &	E&K	John Caretti &	Celtic Commercial Painting	American Igloo Builders	Brandenburg US
K-Five Construction Corp.	Stalworth Underground, LLC	Brosseau Roofing	Escarpita	Menconi	Continental Painting &	Crown Corr	Dismantlement
Lima Excavating	Thatcher	Kedmont Waterproofing	Ibuilders Corp	Terrazzo	Decorating	Hill Mechanical	Slate
Lindahl Brothers, Inc.	Foundations, Inc.	Knickerbocker	Just Rite Acoustics		Ibuilders Corp.	Metalmaster- Roofmaster	Alpine
Norman		Roofing	Maman Corp		K&E Painting & Decorating	Mid-States Glass	Heneghan
Mechanical, Inc. Plote Construction		M Cannon Roofing	Performance Contracting		MJB Decorating	and Metal	American Demolition
Quality Excavation		Metalmaster Roofmaster	The Levy Company		MS. Sebastian Painting	MillerClapperton Riddiford Roofing	Milburn Demolition
Reyes Group Ltd.		Riddiford Roofing	Thorne Associates		The Matan Group	J	National Wrecking
Rossi Contractors Inc.			TORO Construction		Uptown Painting & Decorating		
